

	APPENDIX A CONSTRUCTION PROGRAMME AND PROACTIVE ENVIRONMENTAL PROTECTION PROFORMA	

Construction Programme (Oct 2024 – Dec 2025)


Revision : Revision 15 (June 2025)

Legend:

- Baseline Milestone: Diamond symbol
- Baseline Summary: Horizontal line with diamond at end
- Task: Blue horizontal bar
- Critical Task: Red horizontal bar
- Milestone: Diamond symbol
- Summary: Horizontal line with diamond at end
- Inactive Milestone: Light blue horizontal bar
- Inactive Summary: Light blue horizontal line with diamond at end
- Manual Task: Diamond symbol
- Manual Summary Rollup: Horizontal line with diamond at end
- Manual Summary: Dotted horizontal line
- Start-only: Green vertical bar
- Finish-only: Green vertical bar
- External Task: Green horizontal bar
- External Milestone: Green vertical bar
- Path Driving Predecessor Milestone Task: Diamond symbol
- Path Driving Predecessor Summary Task: Horizontal line with diamond at end
- Path Driving Predecessor Normal Task: Diamond symbol
- Baseline: Grey horizontal bar

Design & Construction of Kong Nga Po Police Training Facilities Programme

Revision : Revision 15 (June 2025)

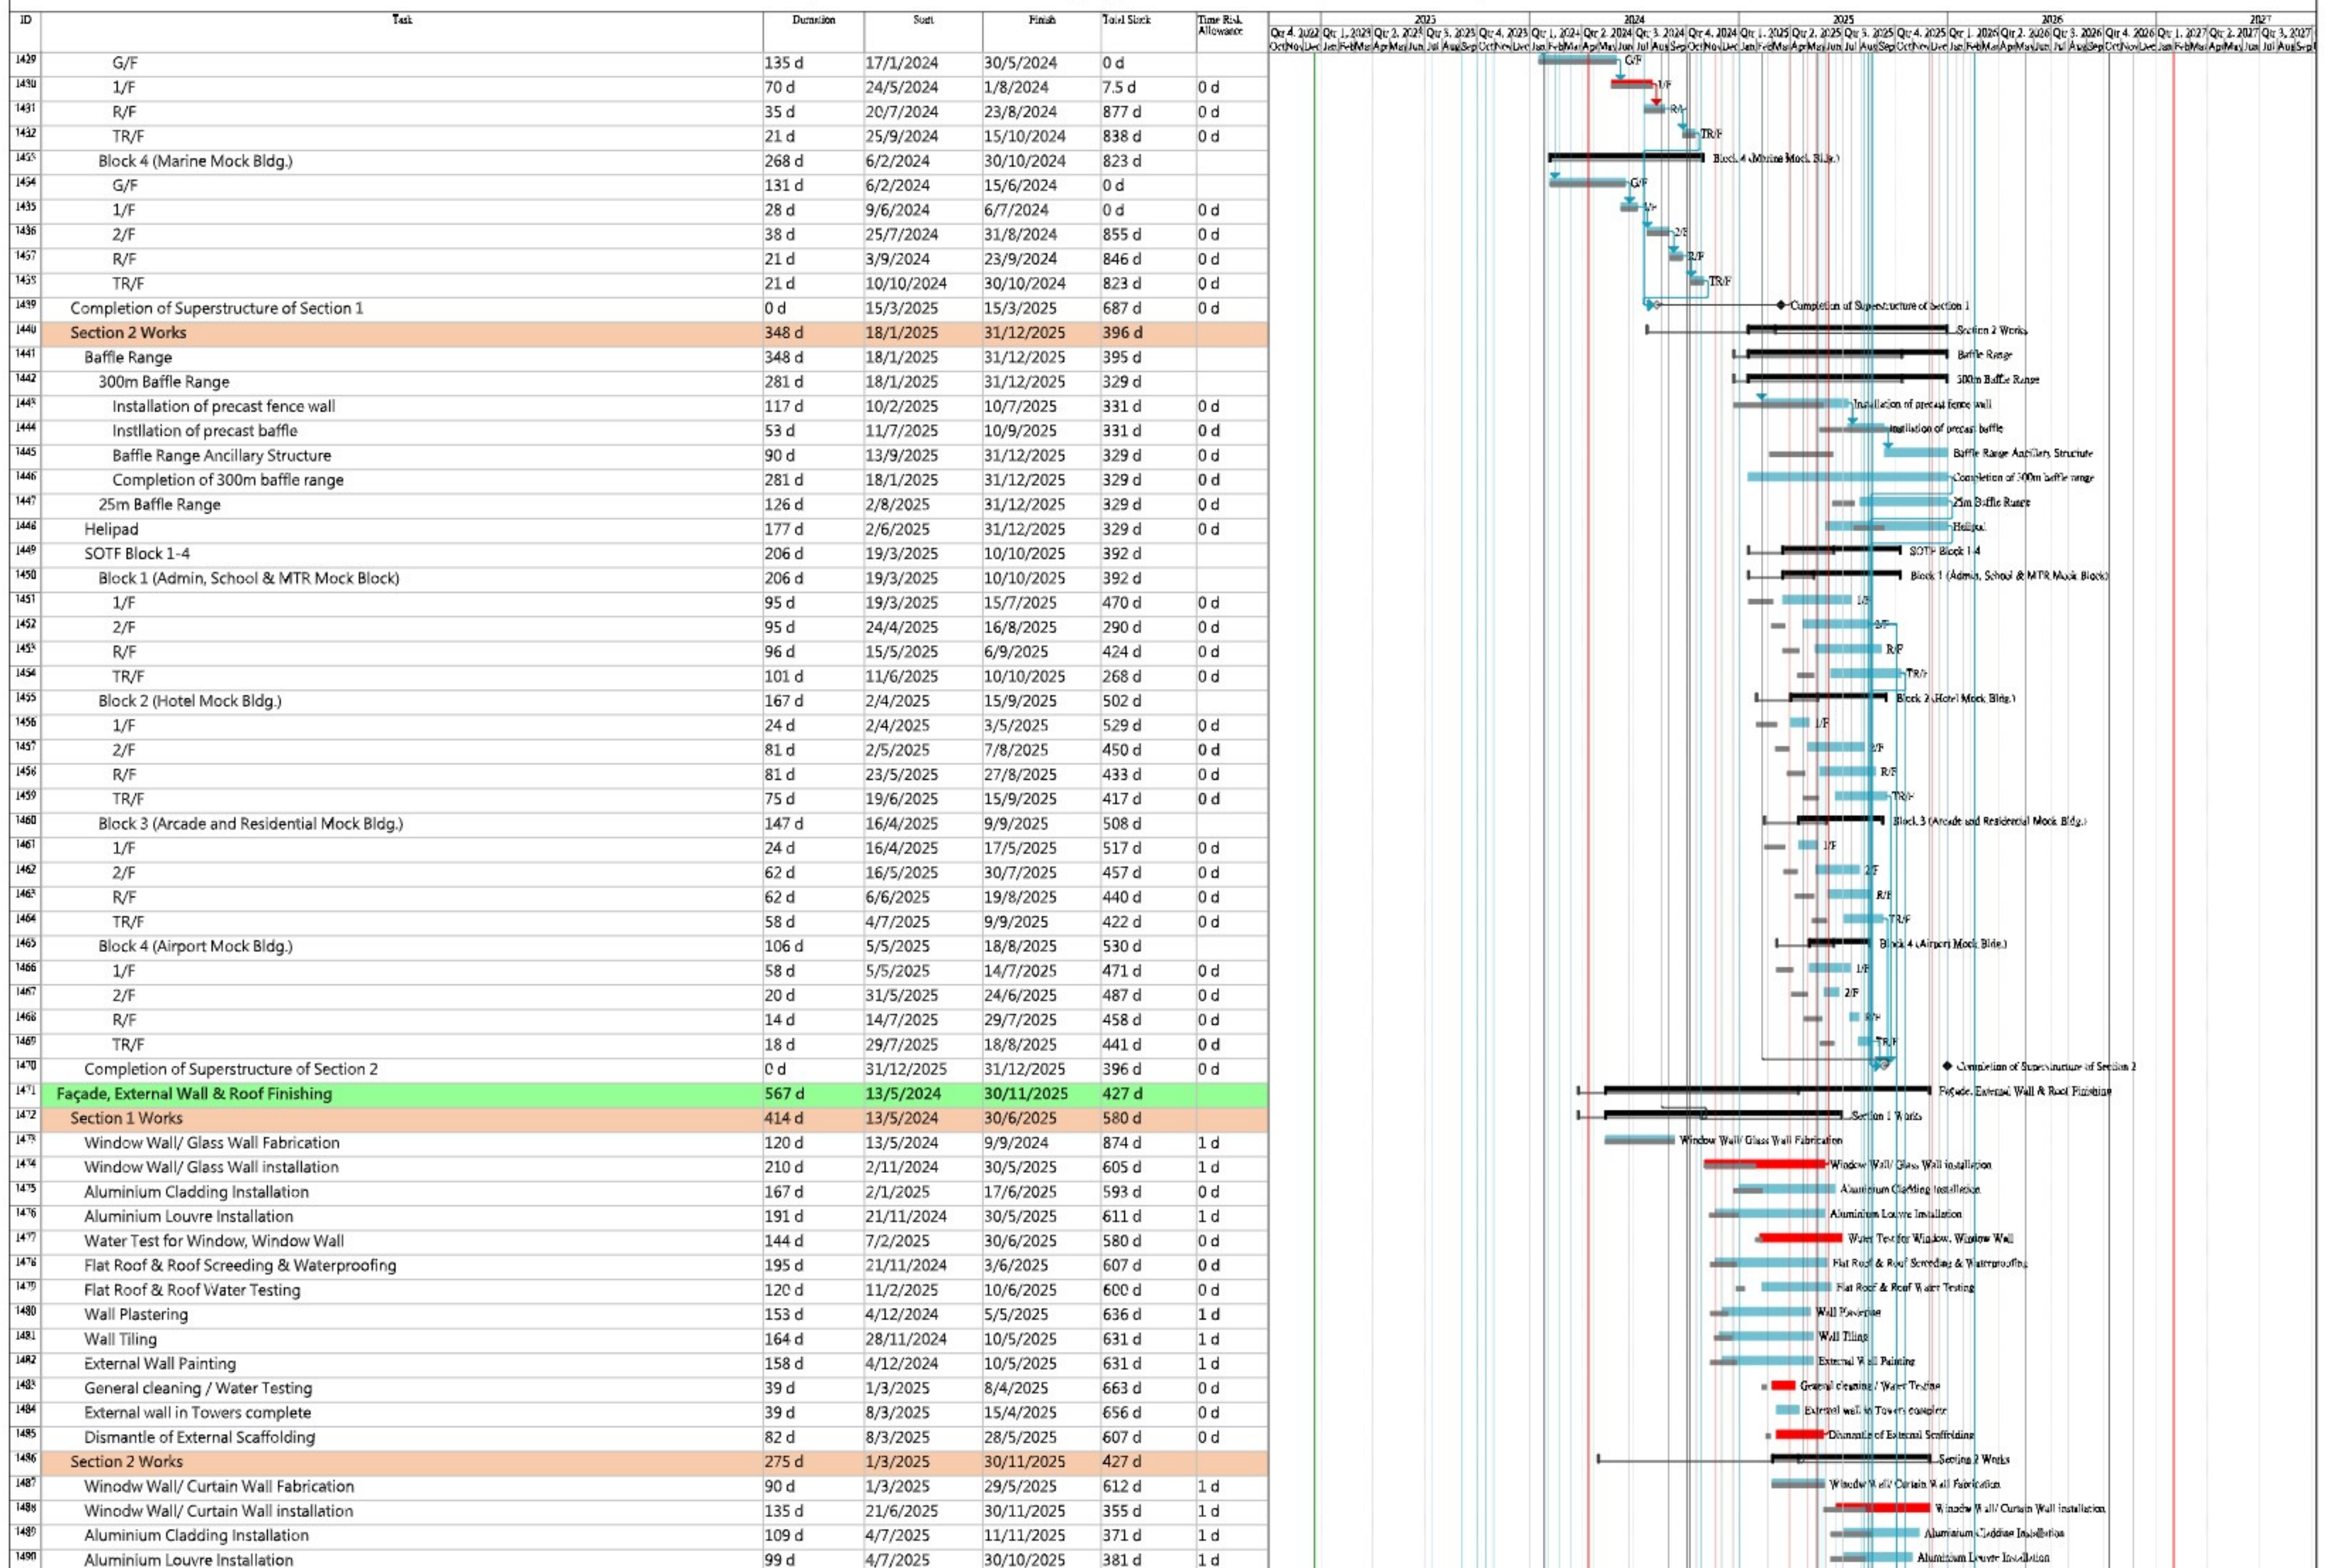

Revision : Revision 15 (June 2025)

中國建築聯營
CHINA STATE JOINT VENTURE

Symbol	Meaning
◇	Milestone
◆	Manual Task
Start-only	Start-only
Path Driving Predecessor Milestone Task	Path Driving Predecessor Milestone Task
Baseline Milestone	Baseline Milestone
Summary	Summary
Duration-only	Duration-only
Finish-only	Finish-only
Path Driving Predecessor Summary Task	Path Driving Predecessor Summary Task
Task	Task
Inactive Milestone	Inactive Milestone
Manual Summary Rollup	Manual Summary Rollup
External Task	External Task
Path Driving Predecessor Manual Task	Path Driving Predecessor Manual Task
Critical Task	Critical Task
Inactive Summary	Inactive Summary
Manual Summary	Manual Summary
External Milestone	External Milestone
Baseline	Baseline

Design & Construction of Kong Nga Po Police Training Facilities Programme

Revision : Revision 15 (June 2025)

ID	Task	Duration	Start	Finish	Total Slack	Time Risk Allowance	2023	2024	2025	2026	2027															
							Qtr 4, 2022 Oct/Nov/Dec	Qtr 1, 2023 Jan/Feb/Mar	Qtr 2, 2023 Apr/May/June	Qtr 3, 2023 Jul/Aug/Sep	Qtr 4, 2023 Oct/Nov/Dec	Qtr 1, 2024 Jan/Feb/Mar	Qtr 2, 2024 Apr/May/June	Qtr 3, 2024 Jul/Aug/Sep	Qtr 4, 2024 Oct/Nov/Dec	Qtr 1, 2025 Jan/Feb/Mar	Qtr 2, 2025 Apr/May/June	Qtr 3, 2025 Jul/Aug/Sep	Qtr 4, 2025 Oct/Nov/Dec	Qtr 1, 2026 Jan/Feb/Mar	Qtr 2, 2026 Apr/May/June	Qtr 3, 2026 Jul/Aug/Sep	Qtr 4, 2026 Oct/Nov/Dec	Qtr 1, 2027 Jan/Feb/Mar	Qtr 2, 2027 Apr/May/June	Qtr 3, 2027 Jul/Aug/Sep
1553	Section 2 Works	158 d	27/7/2025	31/12/2025	0 d																					
1554	Internal Partitions, Doors & Associated Fixtures - Dry Trades	88 d	27/7/2025	22/10/2025	396 d																					
1555	Steel& Metal Works	151 d	27/7/2025	24/12/2025	396 d	1 d																				
1556	Internal Dry Partitioning Works	131 d	10/8/2025	18/12/2025	396 d	1 d																				
1557	Doors& Ironmongeries	121 d	24/8/2025	22/12/2025	396 d	1 d																				
1558	Internal Ceiling & Associated Fixtures - Dry Trades	123 d	31/8/2025	31/12/2025	396 d																					
1559	Suspended Ceiling Installation	123 d	31/8/2025	31/12/2025	396 d	1 d																				
1560	Internal Fitting-out to Special Areas	116 d	7/9/2025	31/12/2025	396 d	1 d																				
1561	Internal Fixtures& Furniture & Signage	109 d	14/9/2025	31/12/2025	396 d	1 d																				
1562	External Works	1090 d	22/7/2023	15/7/2026	200 d																					
1563	Section 1 Works	740 d	22/7/2023	30/7/2025	550 d																					
1564	Training Ground	545 d	22/7/2023	16/1/2025	745 d																					
1565	2-WD Training Ground (Block 3)	309.5 d	22/7/2023	26/5/2024	980.5 d																					
1566	Excavation for Underground Service and Utilities Works	30 d	22/7/2023	20/8/2023	0 d																					
1567	NICE001 - 14 days EOT Claimed	14 d	21/8/2023	3/9/2023	0 d																					
1568	NICE002 - 4 days EOT Claimed	4 d	4/9/2023	7/9/2023	0 d																					
1569	NICE003 - 10 days EOT Claimed	10 d	8/9/2023	17/9/2023	0 d																					
1570	NICE004 - 3.5 days EOT Claimed	3.5 d	18/9/2023	21/9/2023	0 d																					
1571	NICE005 - 20 days EOT Claimed	20 d	21/9/2023	11/10/2023	0 d																					
1572	NICE006 - 5.5 days EOT Claimed	5.5 d	11/10/2023	16/10/2023	0 d																					
1573	U/G Drainage Installation	45 d	26/10/2023	10/12/2023	0 d																					
1574	U/G Drainage Installation	45 d	26/10/2023	10/12/2023	0 d																					
1575	Concrete Surround Works	14 d	10/12/2023	24/12/2023	0 d																					
1576	Earthing Installation Works	35 d	22/10/2023	25/11/2023	0 d																					
1577	Backfill	30 d	17/12/2023	16/1/2024	0 d																					
1578	U/G Cable Pits / Ducts for BS / SFH / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	100 d	16/1/2024	25/4/2024	0 d																					
1579	Complete U/G Services & Utilities Works	0 d	25/4/2024	25/4/2024	0 d																					
1580	Backfilling Works	45 d	25/2/2024	10/4/2024	0 d																					
1581	Driving Ground Concreting Works	30 d	10/4/2024	10/5/2024	980.5 d																					
1582	Finishing Works and Road Painting	16 d	10/5/2024	26/5/2024	980.5 d																					
1583	Parking and Training Facilities	301 d	10/1/2024	5/11/2024	817 d																					
1584	Excavation for Underground Service and Utilities Works	40 d	10/1/2024	18/2/2024	0 d																					
1585	U/G Drainage Installation	60 d	25/1/2024	24/3/2024	0 d																					
1586	Concrete Surround Works	14 d	20/3/2024	2/4/2024	0 d																					
1587	Earthing Installation Works	30 d	24/2/2024	24/3/2024	0 d																					
1588	Backfill	30 d	27/3/2024	25/4/2024	0 d																					
1589	U/G Cable Pits / Ducts for BS / SFH / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	60 d	26/4/2024	24/6/2024	0 d																					
1590	Complete U/G Services & Utilities Works	0 d	24/6/2024	24/6/2024	0 d																					
1591	Backfilling Works	45 d	5/6/2024	19/7/2024	0 d																					
1592	Driving Ground Concreting Works	30 d	20/7/2024	18/8/2024	896 d																					
1593	Finishing Works and Road Painting	15 d	22/10/2024	5/11/2024	817 d																					
1594	Braking Training (Block 4)	282 d	17/10/2023	24/7/2024	921 d																					
1595	Excavation for Underground Service and Utilities Works	55 d	17/10/2023	10/12/2023	0 d																					
1596	Excavation for Underground Service and Utilities Works	45 d	17/10/2023	30/11/2023	0 d																					
1597	NICE003 - 10 days EOT Claimed	10 d	1/12/2023	10/12/2023	0 d																					
1598	U/G Drainage Installation	60 d	16/12/2023	13/2/2024	0 d																					
1599	Concrete Surround Works	14 d	9/2/2024	22/2/2024	0 d																					
1600	Earthing Installation Works	40 d	6/12/2023	14/1/2024	0 d																					
1601	Backfill	30 d	16/2/2024	16/3/2024	0 d																					
1602	U/G Cable Pits / Ducts for BS / SFH / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	60 d	17/3/2024	15/5/2024	991 d																					
1603	Complete U/G Services & Utilities Works	0 d	15/5/2024	15/5/2024	991 d																					
1604	Backfilling Works	45 d	26/4/2024	9/6/2024	921 d																					
1605	Driving Ground Concreting Works	30 d	10/6/2024	9/7/2024	921 d																					
1606	Finishing Works and Road Painting	15 d	10/7/2024	24/7/2024	921 d																					
1607	Skid Pan (Block 5)	227 d	1/12/2023	14/7/2024	931 d																					
1608	Excavation for Underground Service and Utilities Works	40 d	1/12/2023	9/1/2024	0 d																					
1609	U/G Drainage Installation	50 d	16/12/2023	3/2/2024	0 d																					
1610	Concrete Surround Works	14 d	30/1/2024	12/2/2024	0 d																					
1611	Earthing Installation Works	35 d	15/1/2024	18/2/2024	0 d																					

Layout Plan with major construction activities

Legend:

Foundation construction and associated works

- Soil Storage

Handed over to user

-Tree planting works

Handed over to user

Handed over to user

- Open cut excavation
- Soil removal/ Soil Storage
- U.U. Lead in and Pipe Duct Connection
- Construction of footings
- Installation of structural steelworks for 300m baffle range

Handed over to user

Handed over to user

- Backfilling
- U.U. Lead in and Pipe Duct Connection
- Construction of footings
- Construction of superstructure

- U.U. Lead in and Pipe Duct Connection
- Construction of superstructure
- E&M installation

- E&M installation

Handed over to user

Handed over to user

Major construction activities carried out in period of October 2025

Legend:

Foundation construction and associated works

- Soil Removal

- Handed over to user

- Tree planting works
- Hand over to user

- Handed over to user

- Handed over to user

- Excavation
- Soil removal
- U.U. Lead in and Pipe Duct Connection
- Construction of fence wall
- Painting
- Installation of structural steelworks for 300m baffle range

- U.U. Lead in and Pipe Duct Connection
- Construction of superstructure
- E&M installation

- Backfilling
- U.U. Lead in and Pipe Duct Connection
- Construction of substructure
- Construction of superstructure

- E&M installation

- Handed over to user

- Handed over to user

Major construction activities carried out in period of Nov 2025 ~ Jan 2026

Proactive Environmental Protection Proforma

Proactive Environmental Protection Proforma

Ref*	Proposed Construction Method	Location/Working Period	Anticipated Major Impacts	Recommended Mitigation Measures
EIA 3.9.1; EM&A Log 2.2	Open cut excavation	Kong Nga Po Site	Dust impact from excavation activities and earth moving	• Use of regular water spraying (once every 1.25 hours or 8 times per day) at all active works area exposed site surfaces and unpaved roads, particularly during dry weather • Deploy water bowser for regular water spraying to enhance dust suppression • Manual water spraying for dusty operation where inaccessible by water bowser • Speed control of site transportation • Stockpile of dusty materials will be covered by tarpaulin sheets to avoid wind-blown dust • Vehicles used for transporting dusty materials/spoils will be covered by mechanical cover before leaving the site • Wheel washing facilities will be provided and cleaning the wheel of all vehicles before leaving the site
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition

				• Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of construction materials to reduce the potential for water pollution • Provide wastewater treatment facilities prior to discharge of wastewater • Regular inspection and maintenance of wastewater treatment facilities • Wastewater pumped out of the excavation areas will be treated to remove suspended solids prior to discharge • Hard paving or well-compact of main haul road to minimize washout of soil • Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged.
EIA 7.5.1.1 &			Waste Generation	• Training of site personnel in proper waste management and

7.5.1.2; EM&A Log 6.2				chemical handling procedures • Proper storage and sorting of excavated inert materials to maximize on site reuse for backfilling • Surplus inert C&D materials will be disposed of at designated Government's PFRF.
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Chemical waste should be stored at chemical waste container and collected by a licensed collector to transport and dispose of at the approved Chemical Waste Treatment Centre • Drip tray and chemical spillage kit will be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to frontline workers for the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Restrict construction area to minimize the impact on existing retained trees
EIA 3.9.1; EM&A Log 2.2	Soil Removal	Kong Nga Po Site	Dust impact from excavation activities and earth	• Use of regular water spraying (once every 1.25 hours or 8 times per day) at all active works area exposed site surfaces and unpaved roads, particularly during dry weather

			moving	• Water spraying during loading and unloading of excavated materials • Vehicles used for transporting dusty materials/spoils will be covered by mechanical cover before leaving the site • Deploy water bowser for regular water spraying to enhance dust suppression • Speed control of site transportation • Stockpile of dusty materials will be covered by tarpaulin sheets to avoid wind-blown dust • Wheel washing facilities will be provided and cleaning the wheel of all vehicles before leaving the site
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition • Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of excavated materials to reduce the potential for water pollution

				• Provide wastewater treatment facilities prior to discharge of wastewater • Regular inspection and maintenance of wastewater treatment facilities • Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged.
EIA 7.5.1.1 & 7.5.1.2; EM&A Log 6.2			Waste Generation	• Training of site personnel in proper waste management and chemical handling procedures • Proper storage and sorting of excavated inert materials to maximize on site reuse for backfilling • Surplus inert C&D materials will be disposed of at designated Government's PFRF.
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Chemical waste should be stored at chemical waste container and collected by a licensed collector to transport and dispose of at the approved Chemical Waste Treatment Centre • Drip tray and chemical spillage kit will be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to frontline workers for the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative

				species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Restrict construction area to minimize the impact on existing retained trees
EIA 3.9.1; EM&A Log 2.2	Construction of footings	Kong Nga Po Site	Air	• Regular inspection and maintenance of plant and equipment in good condition • Regularly clean up stockpiles and debris to avoid accumulation of materials • Dusty materials exceeding 20 bags shall be stored in area sheltered on top and the three sides or covered entirely by impervious sheeting.
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition • Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out

EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	- Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged. - Designated location for residual concrete washout - Provide wastewater treatment facilities prior to discharge of wastewater
EIA 7.5.1.4; EM&A Log			Chemical Waste	Drip tray and chemical spillage kit shall be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	- Provide training to frontline workers for the conservative species - Provision of protective fence for the conservative species - Regular inspection for concerned vegetation and conservative species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	- Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement - Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts
EIA 3.9.1; EM&A Log 2.2	Construction of substructure and	Kong Nga Po Site	Air	- Regular inspection and maintenance of plant and equipment in good condition - Regularly clean up stockpiles and debris to avoid

	superstructure			accumulation of materials Dusty materials exceeding 20 bags shall be stored in area sheltered on top and the three sides or covered entirely by impervious sheeting.
EIA 4.4.6; EM&A Log 3.2			Noise Control	- Regular inspection and maintenance of plant & equipment in good condition - Enclose the noisy part of machineries with noise enclosure - Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	- Valid construction noise permit should be obtained and displayed on site - In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	- Cover the stockpiles of construction materials to reduce the potential for water pollution - Provide wastewater treatment facilities prior to discharge of wastewater - Wastewater generated from surface runoff shall be treated prior to discharge - Manholes should be temporarily sealed to prevent silt, construction materials or debris from entering the drainage system.

EIA 7.5.1.1; EM&A Log 6.2			Waste Management	• Cover stockpiles of C&D materials by impervious sheets to avoid wind-blown dust. • Spray water on all dusty materials including C&D materials immediately prior to any loading transfer operation • Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Drip tray and chemical spillage kit shall be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to frontline workers for the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts
EIA 3.9.1; EM&A Log 2.2	Construction of footbridge	Kong Nga Po Site	Air	• Regular inspection and maintenance of plant and equipment in good condition

				• Water spraying during loading and unloading of excavated materials • Regularly clean up stockpiles and debris to avoid accumulation of materials • Dusty materials exceeding 20 bags shall be stored in area sheltered on top and the three sides or covered entirely by impervious sheeting.
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of construction materials to reduce the potential for water pollution • Provide wastewater treatment facilities prior to discharge of wastewater • Wastewater generated from surface runoff shall be treated prior to discharge
EIA 7.5.1.1;			Waste	• Cover stockpiles of C&D materials by impervious sheets to

EM&A Log 6.2			Management	avoid wind-blown dust. • Spray water on all dusty materials including C&D materials immediately prior to any loading transfer operation • Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Drip tray and chemical spillage kit shall be provided on site
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts
EIA 3.9.1; EM&A Log 2.2	Backfilling	Kong Nga Po Site	Air	• Deploy water bowser for regular water spraying to enhance dust suppression • Manual water spraying for dusty operation where inaccessible by water bowser • Speed control of site transportation • Stockpile of dusty materials will be covered by tarpaulin sheets to avoid wind-blown dust • Vehicles used for transporting dusty materials/spoils will be covered by mechanical cover before leaving the site

				Wheel washing facilities will be provided and cleaning the wheel of all vehicles before leaving the site
EIA 4.4.6; EM&A Log 3.2			Noise Control	- Regular inspection and maintenance of plant & equipment in good condition - Enclose the noisy part of machineries with noise enclosure - Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	- Valid construction noise permit should be obtained and displayed on site - In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	- Cover the stockpiles of construction materials to reduce the potential for water pollution - Provide wastewater treatment facilities prior to discharge of wastewater - Regular inspection and maintenance of wastewater treatment facilities - Wastewater pumped out of the excavation areas will be treated to remove suspended solids prior to discharge - Hard paving or well-compact of main haul road to minimize washout of soil - Wheels of all vehicles and plants will be cleaned before

				leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged.
EIA 7.5.1.1 & 7.5.1.2; EM&A Log 6.2			Waste Generation	• Training of site personnel in proper waste management and chemical handling procedures • Proper storage and sorting of excavated inert materials to maximize on site reuse for backfilling • Surplus inert C&D materials will be disposed of at designated Government's PFRF or reuse at other contracts.

**EIA Ref/ EM&A Log/ Design Document Ref*

***Details of equipment, vehicles, plants, processes, technologies for the construction method*

Design and Construction of Kong Nga Po Police Training Facilities
Proactive Environmental Protection Proforma

Working Period: October 2025

Ref*	Proposed Construction Method	Location/Working Period	Anticipated Major Impacts	Recommended Mitigation Measures	Photo Records (Partial)
EIA 3.9.1; EM&A Log 2.2	Open cut excavation	Kong Nga Po Site	Dust impact	- Manual water spraying for dust suppression - Regular inspection and maintenance of plant and equipment in good condition - Cover stockpile with impervious sheets or grout - Provide wheel washing facility at site entrance	 By subcontractor at KNP site



By subcontractor at KNP site



By subcontractor at KNP site


EIA 4.4.6; EM&A Log 3.2			Noise	• Regular inspection and maintenance of plant & equipment in good condition • Deploy Quality Powered Mechanical Equipment (QPME) if possible • Valid construction noise permit should be displayed at site entrance.	 By main contractor at KNP site  By main contractor at KNP site
--	--	--	--------------	--	---

EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to workers about the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative species	 By main contractor at KNP site  By subcontractor at KNP site
---	--	--	------------------------	--	---

EIA 3.9.1; EM&A Log 2.2	Soil Removal	Kong Nga Po Site	Air	• Deploy water bowser for regular water spraying to enhance dust suppression • Cover dusty materials with impervious sheets • Exposed slopes covered with waterproof layers such as tarpaulin sheets or grout to reduce the potential for sediment laden runoff entering the drainage system. • The speed of the trucks within the site should be controlled to about 10km/hour in order to reduce adverse dust impacts and secure the safe movement around the site.	 By main contractor at KNP site  By main contractor at KNP site
--	---------------------	-------------------------	------------	--	---

EIA 4.4.6; EM&A Log 3.2			Noise	- Regular inspection and maintenance of plant & equipment in good condition - Deploy Quality Powered Mechanical Equipment (QPME) if possible	 By main contractor at KNP site
EIA 5.6.1.2 and EM&A Log 4.2			Water Quality	- Cover exposed slopes with impervious sheets or cement grout. - Wastewater pumped out of the excavation areas shall be treated to remove suspended solid prior to discharge. - Provide desilting/ sedimentation devices for wastewater treatment prior to discharge.	 By main contractor at KNP site

				Provide drip tray to prevent spillage of fuels	 21.10.2025 By main contractor at KNP site
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	- Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement - Implement temporary traffic arrangement which control construction area to	 17.10.2025 By main contractor at KNP site

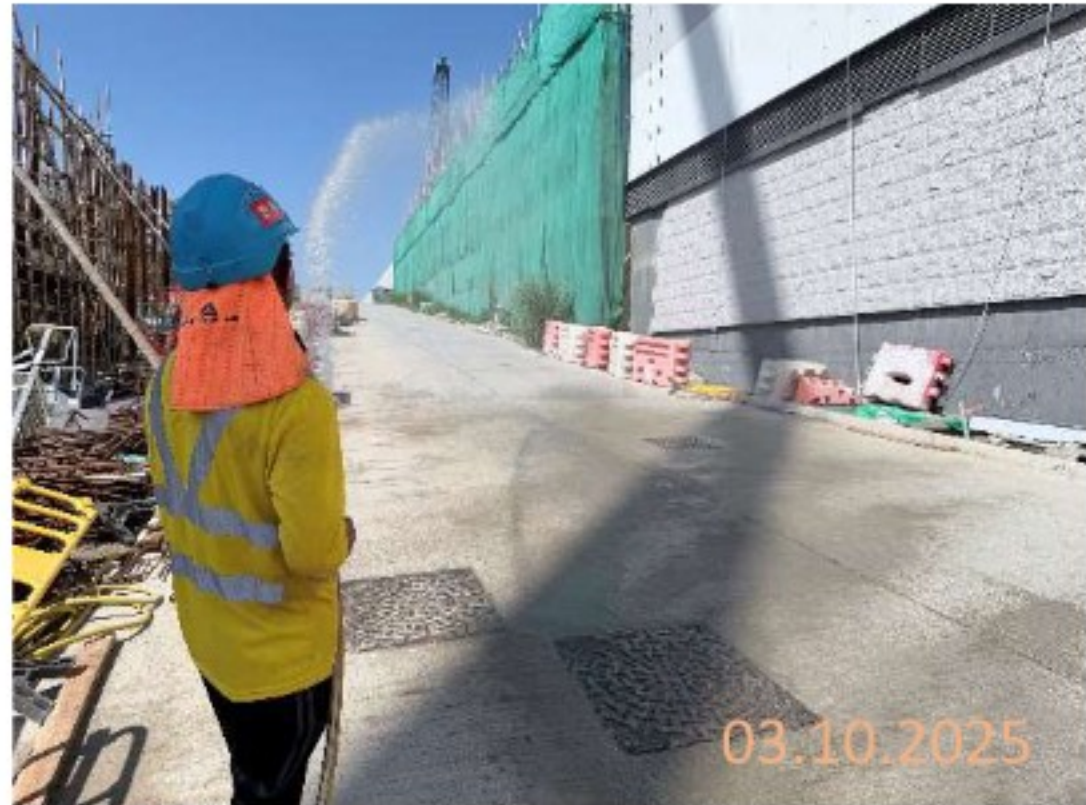				minimize landscape and visual impacts • Minimize visual impact during construction stage. Site office not visually prominent from public room and surrounding • Planting will take place as soon the planting area is installed with subsoil drainage • Decorative hoarding is provided	
EIA 3.9.1; EM&A Log 2.2	Construction of footings, substructure and superstructure	Kong Nga Po Site	Air	• Cover dusty materials with impervious sheets • Exposed slopes covered with waterproof layers such as tarpaulin sheets or grout to reduce the potential for sediment laden runoff entering	

				the drainage system. Provide wheel washing facility at site entrance	By subcontractor at KNP site  By subcontractor at KNP site
EIA 4.4.6; EM&A Log 3.2			Noise	Valid construction noise permit should be obtained and displayed on site	 By main contractor at KNP site
EIA 5.6.1.3 and EM&A			Water Quality	Surface water from concrete batching areas	

Log 4.2

and the rest of the site should be separated as far as possible.

- Temporary drainage is free of obstruction.
- Gullies are sealed to prevent silt or debris from entering the drainage system.



By main contractor at KNP site



By main contractor at KNP site

EIA 7.5.1.2 and EM&A Log 6.2			Waste Management	• Segregation and storage of different types of waste in different containers or skips or stockpiles to enhance reuse or recycling of materials and their proper disposal • Sort non-inert C&D materials to recover any recyclable portions	 By main contractor at KNP site  By main contractor at KNP site
---	--	--	-----------------------------	--	--
