

APPENDIX A

**CONSTRUCTION PROGRAMME AND
PROACTIVE ENVIRONMENTAL
PROTECTION PROFORMA**

Construction Programme (Dec 2025 – Feb 2026)

Revision : Revision 16 (August 2025)


中國運籌聯營

CHINA STATE JOINT VENTURE

Baseline Milestone		Critical Task		Inactive Milestone		Duration-only		Start-only		External Milestone		Path Driving Predecessor Normal Task	
Baseline Summary		Milestone		Inactive Summary		Manual Summary Rollup		Finish-only			Path Driving Predecessor Milestone Task		Baseline
Task		Summary		Manual Task		Manual Task		External Tasks			Path Driving Predecessor Summary Task		


Design & Construction of Kong Nga Po Police Training Facilities Programme

Revision : Revision 16 (August 2025)

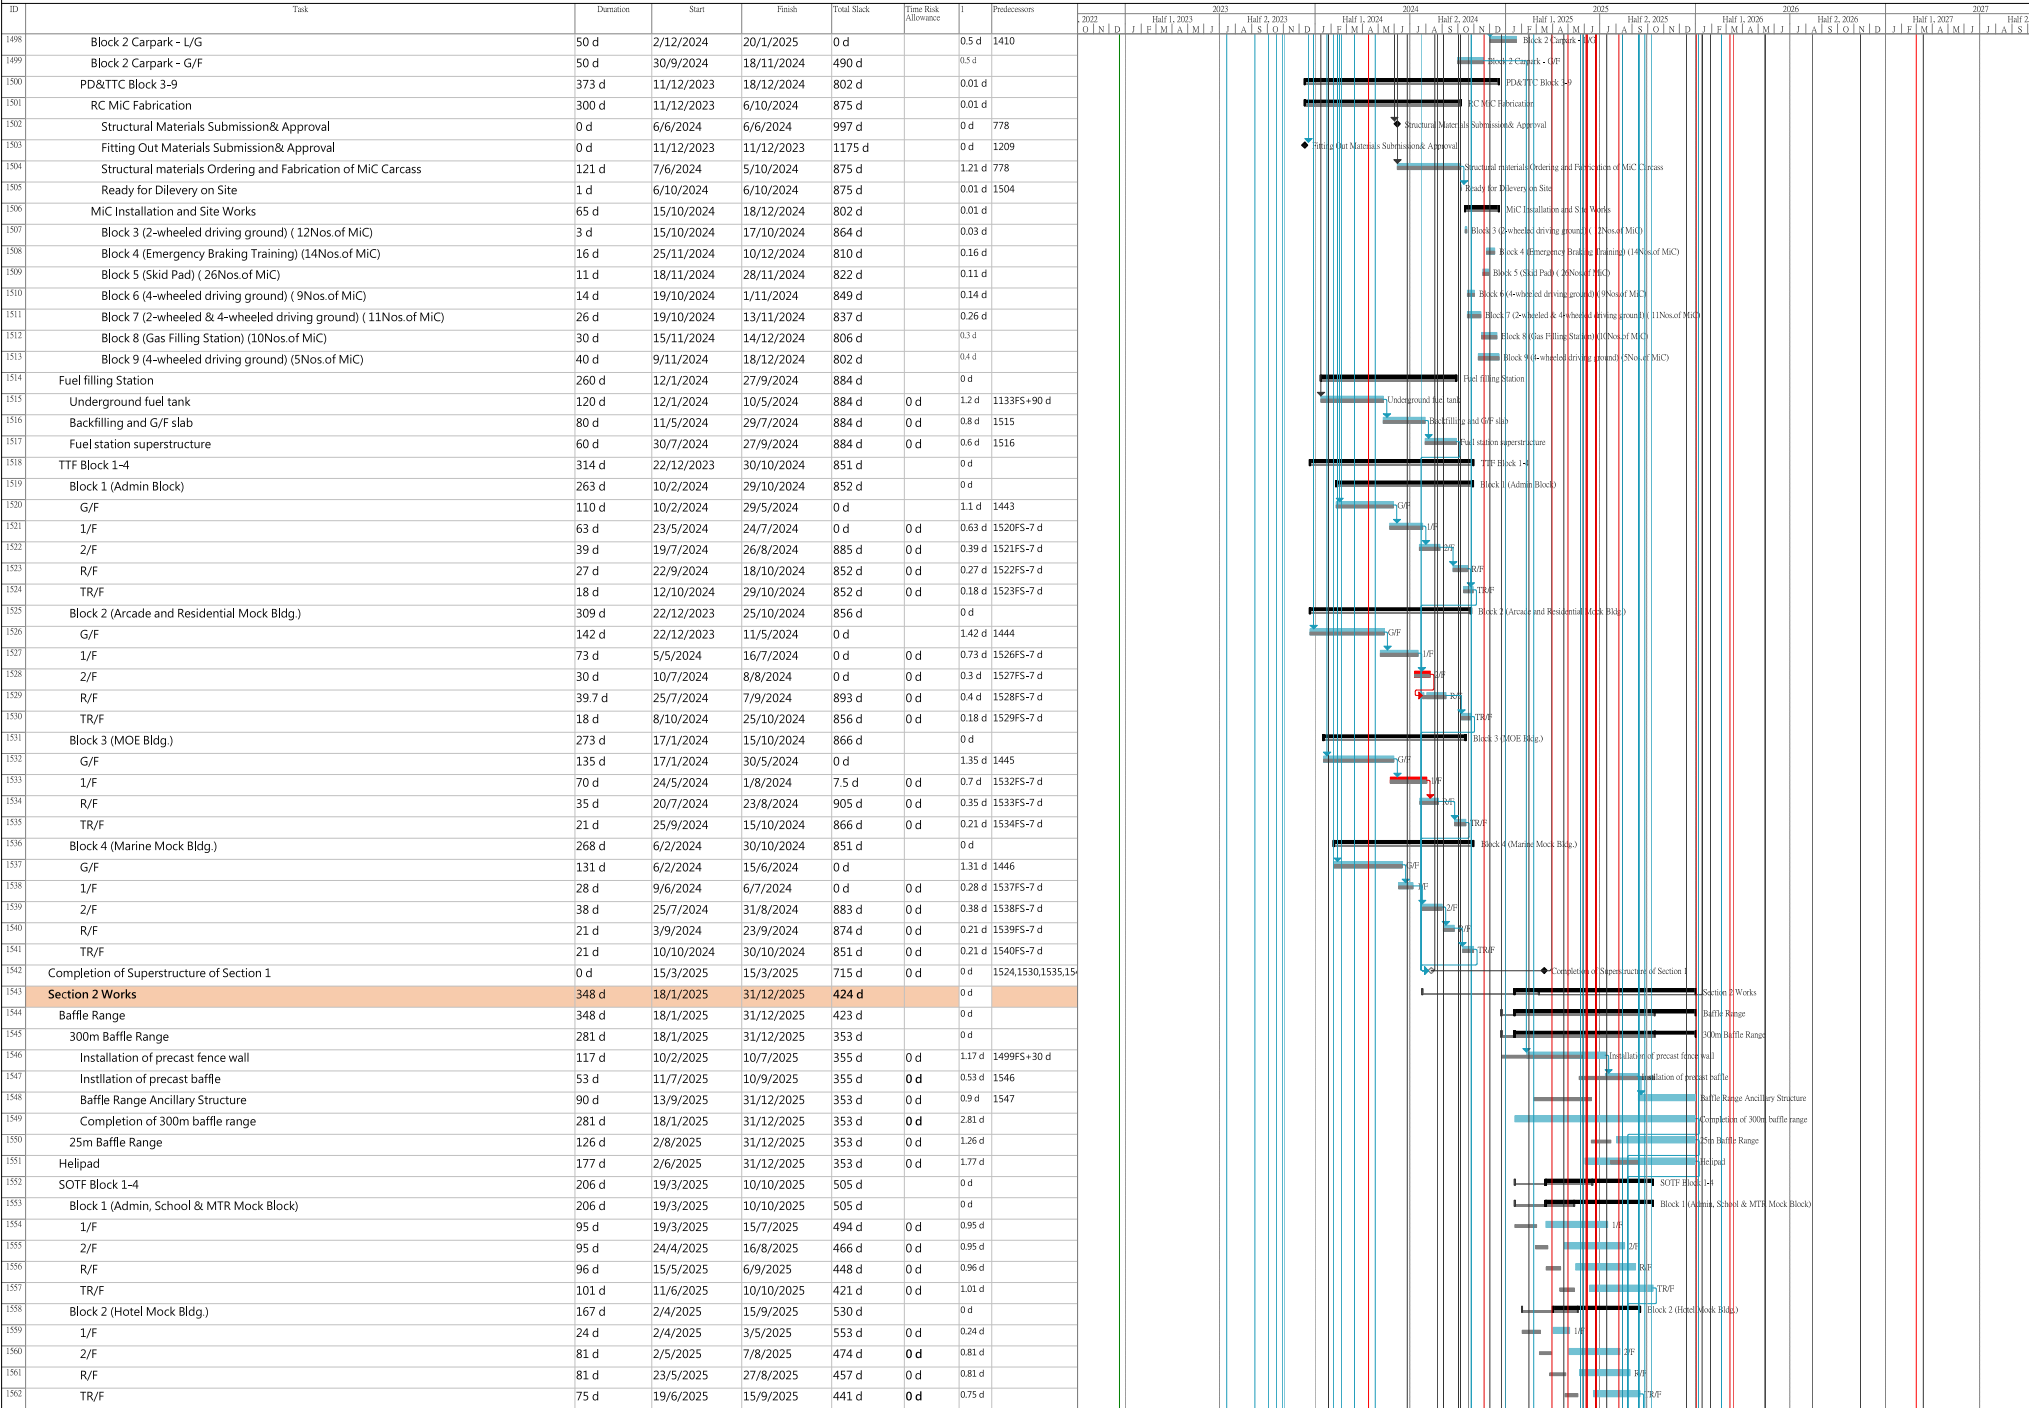


Design & Construction of Kong Nga Po Police Training Facilities Programme

Revision : Revision 16 (August 2025)

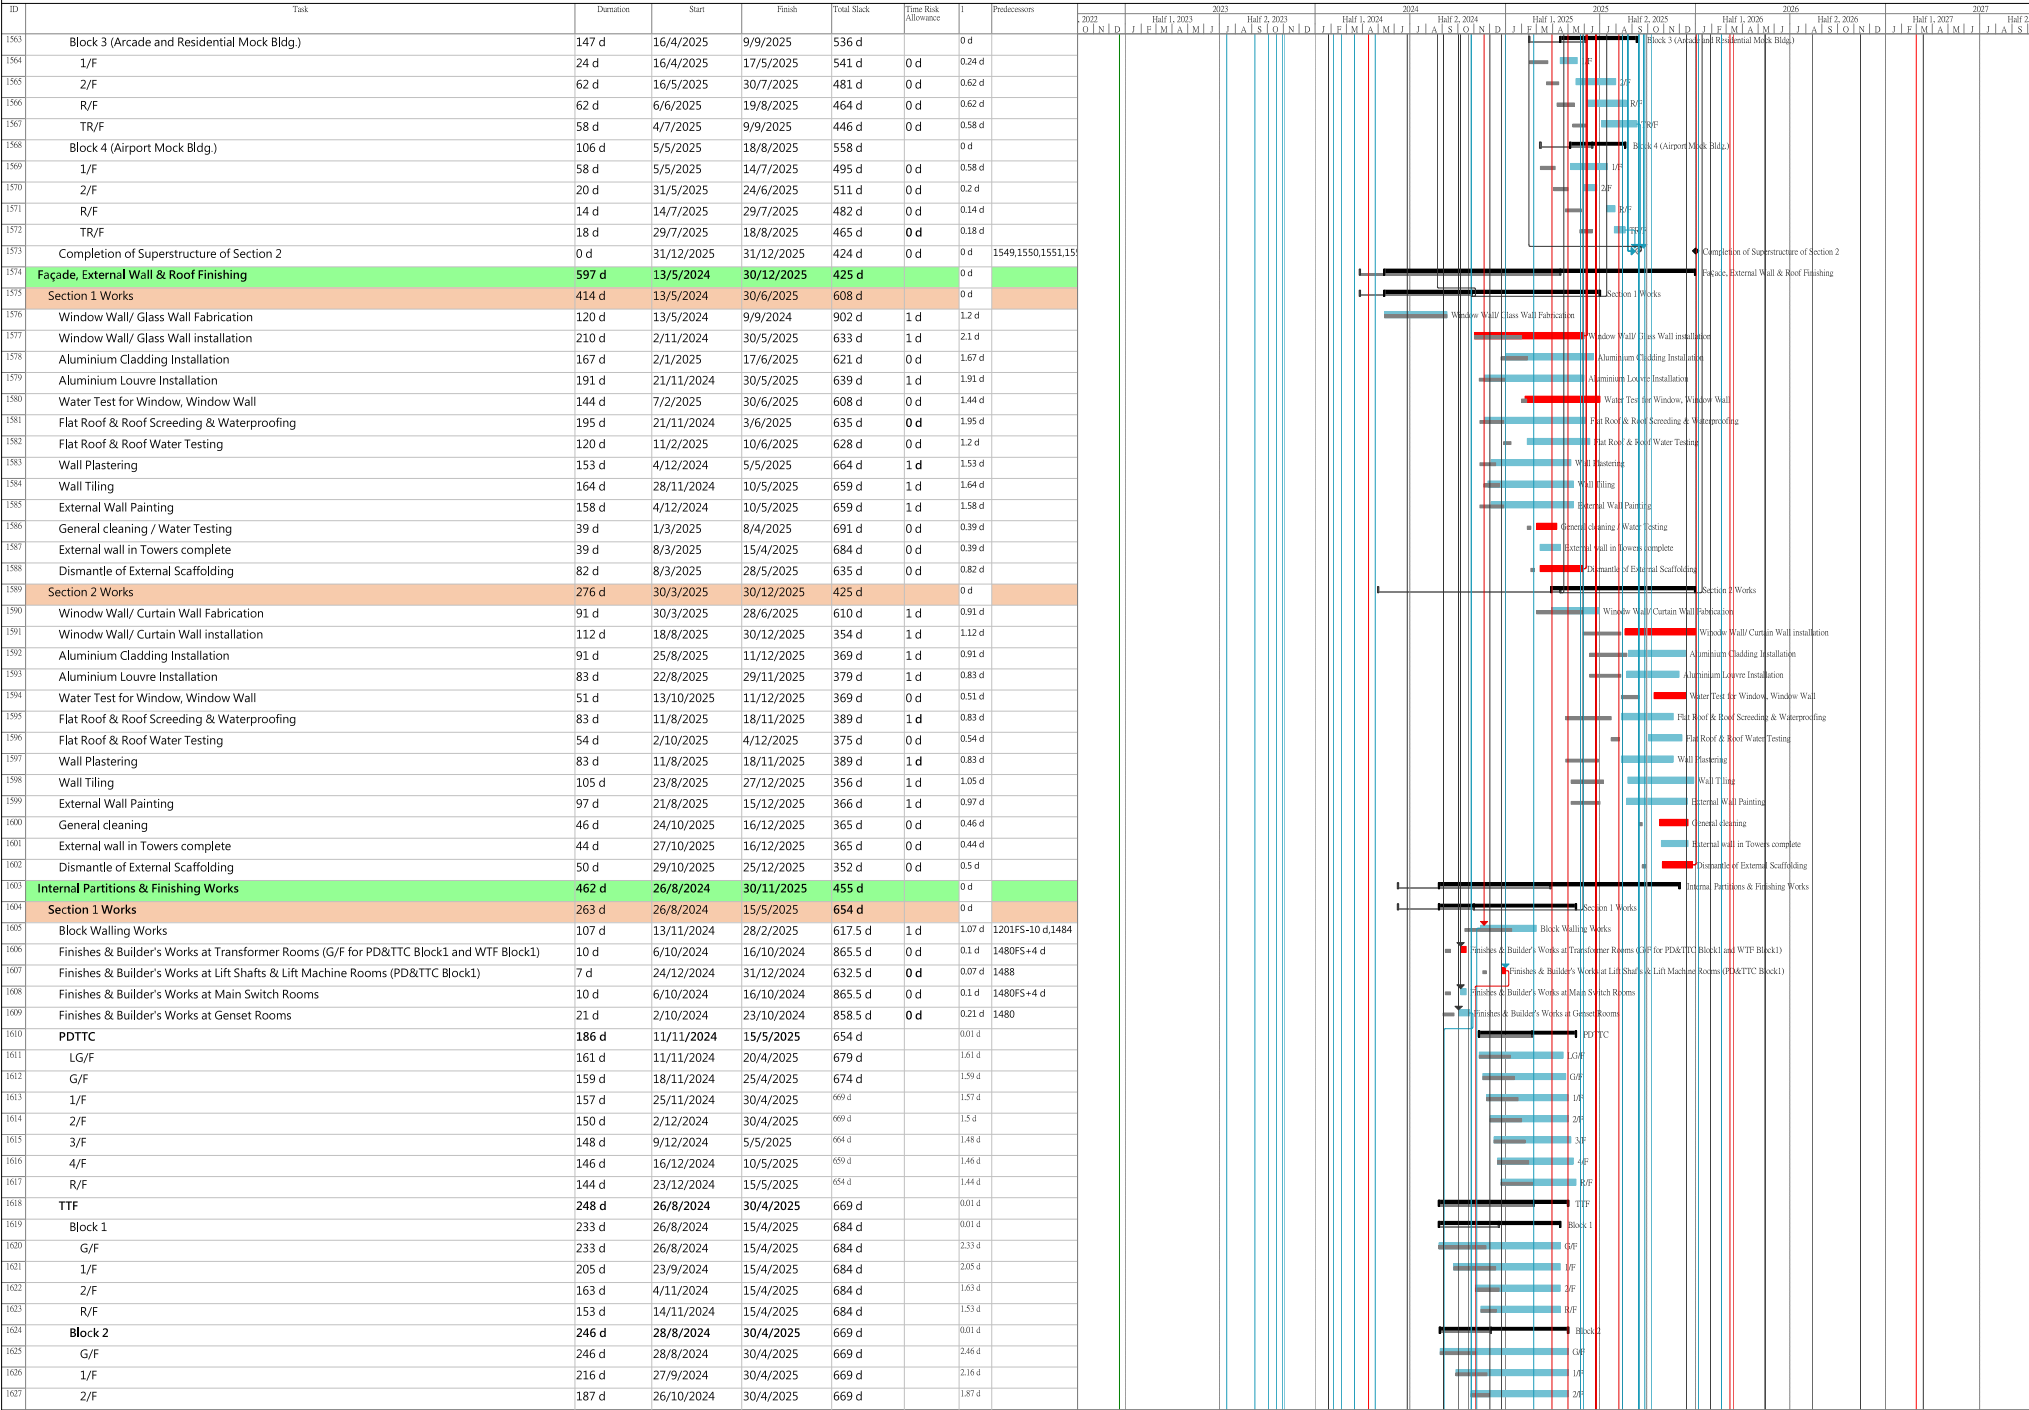

Design & Construction of Kong Nga Po Police Training Facilities Programme

Revision : Revision 16 (August 2025)

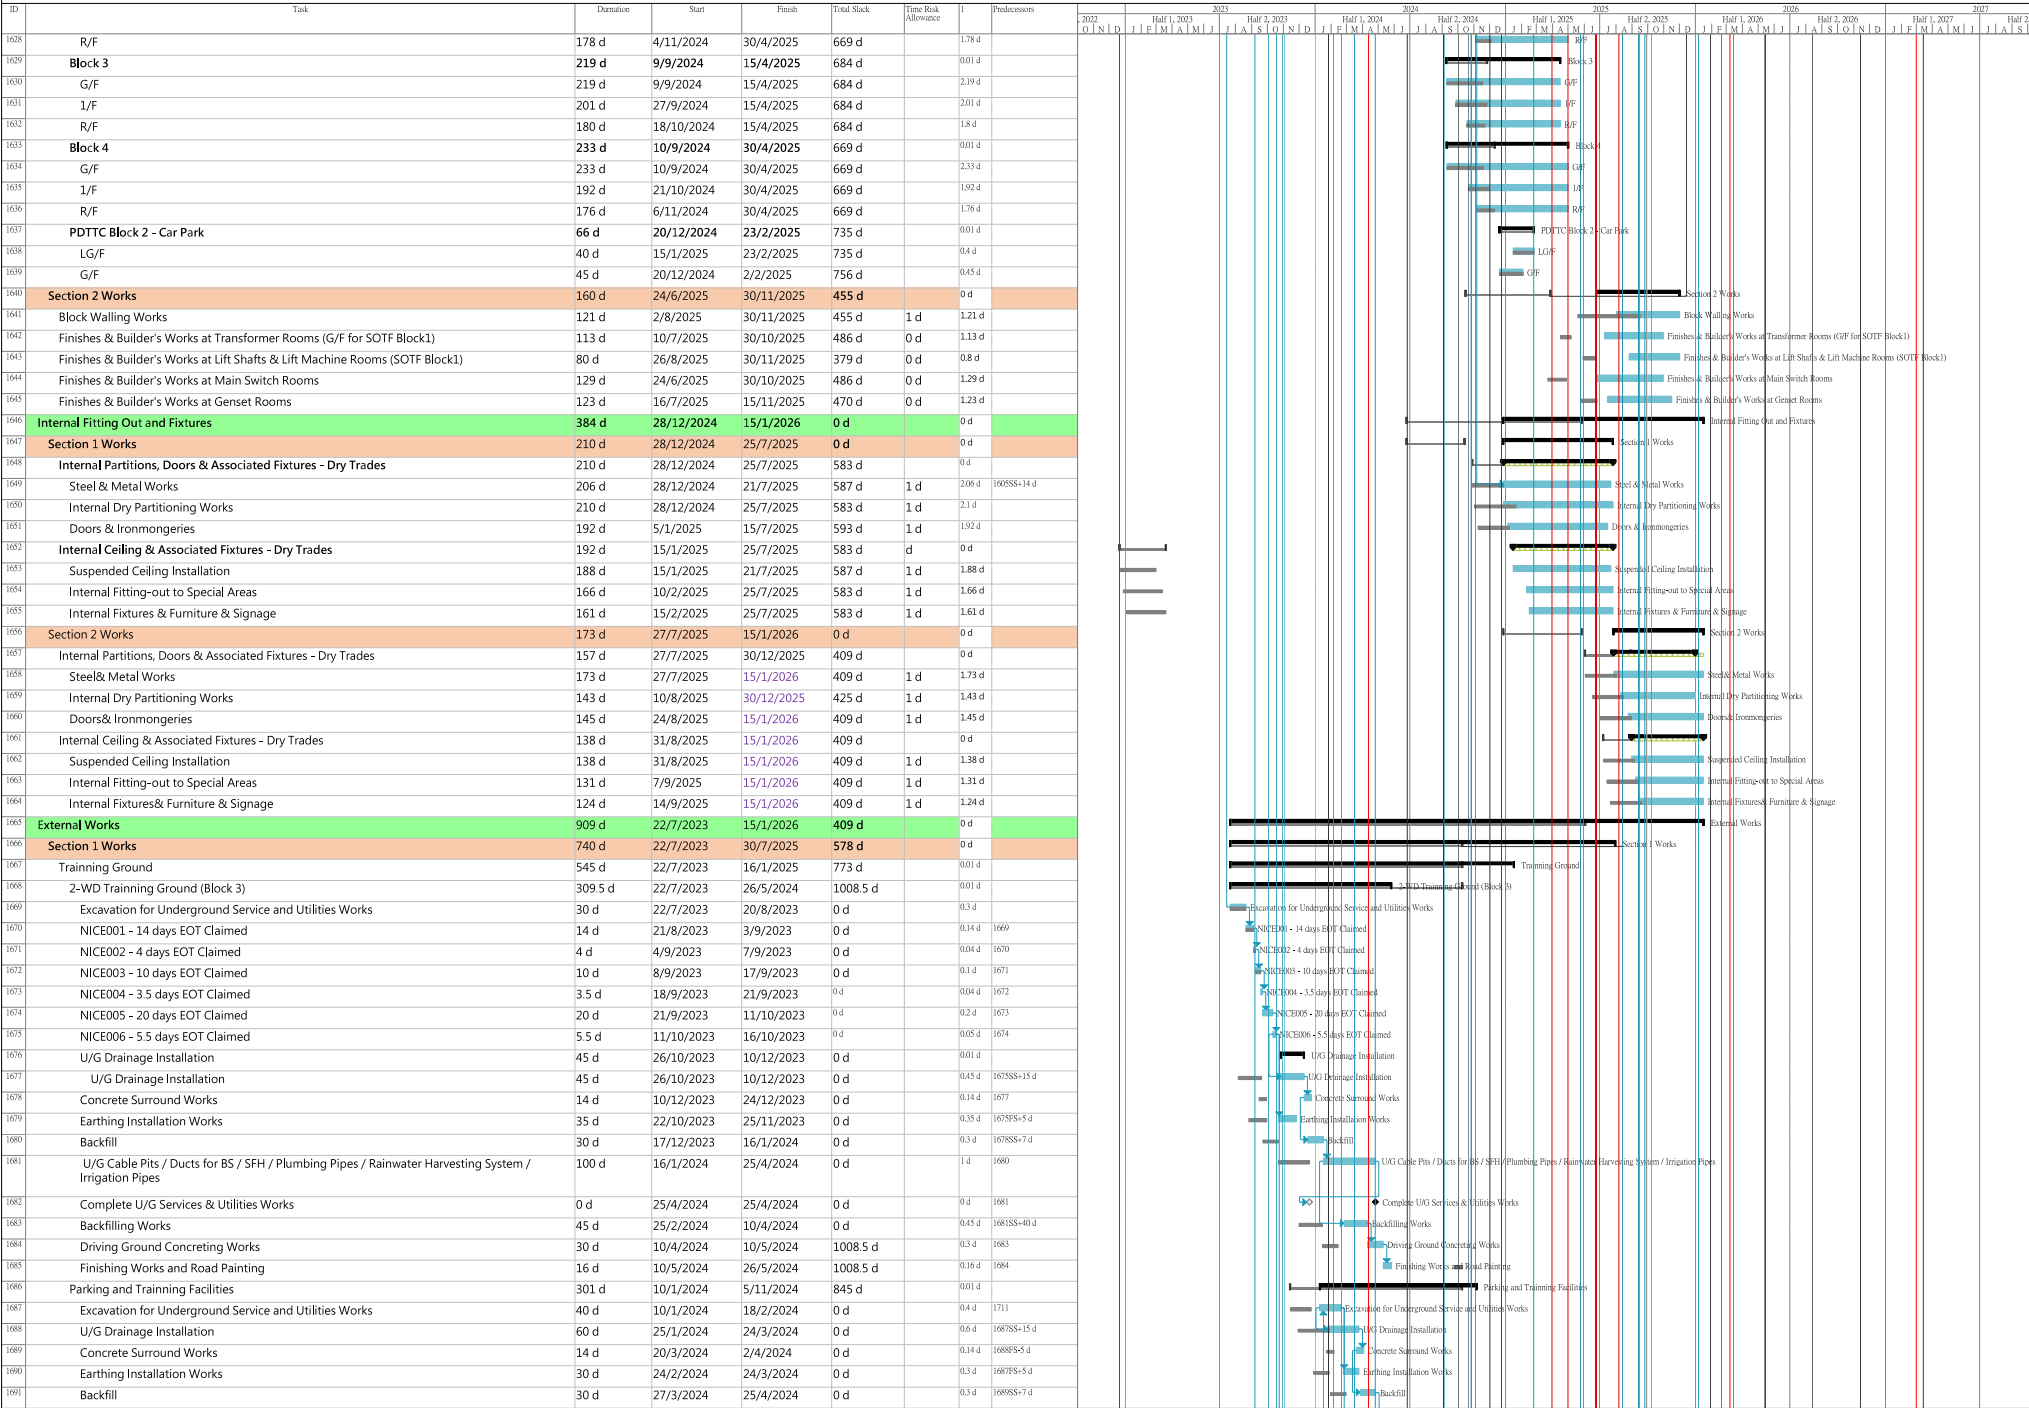

Design & Construction of Kong Nga Po Police Training Facilities Programme

Revision : Revision 16 (August 2025)

ID	Task	Duration	Start	Finish	Total Slack	Time Risk Allowance	I	Predecessors	2022	2023	2024	2025	2026	2027
1692	U/G Cable Pits / Ducts for BS / SFH / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	60 d	26/4/2024	24/6/2024	0 d		0.6 d	1691						
1693	Complete U/G Services & Utilities Works	0 d	24/6/2024	24/6/2024	0 d		0 d	1692						
1694	Backfilling Works	45 d	5/6/2024	19/7/2024	0 d		0.45 d	1693SS+40 d						
1695	Driving Ground Concreting Works	30 d	20/7/2024	18/8/2024	924 d		0.3 d	1694						
1696	Finishing Works and Road Painting	15 d	22/10/2024	5/11/2024	845 d		0.15 d	173SSS						
1697	Braking Training (Block 4)	282 d	17/10/2023	24/7/2024	949 d		0.01 d							
1698	Excavation for Underground Service and Utilities Works	55 d	17/10/2023	10/12/2023	0 d		0.01 d							
1699	Excavation for Underground Service and Utilities Works	45 d	17/10/2023	30/11/2023	0 d		0.45 d	1675						
1700	NICE003 - 10 days EOT Claimed	10 d	1/12/2023	10/12/2023	0 d		0.1 d	1699						
1701	U/G Drainage Installation	60 d	16/12/2023	13/2/2024	0 d		0.6 d	1700SS+15 d						
1702	Concrete Surround Works	14 d	9/2/2024	22/2/2024	0 d		0.14 d	1701FS+5 d						
1703	Earthing Installation Works	40 d	6/12/2023	14/1/2024	0 d		0.4 d	1699FS+5 d						
1704	Backfill	30 d	16/2/2024	16/3/2024	0 d		0.3 d	1702SS+7 d						
1705	U/G Cable Pits / Ducts for BS / SFH / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	60 d	17/3/2024	15/5/2024	1019 d		0.6 d	1704						
1706	Complete U/G Services & Utilities Works	0 d	15/5/2024	15/5/2024	1019 d		0 d	1705						
1707	Backfilling Works	45 d	26/4/2024	9/6/2024	949 d		0.45 d	1705SS+40 d						
1708	Driving Ground Concreting Works	30 d	10/6/2024	9/7/2024	949 d		0.3 d	1707						
1709	Finishing Works and Road Painting	15 d	10/7/2024	24/7/2024	949 d		0.15 d	1708						
1710	Skid Pan (Block 5)	227 d	1/12/2023	14/7/2024	959 d		0.01 d							
1711	Excavation for Underground Service and Utilities Works	40 d	1/12/2023	9/1/2024	0 d		0.4 d	1699						
1712	U/G Drainage Installation	50 d	16/12/2023	3/2/2024	0 d		0.5 d	1711SS+15 d						
1713	Concrete Surround Works	14 d	30/1/2024	12/2/2024	0 d		0.14 d	1712FS+5 d						
1714	Earthing Installation Works	35 d	15/1/2024	18/2/2024	0 d		0.35 d	1711FS+5 d						
1715	Backfill	30 d	6/2/2024	6/3/2024	0 d		0.3 d	1713SS+7 d						
1716	U/G Cable Pits / Ducts for BS / SFH / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	60 d	7/3/2024	5/5/2024	0 d		0.6 d	1715						
1717	Complete U/G Services & Utilities Works	0 d	5/5/2024	5/5/2024	1029 d		0 d	1716						
1718	Backfilling Works	45 d	16/4/2024	30/5/2024	959 d		0.45 d	1716SS+40 d						
1719	Driving Ground Concreting Works	30 d	31/5/2024	29/6/2024	959 d		0.3 d	1718						
1720	Finishing Works and Road Painting	15 d	30/6/2024	14/7/2024	959 d		0.15 d	1719						
1721	4-WD Training Ground (Block 6 and Block 9)	272 d	30/3/2024	26/12/2024	794 d		0.01 d							
1722	Excavation for Underground Service and Utilities Works	40 d	30/3/2024	8/5/2024	0 d		0.4 d	1733						
1723	U/G Drainage Installation	45 d	14/4/2024	28/5/2024	0 d		0.45 d	1722SS+15 d						
1724	Concrete Surround Works	14 d	24/5/2024	6/6/2024	0 d		0.14 d	1723FS+5 d						
1725	Earthing Installation Works	30 d	14/5/2024	12/6/2024	0 d		0.3 d	1722FS+5 d						
1726	Backfill	30 d	31/5/2024	29/6/2024	0 d		0.3 d	1724SS+7 d						
1727	U/G Cable Pits / Ducts for BS / SFH / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	150 d	30/6/2024	26/11/2024	0 d		1.5 d	1726						
1728	Complete U/G Services & Utilities Works	30 d	28/8/2024	26/12/2024	794 d		0.3 d	1727						
1729	Backfilling Works	45 d	9/8/2024	22/9/2024	847 d		0.45 d	1727SS+40 d						
1730	Driving Ground Concreting Works	27 d	23/9/2024	19/10/2024	847 d		0.27 d	1729						
1731	Finishing Works and Road Painting	15 d	20/10/2024	3/11/2024	847 d		0.15 d	1730						
1732	2-WD and 4-WD Training Ground (Block 7)	312 d	19/2/2024	26/12/2024	794 d		0.01 d							
1733	Excavation for Underground Service and Utilities Works	40 d	19/2/2024	29/3/2024	0 d		0.4 d	1687						
1734	U/G Drainage Installation	55 d	5/3/2024	28/4/2024	0 d		0.55 d	1733SS+15 d						
1735	Concrete Surround Works	14 d	24/4/2024	7/5/2024	0 d		0.14 d	1734FS+5 d						
1736	Earthing Installation Works	30 d	4/4/2024	3/5/2024	0 d		0.3 d	1733FS+5 d						
1737	Backfill	30 d	1/5/2024	30/5/2024	0 d		0.3 d	1735SS+7 d						
1738	U/G Cable Pits / Ducts for BS / SFH / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	150 d	31/5/2024	27/10/2024	0 d		1.5 d	1737						
1739	Complete U/G Services & Utilities Works	60 d	29/7/2024	26/12/2024	794 d		0.6 d	1738						
1740	Backfilling Works	45 d	10/7/2024	23/8/2024	15 d		0.45 d	1738SS+40 d						
1741	Driving Ground Concreting Works	30 d	24/8/2024	22/9/2024	874 d		0.3 d	1740						
1742	Finishing Works and Road Painting	15 d	23/9/2024	7/10/2024	874 d		0.15 d	1741						
1743	Gas Filling Station (Block 8)	253 d	9/5/2024	16/1/2025	773 d		0.01 d							
1744	Excavation for Underground Service and Utilities Works	50 d	9/5/2024	27/6/2024	0 d		0.5 d	1722						
1745	U/G Drainage Installation	45 d	24/5/2024	7/7/2024	773 d		0.45 d	1744SS+15 d						
1746	Concrete Surround Works	14 d	8/7/2024	21/7/2024	773 d		0.14 d	1745						
1747	Earthing Installation Works	30 d	13/7/2024	11/8/2024	931 d		0.3 d	1745FS+5 d						
1748	Backfill	34 d	17/7/2024	19/8/2024	773 d		0.34 d	1746FS+5 d						
1749	U/G Cable Pits / Ducts for BS / SFH / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	150 d	20/8/2024	16/1/2025	773 d		1.5 d	1748						
1750	Complete U/G Services & Utilities Works	0 d	16/1/2025	16/1/2025	773 d		0 d	1749						

Design & Construction of Kong Nga Po Police Training Facilities Programme


Revision : Revision 16 (August 2025)

ID	Task	Duration	Start	Finish	Total Slack	Time Risk Allowance	1	Predecessors		2022	2023	2024	2025	2026	2027
1751	Backfilling Works	30 d	9/9/2024	8/10/2024	845 d		0.3 d	1749SS+20 d							
1752	Driving Ground Concreting Works	13 d	9/10/2024	21/10/2024	845 d		0.13 d	1751							
1753	Finishing Works and Road Painting	12 d	22/10/2024	2/11/2024	845 d		0.12 d	1752							
1754	Boundary Fencing, Planters & RC Structures	84 d	8/5/2025	30/7/2025	578 d		0 d								
1755	Boundary Fence Wall Structures	80 d	12/5/2025	30/7/2025	578 d	0 d	0.8 d								
1756	Planter Wall Structures	84 d	8/5/2025	30/7/2025	578 d	0 d	0.84 d								
1757	Complete Boundary Fencing, Planters & RC Structures	0 d	30/7/2025	30/7/2025	578 d	0 d	0 d								
1758	Underground Services & Utilities Works	609 d	30/11/2023	30/7/2025	578 d		0 d								
1759	U/G Drainage Works	277 d	27/10/2024	30/7/2025	578 d	1 d	2.77 d	798FS+30 d							
1760	U/G Cable Pits / Ducts for BS / SFH / AC Water Pipes / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	277 d	27/10/2024	30/7/2025	578 d	1 d	2.77 d	798FS+30 d							
1761	Complete U/G Services & Utilities Works	0 d	30/7/2025	30/7/2025	578 d	0 d	0 d	1759,1760,1767							
1762	Carriageway, Paving & Finishing	282 d	22/10/2024	30/7/2025	578 d	d	0 d								
1763	Steel & Metalworks	262 d	11/11/2024	30/7/2025	578 d	0 d	2.62 d								
1764	EVA / Carriageway & Paving Slabs	65 d	27/5/2025	30/7/2025	578 d	1 d	0.65 d								
1765	Finishings & Fitting-out Works	60 d	1/6/2025	30/7/2025	578 d	0 d	0.6 d								
1766	Complete Carriageway, Paving & Finishing Works	0 d	30/7/2025	30/7/2025	578 d	0 d	0 d	1763,1764,1765,17							
1767	CNE-21 Additional reinstatement works due to BK's defective U-chnnel and associated cable ducts after black rainstorm (8/9/2023)	0 d	22/10/2024	22/10/2024	860 d		0 d								
1768	PMI-10a Extension of Concrete walls of cable drawpits	0 d	26/12/2024	26/12/2024	795 d		0 d								
1769	PMI-10b Enlargement of CLP Cable Drawpit and modification of cable ducts as requested by CLP	0 d	26/12/2024	26/12/2024	795 d		0 d								
1770	Complete External Works of Section1	0 d	30/7/2025	30/7/2025	578 d	0 d	0 d	1761,1766,1753							
1771	Section 2 Works	128 d	10/9/2025	15/1/2026	0 d		0 d								
1772	Boundary Fencing, Planters & RC Structures	0 d	30/12/2025	30/12/2025	372 d		0 d								
1773	Boundary Fence Wall Structures	45 d	7/11/2025	30/12/2025	354 d	1 d	0.45 d								
1774	Planter Wall Structures	45 d	7/11/2025	30/12/2025	354 d	1 d	0.45 d								
1775	Complete Boundary Fencing, Planters& RC Structures	0 d	30/12/2025	30/12/2025	354 d	0 d	0 d								
1776	Underground Services & Utilities Works	112 d	10/9/2025	30/12/2025	425 d		0 d								
1777	U/G Drainage Works	92 d	10/9/2025	30/12/2025	354 d	1 d	0.92 d								
1778	U/G Cable Pits / Ducts for BS / SFH / AC Water Pipes / Plumbing Pipes / Rainwater Harvesting System / Irrigation Pipes	92 d	10/9/2025	30/12/2025	354 d	1 d	0.92 d								
1779	Complete U/G Services & Utilities Works	0 d	30/12/2025	30/12/2025	354 d	0 d	0 d								
1780	Carriageway, Paving & Finishing	0 d	30/12/2025	30/12/2025	355 d		0 d								
1781	Steel & Metalworks	45 d	7/11/2025	30/12/2025	354 d	0 d	0.45 d								
1782	EVA / Carriageway & Paving Slabs	60 d	21/10/2025	30/12/2025	354 d	1 d	0.6 d								
1783	Finishings & Fitting-out Works	30 d	10/12/2025	15/1/2026	341 d	1 d	0.3 d								
1784	Complete Carriageway, Paving & Finishing Works	0 d	15/1/2026	15/1/2026	341 d	0 d	0 d								
1785	Complete External Works of Section2	0 d	15/1/2026	15/1/2026	341 d	0 d	0 d								
1786	Works Outside Site Boundary	30 d	1/7/2025	30/7/2025	578 d		0 d								
1787	U/G Drainage & Utility Connection Works	30 d	1/7/2025	30/7/2025	578 d	0 d	0.3 d								
1788	Run-in/out Construction	30 d	1/7/2025	30/7/2025	578 d	0 d	0.3 d								
1789	Complete Works Outside Site Boundary	0 d	30/7/2025	30/7/2025	578 d	0 d	0 d								
1790	Landscaping Works	997 d	7/6/2024	28/2/2027	0 d		0 d								
1791	Section 1 Works	410 d	16/6/2025	30/7/2026	213 d		0 d								
1792	Hard Landscape Works	30 d	1/7/2025	30/7/2025	578 d	1 d	0.3 d								
1793	Soft Landscape Works	45 d	16/6/2025	30/7/2025	578 d	0 d	0.45 d								
1794	Complete Landscape Works of Section1	0 d	30/7/2025	30/7/2025	578 d	0 d	0 d								
1795	Establishment Period or DLP Period	365 d	31/7/2025	30/7/2026	213 d		3.65 d								
1796	Section 2 Works	997 d	7/6/2024	28/2/2027	0 d		0 d								
1797	Hard Landscape Works	26 d	3/2/2026	28/2/2026	365 d	1 d	0.26 d								
1798	Soft Landscape Works	120 d	1/11/2025	28/2/2026	365 d	2 d	1.2 d								
1799	Nursery (up to 400mm height x 400mm spread)	632 d	7/6/2024	28/2/2026	365 d		6.32 d								
1800	Delivery by Batch	391 d	3/2/2025	28/2/2026	365 d		3.91 d								
1801	Complete Landscape Works of Section2	271 d	3/6/2025	28/2/2026	300 d	0 d	2.71 d								
1802	Establishment Period or DLP Period	365 d	1/3/2026	28/2/2027	0 d		3.65 d								
1803	E&M Installation	892 d	21/9/2023	28/2/2026	365 d		0 d								
1804	Section 1 Works	685 d	21/9/2023	5/8/2025	572 d		0 d								
1805	Transformer Room at G/F (PD&ITC Block1 and TTF Block1)	134 d	27/9/2024	7/2/2025	751 d		0 d								
1806	E&M Works in Transformer Rooms	12 d	27/9/2024	8/10/2024	873 d	0 d	0.12 d								
1807	Handover of TX room to CLP	1 d	8/10/2024	8/10/2024	0 d	0 d	0.01 d	1806							
1808	Transformer Installation	52 d	8/10/2024	29/11/2024	821 d	1 d	0.52 d	1807							
1809	CLP cable laying works	52 d	9/10/2024	29/11/2024	751 d	0 d	0.52 d	1807							
1810	Potential Delay by CLP at KNP Road	70 d	30/11/2024	7/2/2025	751 d		0.7 d	1809							
1811	Energization of Transformers	0 d	7/2/2025	7/2/2025	751 d	0 d	0 d	1810							

Layout Plan with major construction activities

Legend:

Foundation construction and associated works

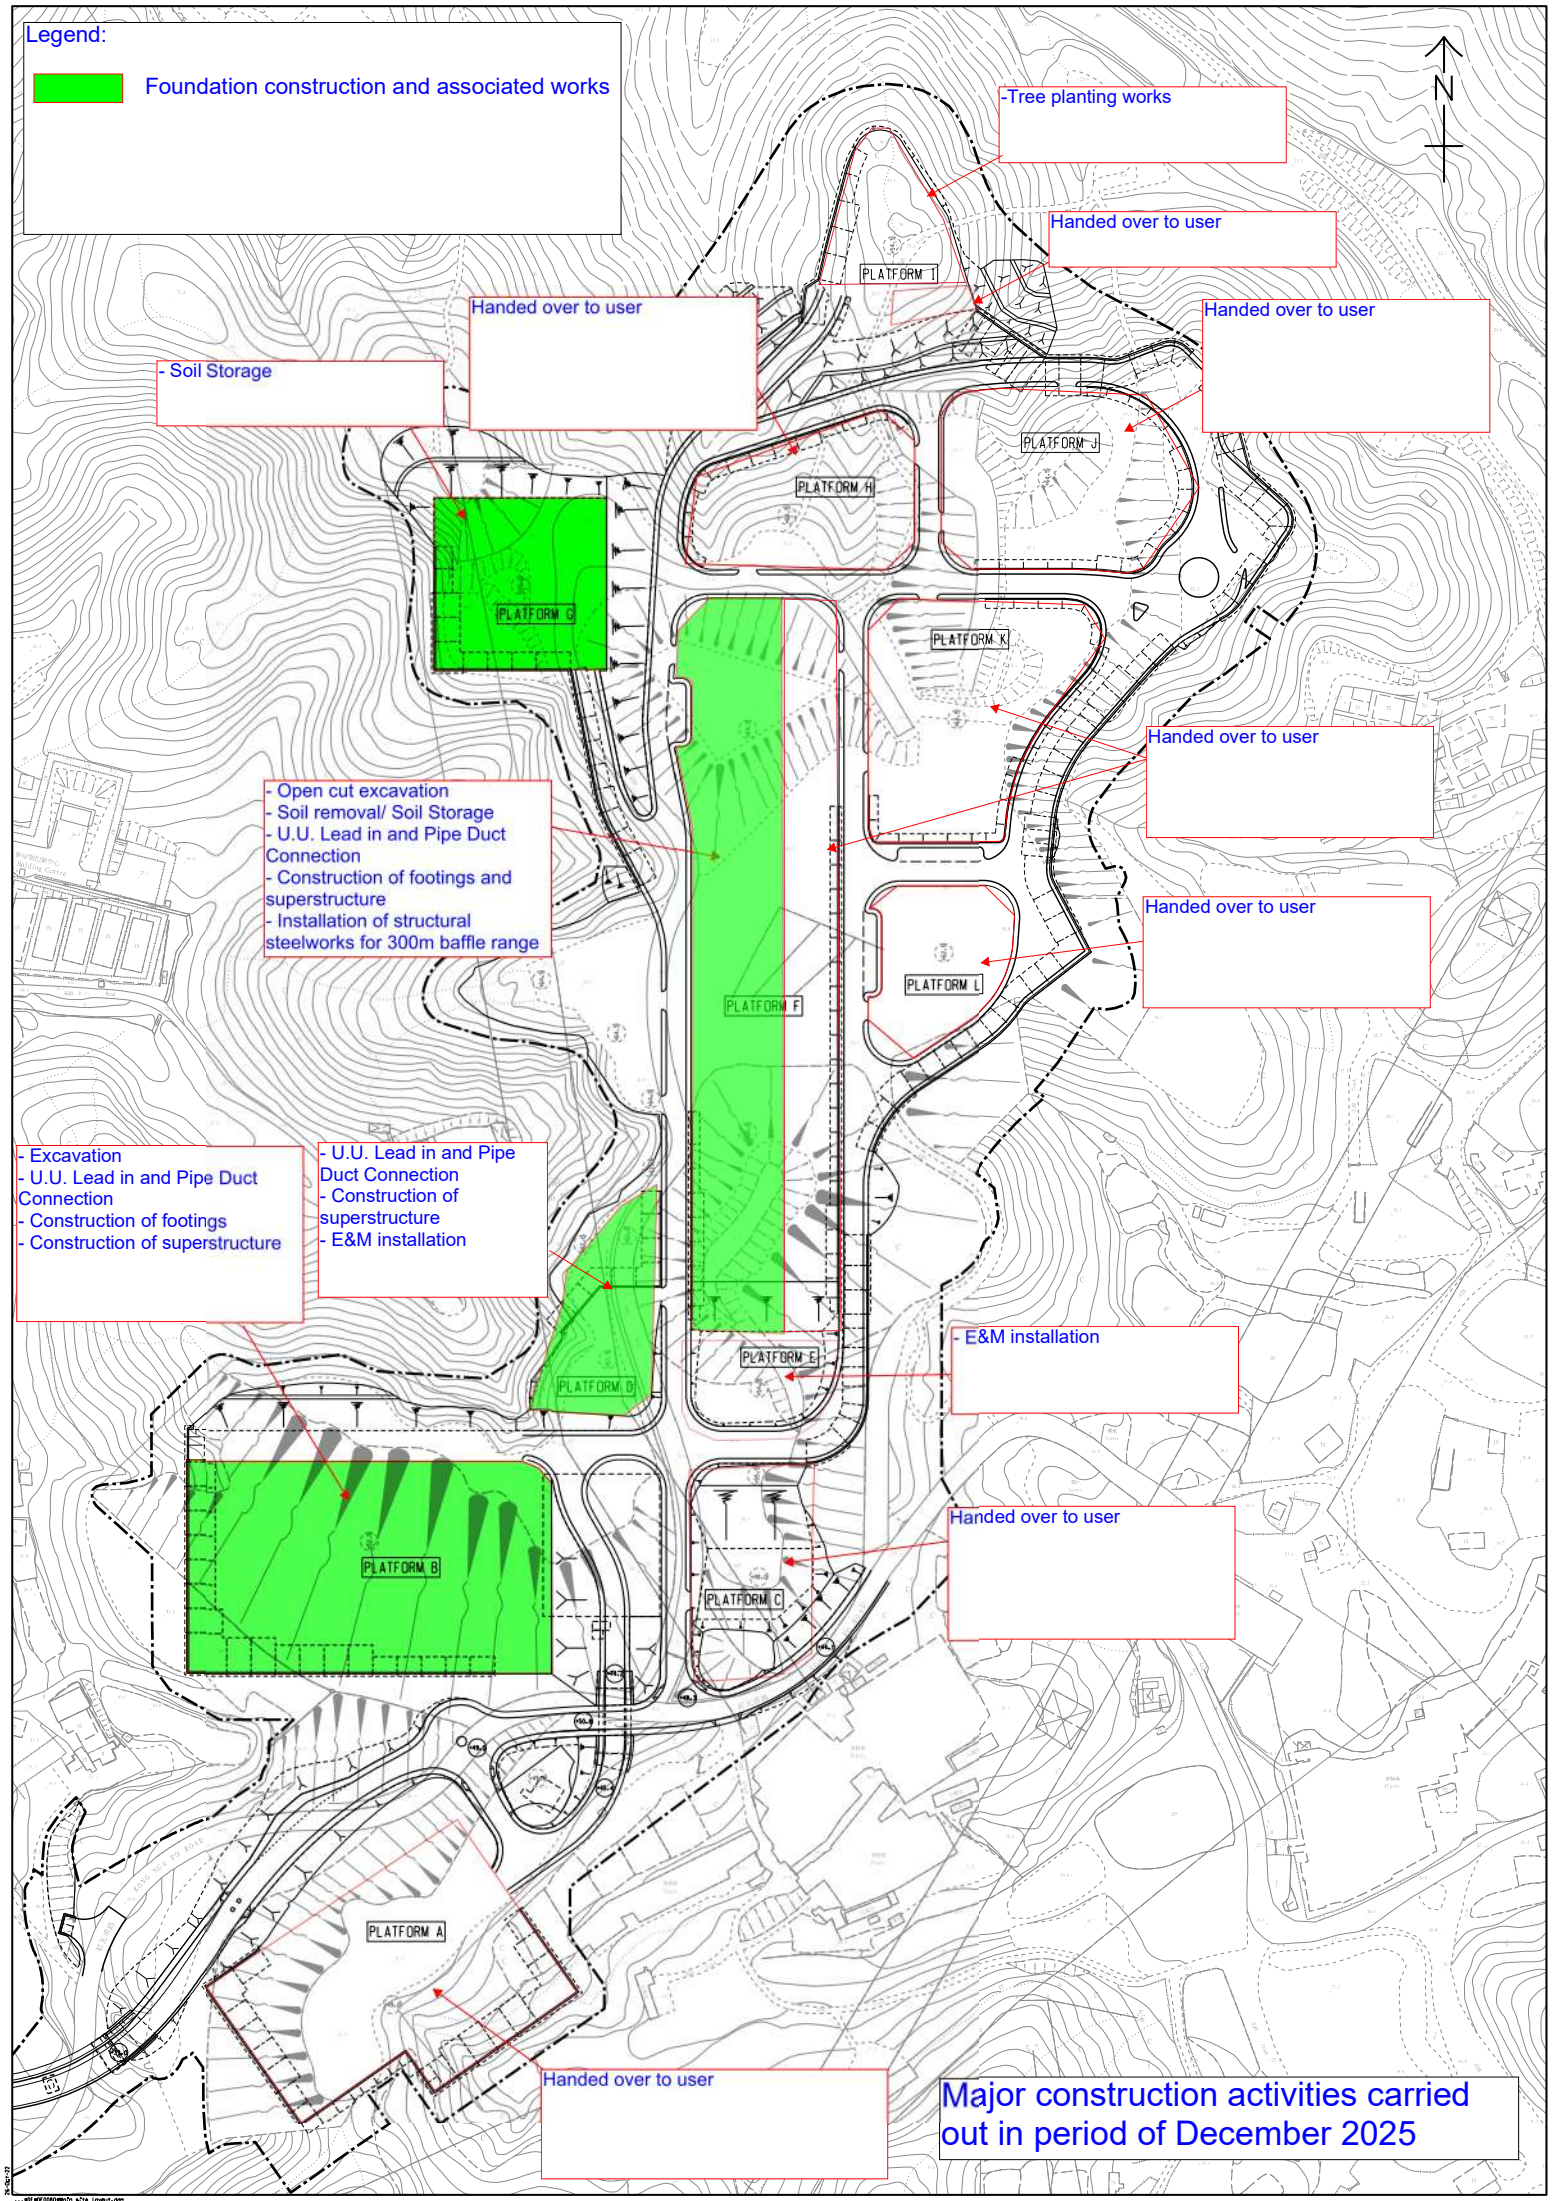


Major construction activities carried out in period of December 2025

Legend:



Foundation construction and associated works

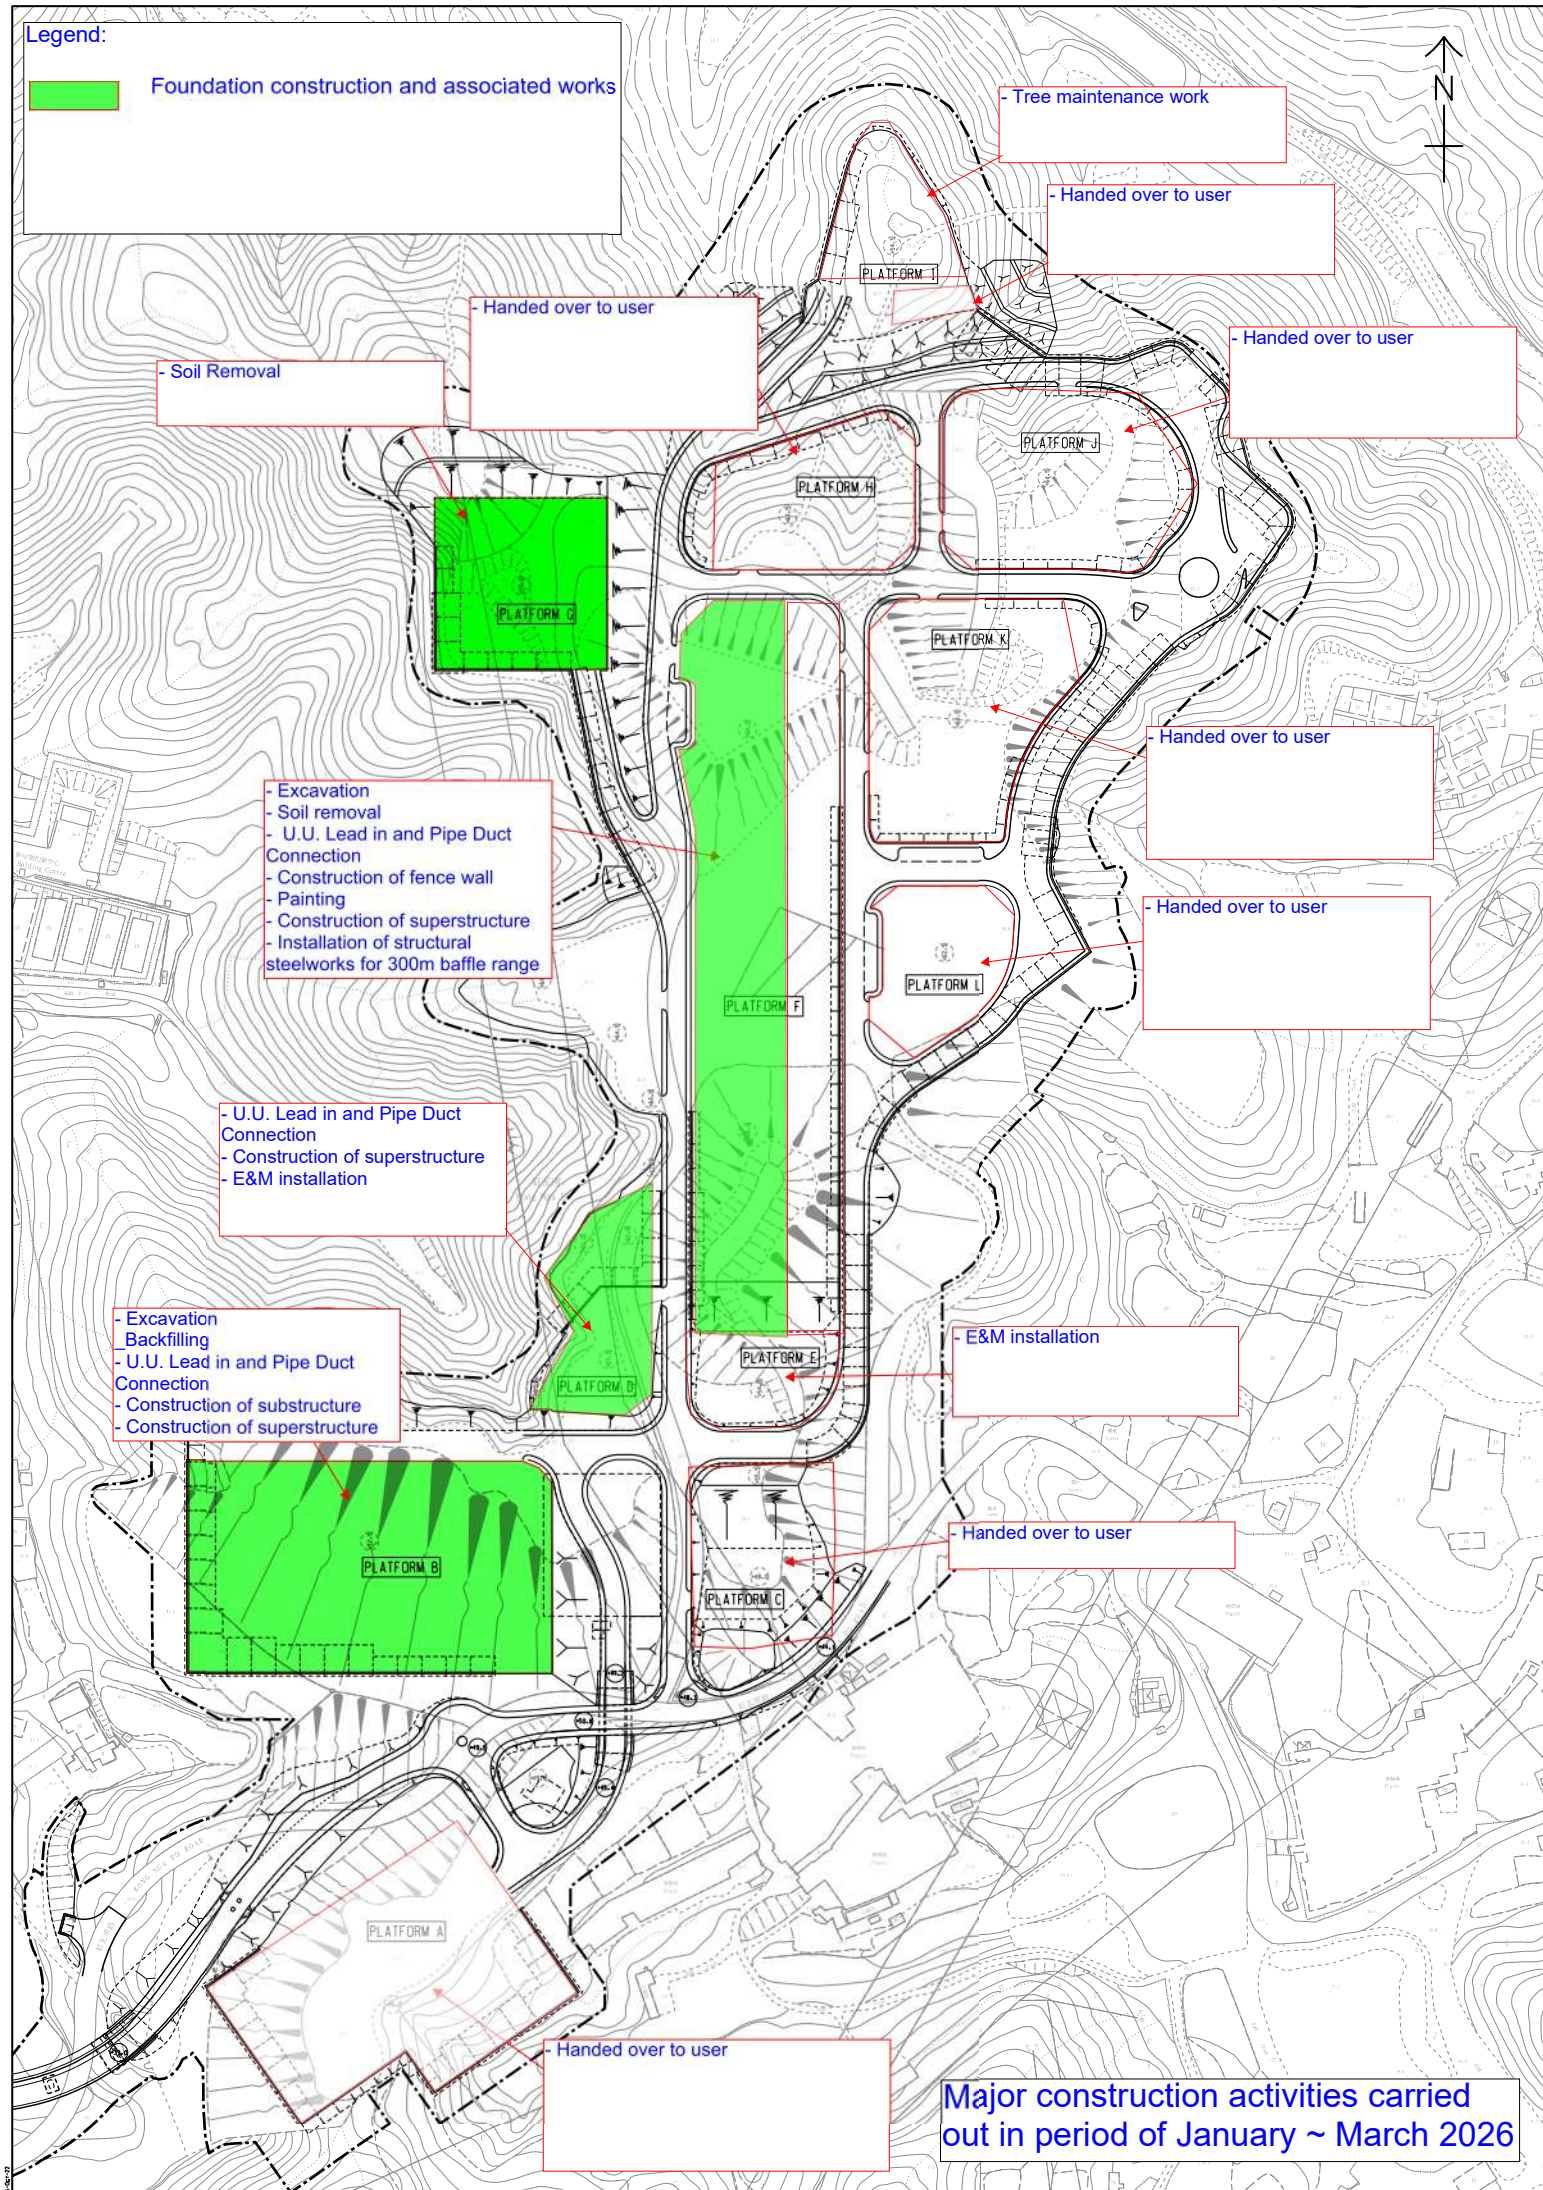

Major construction activities carried out in period of January ~ March 2026

Proactive Environmental Protection Proforma

Proactive Environmental Protection Proforma

Ref*	Proposed Construction Method	Location/Working Period	Anticipated Major Impacts	Recommended Mitigation Measures
EIA 3.9.1; EM&A Log 2.2	Open cut excavation	Kong Nga Po Site	Dust impact from excavation activities and earth moving	• Use of regular water spraying (once every 1.25 hours or 8 times per day) at all active works area exposed site surfaces and unpaved roads, particularly during dry weather • Deploy water bowser for regular water spraying to enhance dust suppression • Manual water spraying for dusty operation where inaccessible by water bowser • Speed control of site transportation • Stockpile of dusty materials will be covered by tarpaulin sheets to avoid wind-blown dust • Vehicles used for transporting dusty materials/spoils will be covered by mechanical cover before leaving the site • Wheel washing facilities will be provided and cleaning the wheel of all vehicles before leaving the site
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition

				• Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of construction materials to reduce the potential for water pollution • Provide wastewater treatment facilities prior to discharge of wastewater • Regular inspection and maintenance of wastewater treatment facilities • Wastewater pumped out of the excavation areas will be treated to remove suspended solids prior to discharge • Hard paving or well-compact of main haul road to minimize washout of soil • Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged.
EIA 7.5.1.1 &			Waste Generation	• Training of site personnel in proper waste management and

7.5.1.2; EM&A Log 6.2				chemical handling procedures • Proper storage and sorting of excavated inert materials to maximize on site reuse for backfilling • Surplus inert C&D materials will be disposed of at designated Government's PFRF.
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Chemical waste should be stored at chemical waste container and collected by a licensed collector to transport and dispose of at the approved Chemical Waste Treatment Centre • Drip tray and chemical spillage kit will be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to frontline workers for the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Restrict construction area to minimize the impact on existing retained trees
EIA 3.9.1; EM&A Log 2.2	Soil Removal	Kong Nga Po Site	Dust impact from excavation activities and earth	• Use of regular water spraying (once every 1.25 hours or 8 times per day) at all active works area exposed site surfaces and unpaved roads, particularly during dry weather

			moving	• Water spraying during loading and unloading of excavated materials • Vehicles used for transporting dusty materials/spoils will be covered by mechanical cover before leaving the site • Deploy water bowser for regular water spraying to enhance dust suppression • Speed control of site transportation • Stockpile of dusty materials will be covered by tarpaulin sheets to avoid wind-blown dust • Wheel washing facilities will be provided and cleaning the wheel of all vehicles before leaving the site
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition • Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of excavated materials to reduce the potential for water pollution

				• Provide wastewater treatment facilities prior to discharge of wastewater • Regular inspection and maintenance of wastewater treatment facilities • Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged.
EIA 7.5.1.1 & 7.5.1.2; EM&A Log 6.2			Waste Generation	• Training of site personnel in proper waste management and chemical handling procedures • Proper storage and sorting of excavated inert materials to maximize on site reuse for backfilling • Surplus inert C&D materials will be disposed of at designated Government's PFRF.
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Chemical waste should be stored at chemical waste container and collected by a licensed collector to transport and dispose of at the approved Chemical Waste Treatment Centre • Drip tray and chemical spillage kit will be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to frontline workers for the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative

				species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Restrict construction area to minimize the impact on existing retained trees
EIA 3.9.1; EM&A Log 2.2	Construction of footings	Kong Nga Po Site	Air	• Regular inspection and maintenance of plant and equipment in good condition • Regularly clean up stockpiles and debris to avoid accumulation of materials • Dusty materials exceeding 20 bags shall be stored in area sheltered on top and the three sides or covered entirely by impervious sheeting.
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition • Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out

EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	- Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged. - Designated location for residual concrete washout - Provide wastewater treatment facilities prior to discharge of wastewater
EIA 7.5.1.4; EM&A Log			Chemical Waste	Drip tray and chemical spillage kit shall be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	- Provide training to frontline workers for the conservative species - Provision of protective fence for the conservative species - Regular inspection for concerned vegetation and conservative species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	- Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement - Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts
EIA 3.9.1; EM&A Log 2.2	Construction of substructure and	Kong Nga Po Site	Air	- Regular inspection and maintenance of plant and equipment in good condition - Regularly clean up stockpiles and debris to avoid

	superstructure			accumulation of materials Dusty materials exceeding 20 bags shall be stored in area sheltered on top and the three sides or covered entirely by impervious sheeting.
EIA 4.4.6; EM&A Log 3.2			Noise Control	- Regular inspection and maintenance of plant & equipment in good condition - Enclose the noisy part of machineries with noise enclosure - Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	- Valid construction noise permit should be obtained and displayed on site - In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	- Cover the stockpiles of construction materials to reduce the potential for water pollution - Provide wastewater treatment facilities prior to discharge of wastewater - Wastewater generated from surface runoff shall be treated prior to discharge - Manholes should be temporarily sealed to prevent silt, construction materials or debris from entering the drainage system.

EIA 7.5.1.1; EM&A Log 6.2			Waste Management	- Cover stockpiles of C&D materials by impervious sheets to avoid wind-blown dust. - Spray water on all dusty materials including C&D materials immediately prior to any loading transfer operation - Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	Drip tray and chemical spillage kit shall be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	- Provide training to frontline workers for the conservative species - Provision of protective fence for the conservative species - Regular inspection for concerned vegetation and conservative species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	- Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement - Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts
EIA 3.9.1; EM&A Log 2.2	Backfilling	Kong Nga Po Site	Air	Deploy water bowser for regular water spraying to enhance dust suppression

				• Manual water spraying for dusty operation where inaccessible by water bowser • Speed control of site transportation • Stockpile of dusty materials will be covered by tarpaulin sheets to avoid wind-blown dust • Vehicles used for transporting dusty materials/spoils will be covered by mechanical cover before leaving the site • Wheel washing facilities will be provided and cleaning the wheel of all vehicles before leaving the site
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition • Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of construction materials to reduce the potential for water pollution • Provide wastewater treatment facilities prior to discharge of wastewater

				- Regular inspection and maintenance of wastewater treatment facilities - Wastewater pumped out of the excavation areas will be treated to remove suspended solids prior to discharge - Hard paving or well-compact of main haul road to minimize washout of soil - Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged.
EIA 7.5.1.1 & 7.5.1.2; EM&A Log 6.2			Waste Generation	- Training of site personnel in proper waste management and chemical handling procedures - Proper storage and sorting of excavated inert materials to maximize on site reuse for backfilling - Surplus inert C&D materials will be disposed of at designated Government's PFRF or reuse at other contracts.
EIA 3.9.1; EM&A Log 2.2	Installation of structural Steelworks for 300m baffle range	Kong Nga Po Site	Air	- Regular inspection and maintenance of plant and equipment in good condition - Water spraying at exposed areas - Regularly clean up stockpiles and debris to avoid accumulation of materials
EIA 4.4.6;			Noise Control	Regular inspection and maintenance of plant & equipment in

EM&A Log 3.2				good condition • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of construction materials to reduce the potential for water pollution • Provide wastewater treatment facilities prior to discharge of wastewater • Wastewater generated from surface runoff shall be treated prior to discharge
EIA 7.5.1.1; EM&A Log 6.2			Waste Management	• Cover stockpiles of C&D materials by impervious sheets to avoid wind-blown dust. • Spray water on all dusty materials including C&D materials immediately prior to any loading transfer operation • Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Drip tray and chemical spillage kit shall be provided on site

EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts
------------------------------------	--	--	--------------------------------	---

**EIA Ref/ EM&A Log/ Design Document Ref*

***Details of equipment, vehicles, plants, processes, technologies for the construction method*

Design and Construction of Kong Nga Po Police Training Facilities
Proactive Environmental Protection Proforma

Working Period: December 2025

Ref*	Proposed Construction Method	Location/Working Period	Anticipated Major Impacts	Recommended Mitigation Measures	Photo Records (Partial)
EIA 3.9.1; EM&A Log 2.2	Open cut excavation	Kong Nga Po Site	Dust impact	- Manual water spraying for dust suppression - Regular inspection and maintenance of plant and equipment in good condition - Cover stockpile with impervious sheets or grout - Provide wheel washing facility at site entrance	 By subcontractor at KNP site

					 By subcontractor at KNP site  By subcontractor at KNP site
--	--	--	--	--	---

EIA 4.4.6; EM&A Log 3.2			Noise	• Regular inspection and maintenance of plant & equipment in good condition • Deploy Quality Powered Mechanical Equipment (QPME) if possible • Valid construction noise permit should be displayed at site entrance.	 By main contractor at KNP site  By main contractor at KNP site
--	--	--	--------------	--	--

EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to workers about the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative species	 By main contractor at KNP site  By subcontractor at KNP site
---------------------------------------	--	--	------------------------	--	---

EIA 3.9.1; EM&A Log 2.2	Soil Removal	Kong Nga Po Site	Air	• Deploy water bowser for regular water spraying to enhance dust suppression • Cover dusty materials with impervious sheets • Exposed slopes covered with waterproof layers such as tarpaulin sheets or grout to reduce the potential for sediment laden runoff entering the drainage system. • The speed of the trucks within the site should be controlled to about 10km/hour in order to reduce adverse dust impacts and secure the safe movement around the site.	 By main contractor at KNP site  By main contractor at KNP site
--	---------------------	-------------------------	------------	--	---

EIA 4.4.6; EM&A Log 3.2			Noise	- Regular inspection and maintenance of plant & equipment in good condition - Deploy Quality Powered Mechanical Equipment (QPME) if possible	 By main contractor at KNP site
EIA 5.6.1.2 and EM&A Log 4.2			Water Quality	- Cover exposed slopes with impervious sheets or cement grout. - Wastewater pumped out of the excavation areas shall be treated to remove suspended solid prior to discharge. - Provide desilting/ sedimentation devices for wastewater treatment prior to discharge.	 By main contractor at KNP site

				Provide drip tray to prevent spillage of fuels	 By main contractor at KNP site
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	- Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement - Implement temporary traffic arrangement which control construction area to	 By main contractor at KNP site

				minimize landscape and visual impacts • Minimize visual impact during construction stage. Site office not visually prominent from public room and surrounding • Planting will take place as soon the planting area is installed with subsoil drainage • Decorative hoarding is provided	
EIA 3.9.1; EM&A Log 2.2	Construction of footings, substructure and superstructure	Kong Nga Po Site	Air	• Cover dusty materials with impervious sheets • Exposed slopes covered with waterproof layers such as tarpaulin sheets or grout to reduce the potential for sediment laden runoff entering	

				the drainage system. Provide wheel washing facility at site entrance	By subcontractor at KNP site  15.12.2025 By subcontractor at KNP site
EIA 4.4.6; EM&A Log 3.2			Noise	Valid construction noise permit should be obtained and displayed on site	 15.12.2025 By main contractor at KNP site

EIA 5.6.1.3 and EM&A Log 4.2			Water Quality	• Surface water from concrete batching areas and the rest of the site should be separated as far as possible. • Temporary drainage is free of obstruction. • Gullies are sealed to prevent silt or debris from entering the drainage system.	By main contractor at KNP site By subcontractor at KNP site
---	--	--	----------------------	--	--

					 By main contractor at KNP site
EIA 7.5.1.2 and EM&A Log 6.2			Waste Management	• Segregation and storage of different types of waste in different containers or skips or stockpiles to enhance reuse or recycling of materials and their proper disposal • Sort non-inert C&D materials to recover any recyclable portions	 By main contractor at KNP site
