

Date: 13 August 2025

Your ref:

Our ref: PL-202508015

Architectural Services Department
40/F, Queensway Government offices
66 Queensway, Hong Kong

Attn: Mr. Vincent Kwok

Dear Mr. Kwok,

Re: Contract No. SS K/509

**Provision of Independent Environmental Checker Consultancy for Design
and Construction of Kong Nga Po Police Training Facilities
Verification of Monthly EM&A Report (July 2025)**

Reference is made to the monthly EM&A report (July 2025) provided by ET via email on 11 August 2025.

Please be informed that we have no adverse comments on the EM&A report (Version 1.0). We hereby verify the submission is in accordance with Condition 3.1 of Environmental Permit No. FEP-01/510/2016.

Thank you for your attention.

Yours sincerely,

For and on behalf of

Acuity Sustainability Consulting Limited



Ir Y.H. LAW

Independent Environmental Checker

c.c. Ka Shing Management Consultancy Ltd.

**Provision of Environmental Team consultancy
for Design and Construction of Kong Nga Po Police
Training Facilities (Programme No. 279LP)**

**Monthly Environmental Monitoring and
Audit Report for July 2025
(Version 1.0)**

Disclaimer

The information provided in this report is for presentation. All information in the report is provided in good faith, and every effort has been made for the information contained herein at the time of publication. However, our company disclaims all responsibilities and liabilities for incompleteness within this report.

Ka Shing Management Consultancy Ltd. www.ka-shign.net
Unit 2, 13/F Kai Yue Commercial Building, 2C Argyle St,
Mong Kok, Kowloon

Our ref: 11-8-2025

11-8-2025

By email: kwokhw@archsd.gov.hk

Architectural Services Department
40/F, High Block, Queensway Government Offices,
66 Queensway, Hong Kong
(Attn: Mr. Vincent Kwok)

Dear Mr. Kwok,

Re: Quotation No. PMB202/8480/2022/A01/A

**Provision of Environmental Team consultancy for Design and Construction of Kong Nga Po
Police Training Facilities (Programme no. 279LP)**

-Submission of the monthly EM&A report in July 2025

We refer to the Environmental Permit No. FEP-01/510/2016 for the captioned project.

Subject to the accuracy and authenticity of all the information provided to us, we hereby
certify, in accordance with Conditions 3.4 of Environmental Permit No. FEP-01/510/2016, that
the information is a representation of what it signifies.

Thank you very much for your attention and please feel free to contact Mr. Lee at 9382 4204
should you require further information.

Yours faithfully,

For and on behalf of
Ka Shing Management Consultant Limited



Mr. W. H. Lee

Environmental Team Leader

Table of Contents

	Page No.
EXECUTIVE SUMMARY	
Introduction	5
Environmental Monitoring and Audit Progress	5
Breaches of Action and Limit Levels	5
Construction Noise	5
Air Quality	6
Ecological Monitoring	6
Environmental Non-Compliance	6
Environmental Complaint	6
Notification of Summons and Successful Prosecutions	6
Reporting Changes	6
Future Key Issues	6-7
1 INTRODUCTION	
Purpose of the report	8
Structure of the report	8
2 PROJECT INFORMATION	
Background	9
Project Organization	9-10
Summary of Construction Works Undertaken During Reporting Month	10
Construction Programme	10
Status of Environmental Licences, Notifications and Permits	10-11
Summary of EM&A Requirement	11
Status of Compliance with Environmental Permits Conditions	11-12
3 NOISE MONITORING	
Monitoring Requirements	13
Monitoring Location	13
Monitoring Equipment	13-14
Monitoring Parameters, Frequency and Duration	14
Monitoring Methodology and QA/QC Procedures	14-15
Maintenance and Calibration	15
Results and Observations	15-16
Event and Action Plan	16
4 AIR QUALITY MONITORING	
Monitoring Requirements	17
Monitoring Location	17
Monitoring Equipment	17-18
Monitoring Parameters, Frequency and Duration	18
Monitoring Methodology and QA/QC Procedure	18-19
Results and Observations	19-20
Event and Action Plan	20
5 LANDSCAPE AND VISUAL MONITORING	
Monitoring Requirements	21

6	ECOLOGICAL MONITORING	
	Monitoring of Flora Species of Conservation Interest	22
	Post-Transplantation Monitoring and Maintenance Programme	22-23
	Results and Observations	23-24
	Precautionary Measure for Butterfly Species of Conservation Interest	24
	Precautionary Measures to Minimize Indirect Disturbance on Ecology	24
7	ENVIRONMENTAL SITE INSPECTION	
	Site Audits	25-26
	Implementation Status of Environmental Mitigation Measures	26
	Solid and Liquid Waste Management Status	26-27
8	ENVIRONMENTAL NON-CONFORMANCE	
	Summary of Exceedances	28
	Summary of Environmental Non-Compliance	28
	Summary of Environmental Complaint	28
	Summary of Environmental Summon and Successful Prosecution	28
9	FUTURE KEY ISSUES	
	Key Issues in the Coming Three Months	29-30
	Monitoring Schedule for the Next Month	30
10	CONCLUSIONS AND RECOMMENDATIONS	
	Conclusions	31
	Recommendations	31-32

LIST OF TABLES

Table I	Summary Table for EM&A Activities in the Reporting Month
Table II	Summary Table for Events Recorded in the Reporting Month
Table 2.1	Key Contacts of the Project
Table 2.2	Status of Environmental Licences, Notifications and Permits (Contract No. SSK509)
Table 2.3	Summary Table for Status of Compliance / Required Submission
Table 3.1	Location for Noise Monitoring Stations
Table 3.2	Noise Monitoring Equipment
Table 3.3	Noise Monitoring Parameters, Duration and Frequency
Table 3.4	Summary Table of Noise Monitoring Results during the Reporting Month
Table 3.5	Observation at Noise Monitoring Stations
Table 4.1	Location for Air Quality Monitoring Locations
Table 4.2	Air Quality Monitoring Equipment
Table 4.3	Impact Dust Monitoring Parameters, Frequency and Duration
Table 4.4	Summary Table of 1-hour TSP Monitoring Results during the Reporting Month
Table 4.5	Observation at Dust Monitoring Stations
Table 5.1	Observations and Recommendations of Site Audit

LIST OF FIGURES

Figure 1	Site Layout Plan
Figure 2	Location of Air Quality Monitoring Stations
Figure 3	Location of Noise Monitoring Stations

LIST OF APPENDICES

Appendix A	Construction Programme and Proactive Environmental Protection Proforma
Appendix B	Action and Limit Levels
Appendix C	Copies of Calibration Certificates
Appendix D	Environmental Monitoring Schedules
Appendix E	Air Quality Monitoring Results and Graphical Presentation
Appendix F	Noise Monitoring Results and Graphical Presentation
Appendix G	Weather Condition
Appendix H	Ecological Monitoring Records
Appendix I	Event Action Plans
Appendix J	Summary of Exceedance
Appendix K	Environmental Mitigation Implementation Schedule (EMIS)
Appendix L	Waste Generation in the Reporting Month
Appendix M	Complaint Log
Appendix N	Summary of Successful Prosecution
Appendix O	The potential seriousness of the forthcoming environmental impacts and the use of machineries
Appendix P	A List of Machineries Used in Construction Site
Appendix Q	Wastewater Discharge Layout Plan

EXECUTIVE SUMMARY

Introduction

- E1. This document represents the 28th monthly report detailing the Environmental Monitoring and Audit (EM&A) activities for the Kong Nga Po Police Facilities Project, which operates under Environmental Permit No. FEP-01/510/2016. This report was prepared by Ka Shing Management Consultancy Ltd. (Ka Shing) under “Service Contract Quotation No. PMB202/8480/2022/A01/A Provision of Environmental Team consultancy for Design and Construction of Kong Nga Po Police Training Facilities” (hereinafter called the “Service Contract”). The report encapsulates the EM&A activities and findings carried out between the 1st and 31st of July 2025.
- E2. On the 23rd of December 2022, a section of the construction site was transferred to the Architectural Services Department (ArchSD), which assumed responsibility for the building's construction. Furthermore, ArchSD has taken on the role of maintenance agent for the Hong Kong Police Force (HKPF) throughout the operational phase.
- E3. In the month covered by this report, the Project of Police Facilities at Kong Nga Po, which operates under Environmental Permit No. FEP-01/510/2016, engaged in the following contractual work: Contract No. SSK509, which encompasses the design and construction of the Kong Nga Po Police Training Facilities.

Environmental Monitoring and Audit Progress

- E4. A summary of the EM&A activities in this reporting month is listed in **Table I** below:

Table I Summary Table for EM&A Activities in the Reporting Month

EM&A Activities	Date
Noise Monitoring	11, 17, 23, 29 July 2025
Air Quality Monitoring	05, 11, 17, 23, 29 July 2025
Environmental Site Inspection	11, 17, 23, 29 July 2025
Ecological Monitoring	23, 28 July 2025
Landscape & Visual Inspection	11, 17, 23, 29 July 2025

Breaches of Action and Limit Levels

- E5. Summary of the environmental exceedances of the reporting month is tabulated in **Table II**.

Construction Noise

- E6. During the reporting month, the planned noise monitoring for construction took place as scheduled, with no recorded incidents of the Action/Limit Levels being exceeded.

Air Quality

E7. Throughout the reporting period, all planned air quality monitoring associated with construction was executed, and there were no recorded instances where the Action/Limit Levels were surpassed.

Table II Summary Table for Events Recorded in the Reporting Month

Environmental Monitoring	Parameter	No. of Non-Project related Exceedances		No. of Exceedance related to the Construction Works of the Contract		Action Taken
		Action Level	Limit Level	Action Level	Limit Level	
Noise	$L_{eq}(30min)$	0	0	0	0	N/A
Air Quality	1-hr TSP	0	0	0	0	N/A

Ecological Monitoring

E8. The ecological monitoring slated for the reporting month was conducted according to schedule. Details of the findings from this ecological monitoring for the respective period are available in **Appendix H**.

Environmental Non-Compliance

E9. During the reporting month, no environmental compliance violations were documented.

Environmental Complaint

E10. No environmental complaints were recorded during the reporting period. In the event of any complaints, they would be documented in the Complaint Log found in **Appendix M**.

Notification of Summons and Successful Prosecutions

E11. Throughout the month covered in this report, there were no instances of receiving notifications regarding summons or confirmations of successful prosecutions.

Reporting Changes

E12. On the 23rd of December 2022, a section of the construction site was handed over to the Architectural Services Department (ArchSD). ArchSD has taken on the task of overseeing the construction activities for the building. This Monthly Environmental Monitoring and Audit (EM&A) Report offers a summary of the site operations and the status of the environmental safeguards being implemented under the contract with ArchSD.

Future Key Issues

E13. The major site activities for the coming three months include:

1. Open cut excavation
2. Removal of soil

3. Construction of footings
4. Construction of substructure and superstructure
5. Construction of footbridge
6. Construction of fence wall and boundary wall
7. Installation of structural steelworks for 300m baffle range
8. Backfilling
9. U.U. Lead in and Pipe Duct Connection

E14. The aforementioned construction activities could potentially lead to environmental impacts, with the primary concerns centered around construction dust, noise, water quality, and waste management. For detailed information, please refer to **Appendix A** regarding the anticipated major impacts from the construction works and corresponding recommended mitigation measures.

1 INTRODUCTION

1.1 The Architectural Services Department (ASD) has commissioned Ka Shing Management Consultancy Ltd. (Ka Shing) as the Environmental Team (ET) to conduct the Environmental Monitoring and Audit (EM&A) activities for the Kong Nga Po Police Facilities Project, as dictated by Environmental Permit No. FEP-01/510/2016.

1.2 The main construction activities for the Project began on the 3rd of July, 2020, and the primary location at Kong Nga Po was handed over to the Architectural Services Department (ASD) on the 23rd of December, 2022. The ASD has assumed control over the building construction tasks and will serve as the maintenance representative for the Hong Kong Police Force (HKPF) once the project is operational.

Purpose of the report

1.3 This document constitutes the 28th EM&A Report, offering a consolidated overview of the monitoring outcomes for impacts and the audit results from the EM&A program over the reporting interval spanning from the 1st and 31st of July 2025.

Structure of the report

1.4 The structure of the report is as follows:

- Section 1: Introduction
- Section 2: Project Information
- Section 3: Noise Monitoring
- Section 4: Air Quality Monitoring
- Section 5: Landscape and Visual Monitoring
- Section 6: Ecological Monitoring
- Section 7: Environmental Site Inspection.
- Section 8: Environmental Non-conformance
- Section 9: Future Key Issues
- Section 10: Conclusions and Recommendations

2 PROJECT INFORMATION

Background

- 2.1 The Project mainly includes construction and operation of various police facilities. The police facilities include:
- (i) a helipad;
 - (ii) two firing ranges; and
 - (iii) other facilities, associated infrastructure & utilities, etc.
- 2.2 The Project falls under the category of a Designated Project as defined by the Environmental Impact Assessment Ordinance (EIAO). In October 2016, an Environmental Impact Assessment (EIA) Report (Report No.: AEIAR-201/2016) was approved for the Project in accordance with the EIA Study Brief (No. ESB-276/2014) and the Technical Memorandum on Environmental Impact Assessment Process (EIAO-TM). The corresponding Environmental Permit (EP no.: FEP-01/510/2016) was issued by the Director of Environmental Protection (DEP).
- 2.3 As per the approved Environmental Monitoring and Audit (EM&A) Manual, a comprehensive air quality and noise monitoring program is recommended during the construction phases of the Project to assess and monitor potential dust and noise nuisances. Prior to the commencement of the Project's construction works, baseline air quality and noise monitoring were conducted by the previous Environmental Team (Wellab Limited) from 14th March, 2020, to 2nd April, 2020, to establish the pre-existing conditions at designated sensitive receivers.
- 2.4 **Figure 1** displays the site layout plan for the Project.

Project Organization

- 2.5 Various stakeholders with varying degrees of participation are part of the Project's organizational structure under Environmental Permit number: FEP-01/510/2016, which includes:
- Project Proponent – Architectural Services Department (ArchSD)
 - Contractor– China State JV
 - Environmental Team (ET) – Ka Shing Management Consultancy Ltd.
 - Independent Environmental Checker (IEC) – Acuity Sustainability Consulting Limited
- 2.6 **Table 2.1** summarizes the contact information for key personnel associated with Quotation No. PMB202/8480/2022/A01/A and additional contacts linked with the ArchSD Contract No. SSK509.

Table 2.1 Key Contacts of the Project

Party	Role	Contact Person	Phone No.	Fax No.
Architectural Services Department	Project Proponent	Mr. Vincent Kwok	2867 3939	3542 5223

Contractor (China State JV)	Site Agent	Mr. Kelvin Chan	6272 8828	2866 6325
	Environmental Officer	Ms. Marian Kong	6174 9735	
		Mr. LuLu Mar	5998 8852	
Ka Shing Management Consultancy Ltd.	ETL	Mr. W.H. Lee	2618 2166	2120 7752
Acuity Sustainability Consulting Limited	IEC	Ir. Y.H. Law	2698 6833	2698 9383

Summary of Construction Works Undertaken During Reporting Month

2.7 Significant site activities conducted on-site during the reporting month comprised:

1. Open cut excavation
2. Removal of soil
3. Construction of footings
4. Construction of substructure and superstructure
5. Construction of footbridge
6. Construction of fence wall and boundary wall
7. Backfilling
8. U.U. Lead in and Pipe Duct Connection

Construction Programme

2.8 **Appendix A** contains a version of the Contractors' construction schedules. The primary site activities planned by the Contractor for the upcoming three months have been examined. In **Appendix O**, the expected environmental impacts' potential severity and the deployment of equipment have been evaluated. This appendix additionally provides the Contractor with recommendations and insights on alternative approaches aimed at raising environmental consciousness, refining practices on the construction site, and fostering environmental improvements.

2.9 **Table 2.2** presents a consolidated overview of the pertinent environmental protection permits, licenses, and/or notifications associated with this Project.

Table 2.2 Status of Environmental Licences, Notifications and Permits

Permit / Licence No.	Valid Period		Status
	From	To	
Further Environmental Permit (FEP)			
FEP-01/510/2016	N/A	N/A	Valid
Construction Noise Permit (CNP)			
GW-RN0450-25 (Renewal)	10-05-2025	09-08-2025	Valid
Notification pursuant to Air Pollution Control (Construction Dust) Regulation			
EPD Ref no.: 487864	N/A	N/A	N/A

Billing Account for Construction Waste Disposal			
Account No. 7046289	18-01-2023	N/A	Valid
Registration of Chemical Waste Producer			
WPN5213-641-C4770-01	18-01-2023	N/A	Valid
Effluent Discharge Licence under Water Pollution Control Ordinance			
WT00043663-2023	21-04-2023	30-04-2028	Valid

Summary of EM&A Requirement

2.10 The Environmental Monitoring and Audit (EM&A) program includes the monitoring of construction noise, air quality, ecological conditions, and regular environmental site audits. The specific requirements for the EM&A program are outlined in the following sections:

- Environmental requirements in contract documents;
- Event / Action Plans;
- Environmental mitigation measures, as recommended in the Project EIA study final report;
- All monitoring parameters; and
- Action and Limit levels for all environmental parameters.

Status of Compliance with Environmental Permits Conditions

2.11 **Table 2.3** provides a summary of the adherence to Environmental Permit (EP) No. FEP-01/510/2016 and the necessary submissions connected to this Project as stipulated by the EP.

Table 2.3 Summary Table for Status of Compliance / Required Submission under FEP No. FEP-01/510/2016

FEP Conditions	Submission	Submission Date	Approval Status
1.12	Commencement date of construction of the Project	30/3/2023	*
2.7	Proposal on the Reporting Mechanism and Curriculum Vitae of the IEC	20/3/2023	*
2.10	The date of setting up the Community Liaison Hotline and the contact details	27/2/2023	*
2.11	Management Organization of Main Construction Companies, at least an organization chart, names of responsible persons and their contact details	10/3/2023	*
2.12	Construction Works Schedule and Location Plans	10/3/2023	*
2.13	Layout plan for permeable pavings.	Submitted to EPD on 29/3/2023. Supplementary information submitted to EPD on 23/3/2024.	For approval
2.14	Landscape and visual mitigation plan	Submitted to EPD on 24/3/2025.	For approval

2.16	Plan for perimeter walls/ boundary wall sat project site and sidewalls of firing range	6/12/2024 Supplementary information submitted to EPD by email on 2/5/2025.	For approval
2.19	Submission of Helicopter Flight Plan	1 month before commencement of operation of Helipad	Notification
3.3	Baseline Air Quality and Noise Monitoring Report	30/3/2023	Deposit
4.2	Internet address of a dedicated web site	13/4/2023	*

Remarks: * Approval not required in FEP-01/510/2016

3 NOISE MONITORING

Monitoring Requirements

- 3.1 Following the EM&A Manual, monitoring of construction noise was performed by measuring the A-weighted equivalent continuous sound pressure level (Leq) to track noise generated by construction operations. Each monitoring station is scheduled for weekly noise assessments, with one set of readings to be taken from 0700 to 1900 hours on typical weekdays. The predefined Action/Limit Levels for the environmental monitoring activities are presented in **Appendix B**.

Monitoring Location

- 3.2 As per Section 3.2.3 of the EM&A Manual, impact noise monitoring took place at fourteen specified noise monitoring stations. Following the guidelines of the Project's Environmental Impact Assessment (EIA) report, noise monitoring stations situated within a 300-meter radius of the Project's boundary were taken into account. Consequently, six noise monitoring stations identified as relevant monitoring locations are depicted in Figure 3. The specific locations of these noise monitoring stations are detailed in **Table 3.1**.

Table 3.1 Location of Noise Monitoring Stations

Monitoring Station	Location of Measurement
NM9	Village House, Kong Nga Po
NM10	Village House, Kong Nga Po
NM11	Village House, Kong Nga Po
NM12	Village House, Kong Nga Po
NM13	Village House, Kong Nga Po
NM14	Village House, near Man Kam To Road

Monitoring Equipment

- 3.3 Impact noise monitoring was carried out using Integrating Sound Level Meters. These meters, classified as Type 1, are capable of providing continuous readings of noise levels, including the equivalent continuous sound pressure level (Leq) and percentile sound pressure level (Lx), and they conform to the specifications of International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). The noise monitoring equipment utilized is summarized in **Table 3.2**. The calibration certificates for these devices can be found in **Appendix C**.

Table 3.2 Noise Monitoring Equipment

Equipment	Model	Quantity
Sound Level Meter	BSWA 308	5
Sound Level Meter	Rion NL53	1
Sound Calibrator	SoundTEK ST-120	1

Monitoring Parameters, Frequency and Duration

3.4 Table 3.3 encapsulates the variables monitored, the frequency of monitoring, and the total time span of the noise monitoring activities. The schedule for noise monitoring can be located in **Appendix D**.

Table 3.3 Noise Monitoring Parameters, Duration and Frequency

Monitoring Stations	Parameter	Duration	Frequency	Measurement
NM9	L10(30 min.) dB(A) ^[2]	0700-1900 hrs on normal weekdays	Once per week	Free field ^[1]
NM10				Free field ^[1]
NM11	L90(30 min.) dB(A) ^[2]			Façade
NM12				Façade
NM13	Leq(30 min.) dB(A) ^[2]			Free field ^[1]
NM14				(as six consecutive Leq, 5min readings)

Remarks:

[1]: Correction of +3dB (A) for Free-field Measurement.

[2]: A-weighted equivalent continuous sound pressure level (Leq). It is the constant noise level which, under a given situation and time period, contains the same acoustic energy as the actual time-varying noise level.

L10 is the level exceeded for 10% of the time. For 10% of the time, the sound or noise has a sound pressure level above L10.

L90 is the level exceeded for 90% of the time. For 90% of the time, the noise level is above this level.

Monitoring Methodology and QA/QC Procedures

3.5 The procedures for noise monitoring were conducted in this manner:

- The sound level meter was mounted on a tripod, positioned 1 meter away from the outside of the noise-sensitive facade and at a height of 1.2 meters above ground level;
- To achieve free field measurement conditions, the meter was placed at a distance from any reflective surfaces, and the measured noise levels were then corrected by adding +3 dB(A);
- The battery's condition was examined to guarantee the proper operation of the meter;
- The settings for parameters like frequency weighting, time weighting, and measurement duration were established as detailed below:
 - frequency weighting: A
 - time weighting: Fast

-time measurement: Leq(30 min.) dB(A)

- Noise levels were measured as six consecutive Leq, 5-minute readings during the hours when restrictions did not apply (specifically, from 0700 to 1900 hrs on normal weekdays).
- Calibration of the meter was performed before and after each noise measurement session using a Calibrator set to 94.0 dB at 1000 Hz. Should there be a discrepancy greater than 1.0 dB in calibration levels pre- and post-measurement, the data would be deemed invalid. A repeat measurement would then be necessary following recalibration or repair of the equipment.
- Throughout the monitoring period, parameters such as Leq, L90, and L10 were documented. Observations regarding site conditions and noise origins were also noted on a standard recording form.
- Noise measurements were temporarily halted during instances of significant intrusive noise (for example, barking dogs or helicopter sounds), where feasible. An observation record for the measurement period was to be provided.
- Noise monitoring was suspended in conditions of fog, rain, or when wind speeds were consistently above 5 m/s, or during gusts surpassing 10 m/s. Wind speeds were verified using a portable anemometer capable of measuring speed in meters per second (m/s).

Maintenance and Calibration

- 3.6 Every three months, the microphone head of the sound level meter and the calibrator was gently wiped clean using a soft fabric.
- 3.7 Annually the sound level meter and calibrator underwent inspection and calibration.
- 3.8 Before and after conducting each noise measurement, the precision of the sound level meter must be verified with an acoustic calibrator that produces a set sound pressure level at a specific frequency. Only when the pre- and post-measurement calibration levels are within a 1.0 dB range of each other will the measurements be considered valid.

Results and Observations

- 3.9 **Table 3.4** provides a summary of the noise monitoring outcomes. For an in-depth account and visual depiction of the noise monitoring, refer to **Appendix F**. A summary of the meteorological data for the reporting period is compiled in **Appendix G**.

Table 3.4 Summary Table of Noise Monitoring Results during the Reporting Month

Monitoring Station	Average	Range	Baseline Level	Limit Level
	Leq (30 min) dB(A)	Leq (30 min) dB(A)	dB(A)	dB(A)
NM9 ^[1]	59.3	47.0-68.3	55.9	75
NM10 ^[1]	57.1	46.4-70.8	52.8	
NM11	55.3	46.0-67.7	46.4	
NM12	56.7	46.1-66.9	54.7	
NM13 ^[1]	56.5	47.7-64.7	61.3	
NM14 ^[1]	58.8	47.9-69.1	59.6	

Remarks: [1]: Correction of +3dB (A) for Free-field Measurement.

3.10 Noise monitoring related to construction activities took place according to the planned schedule for the month reported. There were no instances where the Action/Limit Levels were surpassed. A summary of exceedance records for the reporting month can be found in **Appendix J**.

3.11 Based on observations made in the field, the primary sources of noise detected at the allocated noise monitoring stations during the reporting month are as outlined below:

Table 3.5 Observation at Noise Monitoring Stations

Monitoring Station	Major Noise Source
NM9	Loading & unloading, Road traffic, Excavation works
NM10	Loading & unloading, Road traffic, Excavation works
NM11	Road traffic
NM12	Loading & unloading, Road traffic
NM13	Loading & unloading, Road traffic
NM14	Dog barking, Road traffic

Event and Action Plan

3.12 If any non-compliance with the criteria related to the project arises, measures will be taken following the procedures outlined in the Event Action Plan provided in **Appendix I**.

4 AIR QUALITY MONITORING

Monitoring Requirements

- 4.1 As per the EM&A Manual, 1-hour Total Suspended Particulates (TSP) monitoring was carried out to keep track of the air quality associated with the Works Contracts. The predetermined Action/Limit Levels for the air quality monitoring activities are detailed in **Appendix B**.
- 4.2 Monitoring for 1-hour Total Suspended Particulates (TSP) impacts was performed at a minimum of three times within each six-day period at a designated air quality monitoring station.

Monitoring Location

- 4.3 In line with Section 2.2.5 of the EM&A Manual, impact air quality monitoring took place at two specified monitoring stations for the Project, as depicted in Figure 2. The positions of the air quality monitoring stations are detailed in **Table 4.1**.

Table 4.1 Location for Air Quality Monitoring Stations

Monitoring Station	Location of Measurement
AM1	Village House, Kong Nga Po
AM2	Village House, Kong Nga Po

Monitoring Equipment

- 4.4 Due to the denial by local villagers to set up a High-Volume Sampler (HVS) for 1-hour Total Suspended Particulates (TSP) monitoring at the chosen locations and the inability to secure an electricity supply for the HVS, direct-reading dust meters were utilized instead to conduct the 1-hour TSP monitoring. Direct-reading dust meters are widely accepted instruments for measuring 1-hour TSP levels and have been used in the same infrastructure project. The issue to use direct-reading dust meters was presented to the Independent Environmental Checker (IEC). The application of the direct-reading dust meter allows for immediate and straightforward results, facilitating timely EM&A reporting and the execution of the event and action plan. To ensure the validity and accuracy of the readings obtained by the direct-reading method, the HVS performed 1-hour sampling on a bi-monthly schedule.
- 4.5 **Table 4.2** provides a summary of the apparatus employed in the impact air quality monitoring program. The calibration was conducted by Aquality Testconsult Limited. Copies of the calibration certificates for the equipment can be found in **Appendix C**.

Table 4.2 Air Quality Monitoring Equipment

Equipment	Model and Serial No.	Quantity	The valid period is until
Dust Monitor	AEROCET-831/ D12641	1	19 March 2026
Dust Monitor	AEROCET-831/ E11304	1	13 March 2026

4.6 Weather data was sourced from the "Hong Kong Observatory - General Weather Conditions during the Monitoring Period (July 2025)" detailed in **Appendix G**, which was used as a substitute approach to acquire representative wind data.

4.7 During the monitoring days, the field staff also documented the prevailing weather conditions, such as whether it was sunny, cloudy, fine or rainy.

Monitoring Parameters, Frequency and Duration

4.8 **Table 4.3** encapsulates the monitoring variables and the regularity of impact dust assessments conducted throughout the Works Contracts operations. The schedule for air quality observation for the month in question is presented in **Appendix D**.

Table 4.3 Impact Dust Monitoring Parameters, Frequency and Duration

Parameters	Frequency
1-hr TSP	Three times/ 6 days

Monitoring Methodology and QA/QC Procedure

1-hour TSP Air Quality Monitoring

Instrumentation

4.9 The air quality monitoring utilized a direct reading dust meter, as indicated in **Table 4.2**.

4.10 The procedures for operating the dust meter adhere to the guidelines set forth in the Manufacturer's Instruction Manual, as described below:

- The 1-hour dust meter is placed at least 1.3 meters above ground.
- Press and hold the Power key momentarily to power on the unit and make sure that the battery level was not flash or in low level.
- Allow the instrument to stand for about 3 second to display the Sample Screen minutes.
- Press the START / STOP key to run the internal vacuum pump for 1 minute and ready to use.
- Use the select dial to select the PM range and press the START / STOP key to start a measurement.
- Finally, push the START/STOP key to stop the measuring after 3-hour sampling.

- Information such as sampling date, time, value and site condition were recorded during the monitoring period.
- All data were recorded in the data logger for further data processing.

Maintenance/Calibration

4.11 The dust meter required the following maintenance and calibration:

- The dust meter must be checked and calibrated against a High Volume Sampler (HVS) to validate the precision and accuracy of the readings obtained through the direct reading method.
- The correlation between the dust meter and HVS in measuring TSP was established by directly comparing the mass of dust particles collected on a filter paper by the HVS against the dust meter's reading. For accurate calibration, both the dust meter and the HVS should be turned on and off at the same location and at the same time.
- The correlation coefficient was verified to confirm the relationship between the readings from the dust meter and the HVS. This correlation factor was ascertained by comparing the outcomes from both the HVS and the dust meter.
- Prior to the initiation of dust monitoring, a check must be conducted to verify that all equipment is operational and has the necessary power supply. A zero count test was performed before and after each monitoring session to ensure accuracy.

Results and Observations

4.12 The outcomes of the 1-hour TSP monitoring are condensed in **Table 4.4**. For a comprehensive view, detailed results and graphical representations of the 1-hour TSP monitoring data can be found in **Appendix E**.

Table 4.4 Summary Table of 1-hour TSP Monitoring Results during the Reporting Month

Monitoring Station	Concentration ($\mu\text{g}/\text{m}^3$)		Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
	Average	Range		
AM1	77	29-156	308	500
AM2	64	9-101	311	

4.13 The 1-hour TSP monitoring took place according to the planned timetable for the reporting month, and there were no instances of exceeding the established Action/Limit Levels.

4.14 Based on field observations, the primary sources of dust at the specified air quality monitoring stations during the reporting month are listed in **Table 4.5**.

Table 4.5 Observation at Dust Monitoring Stations

Monitoring Station	Major Dust Source
AM1	Equipment operation and movement / road traffic, exposed site area, site vehicle
AM2	Road traffic, exposed site area, site vehicle / equipment operation and movement, vehicle / equipment operation and movement at warehouse nearby

Event and Action Plan

- 4.15 In the event of a project-related violation of the criteria, measures will be taken as specified by the Event Action Plan detailed in **Appendix I**.

5 LANDSCAPE AND VISUAL MONITORING

Monitoring Requirements

- 5.1 The EIA Report recommends implementing strategies to mitigate impacts on landscape and visual resources throughout both the construction and operational phases of the Project.
- 5.2 The execution and upkeep of compensatory planting for landscaping are critical components of this process and must be monitored to confirm their complete fulfillment. It is essential to promptly address any potential clashes between the proposed landscaping efforts and other Project tasks or operational needs to ensure that the mitigation measures' objectives are not compromised. Furthermore, the enforcement of the mitigation measures advised by the EIA will be tracked continuously through the site audit program for the construction phase.
- 5.3 The Environmental Team (ET) carried out a fortnightly review of the execution of measures aimed at mitigating landscape and visual impacts as part of the weekly site audits. The findings and observations from these audit sessions are encapsulated in **Table 5.1**, while the status of implementation can be found detailed in **Appendix K**.

6 ECOLOGICAL MONITORING

Monitoring of Flora Species of Conservation Interest

- 6.1 In line with Section 8.3.2 of the EM&A Manual, a temporary protective barrier must be installed around the plant species of conservation significance identified in the detailed vegetation survey throughout the construction phase. This barrier should be well-maintained and regularly checked to ensure its effectiveness. Monthly checks of each plant species of conservation interest, as pinpointed in the detailed vegetation survey, are required during the construction phase to ensure that these species remain unaffected by the project's construction activities.
- 6.2 The monitoring aims to oversee the prompt execution of suitable environmental management practices and the application of mitigation measures concerning the preserved and relocated specimens of flora species of conservation interest. The correct setup and upkeep of the temporary protective fence surrounding these specimens were examined to assess its efficacy. The protective measures outlined in the approved transplantation proposal's implementation schedule were supervised.
- 6.3 As per the sanctioned detailed vegetation survey report and transplantation proposal, it was determined that 71 *Brainea insignis* specimens, 41 *Spiranthes sinensis* specimens, and 3 *Aquilaria sinensis* specimens should be relocated to the designated receiving site. Additionally, it was decided to preserve in situ 51 *Keteleeria fortunei* specimens, along with 26 small seedlings of *Keteleeria fortunei* and 7 small seedlings of *Aquilaria sinensis*, in the vicinity of Kong Nga Po Road near the Police Dog Unit and the Force Search Unit Training School.

Post-Transplantation Monitoring and Maintenance Programme

- 6.4 In line with the accepted transplantation proposal, the Contractor is mandated to carry out post-transplantation monitoring weekly for the first three months, and then monthly for the remainder of the 12-month establishment phase as well as the subsequent post-establishment phase, continuing until the construction phase of the Project concludes. This routine monitoring is critical for promptly identifying the growth condition of the transplanted species, any signs of construction work within or in the vicinity of the receptor site, and any changes in the environmental conditions of the receptor site.
- 6.5 For the initial year of acclimatization, it was advised to carry out maintenance activities to promote the robust growth of the transplanted species. Considering the state of the transplanted organisms following the 12-month establishment period, it was advised that maintenance activities continue through the Post-establishment Period until the completion

of the Construction Phase. It was recommended to water the transplants daily for the first three months following the move, as well as throughout periods of drought, to maintain soil moisture. Additional maintenance tasks, such as mulching and weeding, should be performed as necessary.

Results and Observations

6.6 During the reporting month, the Contractor carried out monthly evaluations of the flora species of conservation interest on the 28 July 2025. The enforcement of the protective measures detailed in the approved transplantation proposal was reviewed, along with the maintenance of the temporary protective fencing. **Appendix H** contains the photographic documentation and checklists from the monthly assessments. The health of the transplanted and retained species was generally observed to be average to poor. The Contractor was urged to keep a vigilant eye on the transplanted species and to implement the protective measures as specified in the approved transplantation proposal to safeguard these species. Furthermore, the Contractor was given the following directives:

- 1) To provide new identification tags for any *Brainea insignis* that were missing them;
- 2) To substitute any plant labels at the receptor site that had become illegible due to fading;
- 3) To refer to the soil improvement guidelines published by the Greening, Landscape and Tree Management Section (GLTMS) of the Development Bureau (2022) for application in the monitoring and upkeep of the transplanted plant species;
- 4) To set up shade nets;
- 5) To ensure the soil remains moist by adhering to the necessary daily watering schedule.

Transplanted *Brainea insignis* and *Spiranthes sinensis*

6.7 From May 21st to 28th, 2020, 71 *Brainea insignis* specimens and 41 *Spiranthes sinensis* specimens were relocated to the receptor site. The detailed account of the transplantation process was compiled in a Transplantation Report and forwarded to ET(Wellab), IEC(Acuity), and the Supervisor (AECOM) for their examination and documentation. Monitoring after transplantation took place weekly for the initial three months (from June to August 2020) and then monthly throughout the subsequent 12-month establishment period, as well as the post-establishment phase, culminating with the conclusion of the construction phase of the Project. The Contractor was responsible for tracking the health of the transplanted species and carried out maintenance measures such as watering, mulching, and weeding during the first year to nurture the transplanted species' healthy development. Monitoring of the transplanted *Brainea insignis* and *Spiranthes sinensis* took place on the 28 July 2025, within the reporting period, with the findings documented in **Appendix H**. Particular attention was given to the transplanted *Brainea insignis* specimens that were impacted by a bushfire on February 2nd, 2021, with their progress detailed in the post-

transplantation monitoring records. The health of the preserved species was noted to be generally fair. The Contractor was advised to maintain vigilant monitoring of these species and to enforce the stipulated protective measures to ensure their continued preservation.

- 6.8 During the monthly checks, it was observed that there were no construction operations or storage of equipment taking place within the receptor site. The temporary protective barrier had been correctly installed and was being well-maintained to safeguard the transplanted species.

Precautionary Measure for Butterfly Species of Conservation Interest

- 6.9 As stipulated by FEP Condition 2.17, to reduce the impact on butterfly species of conservation concern, efforts shall be made to improve the new grassland habitats within the Project site. This enhancement shall be achieved by cultivating suitable plant species that serve as the larval food source for butterflies of conservation interest, like the Small Three-Ring, thereby supporting the well-being of these species.
- 6.10 The restoration of grassland zones within the Project must be completed prior to the initiation of the Project's operational phase. Information regarding the plant species to be used as larval food plants for butterflies, along with the design and execution details, will be subsequently provided under the building works contract of ArchSD.

Precautionary Measures to Minimize Indirect Disturbance on Ecology

- 6.11 As outlined in Section 9.7.3 of the EIA Report, implementing mitigation strategies for air, noise, water, waste, and landscaping can serve as preventative actions to avert and lessen any secondary effects of disturbance or pollution resulting from construction activities on the surrounding ecology and habitats outside the site. The Environmental Team (ET) conducted weekly site audits to oversee the prompt adoption of appropriate environmental management practices and the execution of mitigation measures at the Project site. The findings from these audits are consolidated in Section 7.3.

7 ENVIRONMENTAL SITE INSPECTION

Site Audits

- 7.1 The Environmental Team (ET) conducted site audits weekly to oversee the prompt adoption of appropriate environmental management practices and the execution of mitigation measures at the Contract site.
- 7.2 The Environmental Team (ET), along with representatives from the Client and the Contractor, conducted site audits on 11, 17, 23, 29 July 2025 of the reported month in 2025.
- 7.3 In the site inspections conducted over the reporting period, there were no particular environmental concerns noted. It should be recognized that these observations pertain solely to the moments of inspection. The findings and advice from these audits are compiled in **Table 5.1**. The absence of identified environmental issues during the joint site inspections does not exempt the Contractor from their obligation to adhere strictly to all legal requirements, the Particular Specifications, and the Environmental Monitoring and Audit (EM&A) Manual.

Table 5.1 Observations of Weekly site Inspection and advice

Parameters	Date	Observations	Advice
Waste Management Implications	11-7-2025	Bags of leftover packaged lunchboxes were observed at the waste collection area. Discarded food can attract rodents, vermin, insects, and other pests, potentially leading to nuisance issues. For instance, fly breeding and/or rodent infestation may spread diseases and pose potential risks to the surrounding environment.	General refuse should be stored in enclosed bins
Water Quality Impact	11-7-2025	In periods of heavy rainfall, construction waste, debris, and refuse may be swept by runoff into nearby gully gratings, introducing pollutants and causing environmental pollution	Construction waste, debris and refuse generated on-site should be stored or contained appropriately to prevent them blocking stormwater drains.
Water Quality Impact	17-7-2025	Sediment and blockage build-up can reduce the channel's capacity to efficiently transport water, causing slower water flow and potential overflow during heavy rainfall	Maintenance and inspection of the drainage system and sediment removal facilities should be carried out regularly to remove any sediment and blockages, especially when rainstorms are forecast
Waste Management Implications	17-7-2025	Not only can wood and construction waste physically compress the underlying soil—reducing its porosity—but such compaction also makes it difficult for roots to grow and limits the soil's ability to absorb nutrients and water, resulting in potential poor grass health	1. Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site

			practices. 2. Construction waste, debris and refuse generated on-site should be stored or contained appropriately to prevent entering nearby watercourses or blocking stormwater drains.
Landscape and Visual Impacts	23-7-2025	The storage areas for materials compact the soil around tree	DEVB T(W) 7/2015 on “tree preservation” stipulates that the material storages are to be kept away from the Tree Protection Zone and vehicular/pedestrian access to avoid compaction of soil around trees
Waste Management Implications	29-7-2025	Not only can wood and construction waste physically compress the underlying soil—reducing its porosity—but such compaction also makes it difficult for roots to grow and limits the soil’s ability to absorb nutrients and water, resulting in potential poor grass health	1. Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. 2. Construction waste, debris and refuse generated on-site should be stored or contained appropriately to prevent entering nearby watercourses or blocking stormwater drains.

Implementation Status of Environmental Mitigation Measures

- 7.4 In accordance with the EIA Report and the Project's EM&A Manual, the outlined mitigation measures are recommended to be implemented throughout the construction phase. An overview of the Environmental Mitigation Implementation Schedule (EMIS) is available in **Appendix K**.

Solid and Liquid Waste Management Status

- 7.5 Pursuant to the EM&A Manual, waste management practices were reviewed in the weekly site audits to assess compliance with the Project's Waste Management Plan (WMP) and pertinent legal and contractual obligations. The auditing process encompassed the examination of waste handling, storage, transport, and disposal methods.
- 7.6 The Contractor has appointed Environmental Officers on-site to manage environmental aspects, implement pollution control strategies, maintain proper site conduct, and educate workers on waste management. Efforts to reduce waste production include actively using Construction and Demolition (C&D) materials. Excavated materials have been sorted and screened on-site to salvage any recyclables. Non-reactive C&D materials were utilized on-

site for backfill and to construct the haul road surface. Furthermore, inert materials from excavation activities were repurposed as fill in other local projects. Excess inert C&D materials were sent to the Government's public fill reception facilities (PFRFs) for use in other projects. To oversee the disposal of inert and non-inert C&D materials and prevent illegal dumping, a system is in place where all materials are weighed by a weighbridge before leaving the site, and the Trip Ticket System is rigorously enforced.

- 7.7 Contractor is encouraged to reduce waste production by recycling or reusing materials. It is imperative that all the mitigation strategies outlined in the EM&A Manual and the waste management plans be thoroughly executed. A summary of the progress in implementing waste management and reduction strategies is provided in **Appendix K**.
- 7.8 This Project produces inert Construction and Demolition (C&D) materials as well as non-inert C&D materials. The non-inert variety consists of general refuse and other waste materials that cannot be repurposed or recycled, necessitating disposal at assigned landfill locations. Data detailing the volume of waste resulting from the Project's construction activities over the reporting period can be found in **Appendix L**.

8 ENVIRONMENTAL NON-CONFORMANCE

Summary of Exceedances

- 8.1 During the reporting month, there were no instances where the air quality exceeded the established Action and Limit Levels.
- 8.2 There were no instances of construction noise surpassing the designated Action and Limit Levels in the reporting period.
- 8.3 If the monitoring data from any specific stations reveal that environmental parameters have surpassed the Action/Limit Levels, then the procedures outlined in the Event and Action Plans in **Appendix I** should be executed. A summary of any exceedance records for the reporting month can be found in **Appendix J**.

Summary of Environmental Non-Compliance

- 8.4 There were no records of environmental compliance breaches during the reported month.

Summary of Environmental Complaint

- 8.5 In the month under review, no complaints were registered. A log of all complaints accumulated since the start of the Project is compiled in **Appendix M**.

Summary of Environmental Summon and Successful Prosecution

- 8.6 Since the beginning of the Project, there have been no instances of successful environmental prosecution or receipt of summons. A comprehensive record of all environmental summonses and successful prosecutions since the Project's inception is documented in **Appendix N**.

9 FUTURE KEY ISSUES

Key Issues in the Coming Three Months

- 9.1 **Appendix A** contains the provisional construction schedules for the Project. Over the next three months, the principal construction tasks to be carried out will include:
1. Open cut excavation
 2. Removal of soil
 3. Construction of footings
 4. Construction of substructure and superstructure
 5. Construction of footbridge
 6. Construction of fence wall and boundary wall
 7. Installation of structural steelworks for 300m baffle range
 8. Backfilling
 9. U.U. Lead in and Pipe Duct Connection
- 9.2 Referring to the site layout plan found in **Appendix A**, which details the expected construction activities for the next three months, the primary environmental concerns related to these activities are likely to be construction dust, noise, water quality, waste management, landscape and visual aesthetics, and ecological impacts. The anticipated environmental effects have been factored into the mitigation strategies planned for the upcoming months.
- 9.3 The Contractor has advised mitigation measures for the next three months, which the Environmental Team (ET), Independent Environmental Checker (IEC), and the Client's Representative have reviewed through email correspondence during site audits. The Proactive Environmental Protection Proforma, which outlines the key site activities, potential environmental impacts, and advised mitigation strategies, has been examined and verified by the IEC and is displayed in **Appendix A**.
- 9.4 During construction and in periods of dry weather, dust can arise from work activities and uncovered site areas. To mitigate dust emissions that could affect nearby villages, the Contractor is advised to diligently apply air quality control measures as outlined in the layout plan in **Appendix A**, to the greatest extent possible. Moreover, the Contractor is reminded to adhere to the Project Implementation Schedule detailed in the approved EIA report/EM&A Manual, implementing suitable dust suppression tactics to curb emissions from intensive construction tasks such as ground excavation and earth moving. This includes managing all active work areas, bare site surfaces, and unpaved roads, especially under dry conditions, by covering 80% of stockpiled materials with impervious coverings and by moistening dusty substances with water just before loading and transfer activities. This ensures materials remain damp during handling in stockpile regions. Additionally, the

Contractor must adhere to the prescribed dust control methods under the Air Pollution Control (Construction Dust) Regulation to prevent negative dust impacts from the Project's construction activities.

- 9.5 Furthermore, construction noise represents a significant environmental concern during the Project's development. It is important to implement noise reduction strategies, such as utilizing quiet machinery and installing noise barriers where relevant. The Contractor has been prompted to regularly inspect and upkeep the sound-dampening materials on noisy sections of plant and machinery, ensuring there are no openings in the noise barriers. They should also actively recognize any potential construction noise impacts to Noise Sensitive Receivers (NSRs) and introduce adequate mitigation measures when required. Additionally, residents in the nearby Kong Nga Po village should be informed in advance about any potentially noisy activities at the work site.
- 9.6 The Contractor is advised to uphold measures that protect water quality throughout the construction process. This includes constructing barriers such as dikes or embankments to prevent flooding around the perimeters of areas where soil is being moved or excavated. Provision should be made for temporary channels to direct runoff effectively into a designated watercourse via a trap designed to capture sediment from the site. These sediment/silt traps should also be integrated into the permanent drainage systems to improve the settling of particulates. It is essential to utilize effective silt removal systems to ensure that the effluent treated by the wastewater treatment plant complies with the standards specified in the WPCO licenses. The Wastewater Discharge Layout Plan, as shown in **Appendix Q** and provided by the Contractor, outlines the specific pathways through which wastewater is to be conveyed from its source to a treatment facility or point of discharge

Monitoring Schedule for the Next Month

- 9.7 **Appendix D** displays the provisional schedule for environmental monitoring activities planned for the upcoming month.

10 CONCLUSIONS AND RECOMMENDATIONS

Conclusions

- 10.1 This Monthly EM&A Report details the environmental monitoring and audit (EM&A) activities conducted in July 2025, following the guidelines set out in the EM&A Manual.
- 10.2 During the month in question, air quality monitoring did not register any instances of surpassing the Action/Limit Levels.
- 10.3 No instances of construction noise exceeding the established Action/Limit Levels were documented in the reporting month's monitoring records.
- 10.4 Site inspections focusing on environmental aspects took place on the 11, 17, 23, 29 July 2025. Additionally, monitoring of landscape and visual impacts was performed on the 11, 17, 23, 29 July 2025, and ecological monitoring was conducted on the 23 July 2025 by ETL within the reporting month. The Contractor also conducted monitoring on 28 July 2025. There were no records of environmental non-compliance for the reporting month. It should be noted that the absence of any particular environmental issues during the joint site inspections does not exempt the Contractor from their obligation to adhere fully to all legal requirements, the specifications outlined in the contract, and the procedures in the EM&A Manual.
- 10.5 During the reporting month, there were no complaints lodged, nor were there any notices of summons or records of successful legal actions received.
- 10.6 The Environmental Team (ET) will persist in overseeing the Environmental Monitoring and Audit (EM&A) program. All environmental obligations are fulfilled, and the necessary mitigation measures are properly executed.

Recommendations

- 10.7 Based on the environmental audits conducted during the reporting month, the subsequent advice was put forward:

Air Quality Impact

- To enhance the dust suppression measures including watering for the dust generation works, exposed site area and haul road;
- To minimize the indirect impacts on air quality resulting from the operation of machineries on the construction site, one of the measures to be adopted is the use of biodiesel B100; and

- To regular check the valid NRMM labels are properly displayed on the regulated machines and non-road vehicles

Construction Noise

- To refer to the ISO 12001:1996 or other comprehensive practices and subsequently develop a thorough inspection and maintenance protocol for the plant and equipment, maintaining a focus on Noise Control; and
- To maintain temporary noise barriers for operations of noisy equipment near the noise sensitive receivers, if necessary.

Water Impact

- To maintain the cover for open stockpile of and exposed slope;
- To keep reviewing and updating temporary drainage system;
- To maintain the earth bunds or sand bag barriers on site to direct stormwater to silt removal facilities; and
- To divert the muddy water at the retention pond to the wetsep for treatment before discharging out.

Waste/Chemical Management

- To check for any accumulation of waste materials or rubbish on site; and
- To avoid improper handling, storage and dispose of oil drums or chemical containers on site.


Ecology

- To maintain soil moisture, daily watering is required;
- To install a shaded net;
- To refer to the Guidelines on Soil Improvement issued by the Greening, Landscape and Tree Management Section (GLTMS) of the Development Bureau (2022) for the effective monitoring and maintenance of transplanted flora species; and
- The wild plants that are growing in undesirable areas should be removed, as they compete with the cultivated flora species of conservation interest.

Landscape and Visual


- To remove the construction materials within the tree protection zone; and
- To keep the tree protection zone large enough to protect the tress.

FIGURE(S)

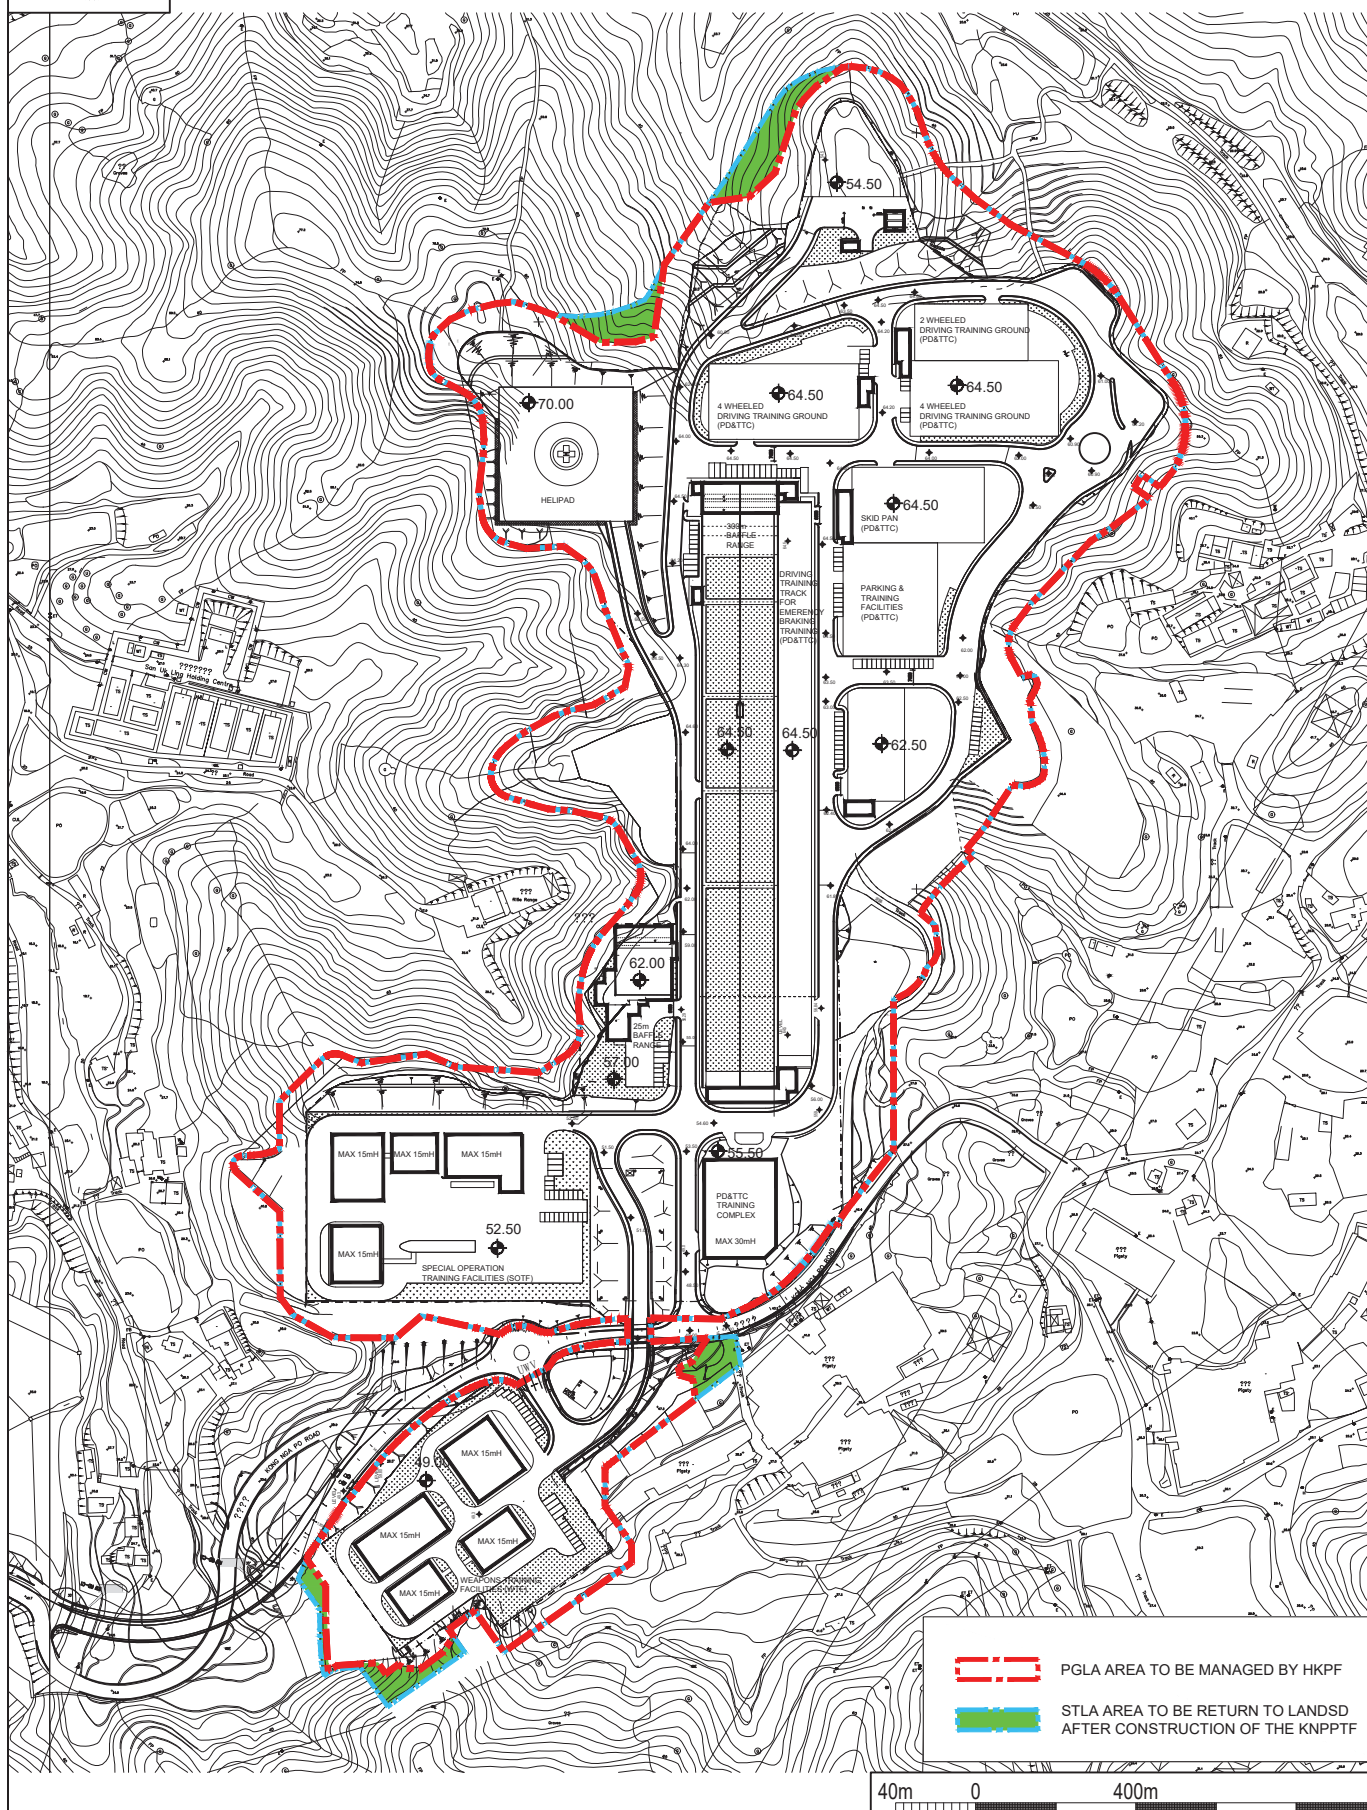

ARCHITECTURAL
SERVICES
DEPARTMENT 建築署

Figure 2 Location of Air Quality Monitoring Stations

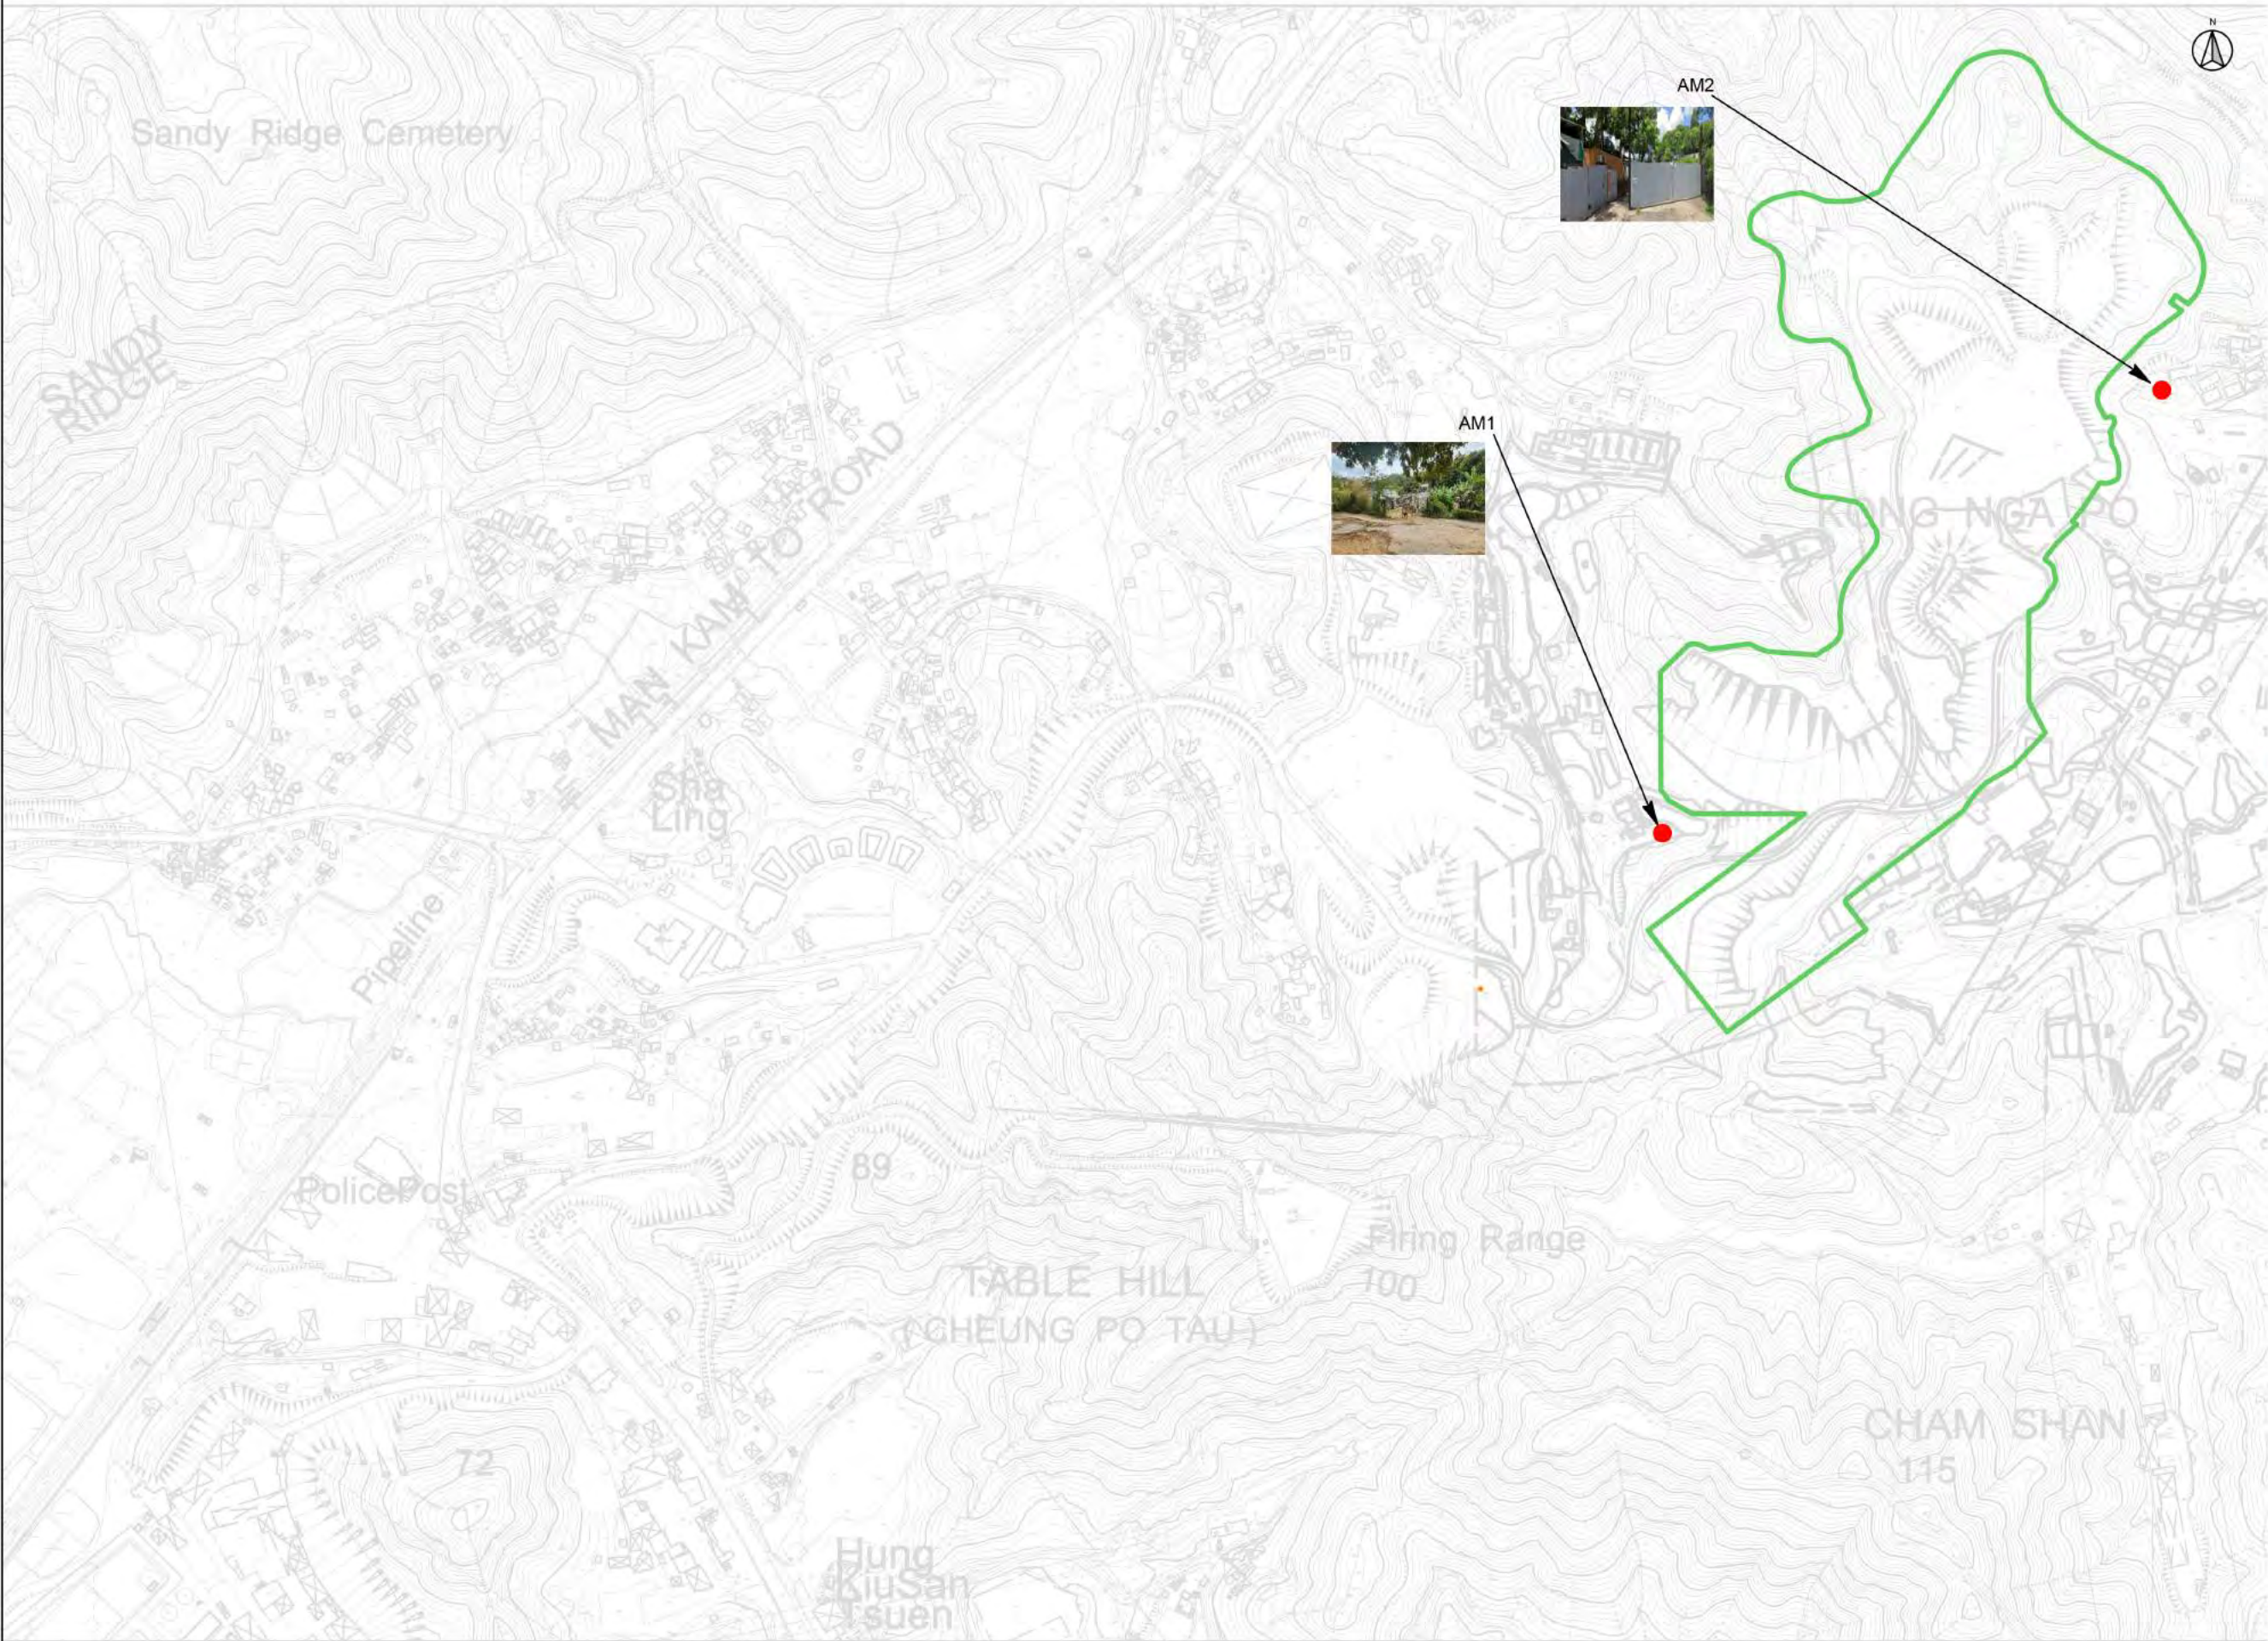

KEY PLAN
SCALE: 1/50000

LEGENDS:

- KONG NGA PO SITE BOUNDARY
- AIR QUALITY MONITORING STATIONS

AIR QUALITY MONITORING STATIONS	
ID	Description
AM1	Village House, Kong Nga Po
AM2	Village House, Kong Nga Po

CLIENT
 Architectural Services Department

Environmental Team
嘉誠管理顧問有限公司
Ka Shing Management Consultancy Ltd.
www.ka-shing.net

This drawing is for the sole purpose of explaining design and construction intent only. No part of this drawing or its related or implied information should supersede local and/or statutory code, regulation or requirement, including but not limited to any supplier and/or manufacturer recommendations. Ka Shing Management Consultancy Ltd accepts no responsibility for compliance checking which should be done by suitably qualified and authorized local design institutes in all cases.

KA SHING MANAGEMENT CONSULTANCY LTD
Unit 2, 13/F Kai Yue Commercial Building, 2C Argyle St.
Mong Kok, Kowloon
Tel: +852 2616 2166 Fax: +852 2120 7752
Email: info@ka-shing.net

2	SECOND ISSUE	03/2023
1	FIRST ISSUE	03/2023

Rev.	Description	Date
Project Title		
PROVISION OF ENVIRONMENTAL TEAM CONSULTANCY FOR DESIGN AND CONSTRUCTION OF KONG NGA PO POLICE TRAINING FACILITIES		

Drawing Title
KONG NGA PO ROAD
AIR QUALITY MONITORING STATIONS

Drawing Status	
Project Ref.	File Ref.
Drawn by	Checked by
Scale	Paper Size
Date	Revision

Drawing Number
KASHING-KNPR-DWG-002

Figure 3 Location of Noise Monitoring Stations



KEY PLAN
SCALE: 1:50000

LEGENDS

- KONG NGA PO SITE BOUNDARY
- NOISE MONITORING STATIONS

ID	Description
NM9	Village House, Kong Nga Po
NM10	Village House, Kong Nga Po
NM11	Village House, Kong Nga Po
NM12	Village House, Kong Nga Po
NM13	Village House, Kong Nga Po
NM14	Village House, near Man Kam To Road

CLIENT

建築署
Architectural Services Department

Environmental Team

嘉誠管理顧問有限公司
Ka Shing Management Consultancy Limited
www.ka-shing.net

This drawing is for the sole purpose of explaining design and construction intent only. No part of this drawing or its related or implied information should supersede local and/or statutory code, regulation or requirement, including but not limited to any supplier and/or manufacturer recommendations. Ka Shing Management Consultancy Ltd accepts no responsibility for compliance checking which should be done by suitably qualified and authorized local design institutes in all cases.

KA SHING MANAGEMENT CONSULTANCY LTD
Unit 2, 13/F Kai Yue Commercial Building, 20 Argyle St, Mong Kok, Kowloon
Tel: +852 2818 2166 Fax: +852 2120 7752
Email: info@ka-shing.net

Rev.	Description	Date
2	SECOND ISSUE	03/2023
1	FIRST ISSUE	03/2023

Project Title

PROVISION OF ENVIRONMENTAL TEAM CONSULTANCY FOR DESIGN AND CONSTRUCTION OF KONG NGA PO POLICE TRAINING FACILITIES

Drawing Title

KONG NGA PO ROAD NOISE MONITORING STATION

Drawing Status

Project Ref.	File Ref.
-	--

Drawn by	Checked by
JC	RH

Scale	Paper Size
1:40000	A3

Date	Revision
-	-

Drawing Number

KASHING-KNPR-DWG-003

APPENDIX A

**CONSTRUCTION PROGRAMME AND
PROACTIVE ENVIRONMENTAL
PROTECTION PROFORMA**

Construction Programme (Jul 2024 – Sep 2025)

Design & Construction of Kong Nga Po Police Training Facilities Programme

Revision : Revision 15 (June 2025)

	Task	Duration	Start	Finish	Total Slack	Time Risk Allowance	2023	2024	2025	2026	2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026	Qtr 2, 2026	Qtr 3, 2026	Qtr 4, 2026	Qtr 1, 2027	Qtr 2, 2027	Qtr 3, 2027	Qtr 4, 2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
1367	Superstructure Construction	751 d	11/12/2023	31/12/2025	396 d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																</

Design & Construction of Kong Nga Po Police Training Facilities Programme

Revision : Revision 15 (June 2025)

ID	Task	Duration	Start	Finish	Total Slack	Time Risk Allowance	2023	2024	2025	2026	2027
1429	G/F	135 d	17/1/2024	30/5/2024	0 d		Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024
1430	1/F	70 d	24/5/2024	1/8/2024	7.5 d	0 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1431	R/F	35 d	20/7/2024	23/8/2024	877 d	0 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1432	TR/F	21 d	25/9/2024	15/10/2024	838 d	0 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1433	Block 4 (Marine Mock Bldg.)	268 d	6/2/2024	30/10/2024	823 d	0 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1434	G/F	131 d	6/2/2024	15/6/2024	0 d		Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1435	1/F	28 d	9/6/2024	6/7/2024	0 d	0 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1436	2/F	38 d	25/7/2024	31/8/2024	855 d	0 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1437	R/F	21 d	3/9/2024	23/9/2024	846 d	0 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1438	TR/F	21 d	10/10/2024	30/10/2024	823 d	0 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1439	Completion of Superstructure of Section 1	0 d	15/3/2025	15/3/2025	687 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1440	Section 2 Works	348 d	18/1/2025	31/12/2025	396 d		Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1441	Baffle Range	348 d	18/1/2025	31/12/2025	395 d		Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1442	300m Baffle Range	281 d	18/1/2025	31/12/2025	329 d		Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1443	Installation of precast fence wall	117 d	10/2/2025	10/7/2025	331 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1444	Installation of precast baffle	53 d	11/7/2025	10/9/2025	331 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1445	Baffle Range Ancillary Structure	90 d	13/9/2025	31/12/2025	329 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1446	Completion of 300m baffle range	281 d	18/1/2025	31/12/2025	329 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1447	25m Baffle Range	126 d	2/8/2025	31/12/2025	329 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1448	Helipad	177 d	2/6/2025	31/12/2025	329 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1449	SOTF Block 1-4	206 d	19/3/2025	10/10/2025	392 d		Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1450	Block 1 (Admin, School & MTR Mock Block)	206 d	19/3/2025	10/10/2025	392 d		Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1451	1/F	95 d	19/3/2025	15/7/2025	470 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1452	2/F	95 d	24/4/2025	16/8/2025	290 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1453	R/F	96 d	15/5/2025	6/9/2025	424 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1454	TR/F	101 d	11/6/2025	10/10/2025	268 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1455	Block 2 (Hotel Mock Bldg.)	167 d	2/4/2025	15/9/2025	502 d		Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1456	1/F	24 d	2/4/2025	3/5/2025	529 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1457	2/F	81 d	2/5/2025	7/8/2025	450 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1458	R/F	81 d	23/5/2025	27/8/2025	433 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1459	TR/F	75 d	19/6/2025	15/9/2025	417 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1460	Block 3 (Arcade and Residential Mock Bldg.)	147 d	16/4/2025	9/9/2025	508 d		Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1461	1/F	24 d	16/4/2025	17/5/2025	517 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1462	2/F	62 d	16/5/2025	30/7/2025	457 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1463	R/F	62 d	6/6/2025	19/8/2025	440 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1464	TR/F	58 d	4/7/2025	9/9/2025	422 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1465	Block 4 (Airport Mock Bldg.)	106 d	5/5/2025	18/8/2025	530 d		Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1466	1/F	58 d	5/5/2025	14/7/2025	471 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1467	2/F	20 d	31/5/2025	24/6/2025	487 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1468	R/F	14 d	14/7/2025	29/7/2025	458 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1469	TR/F	18 d	29/7/2025	18/8/2025	441 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1470	Completion of Superstructure of Section 2	0 d	31/12/2025	31/12/2025	396 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1471	Façade, External Wall & Roof Finishing	567 d	13/5/2024	30/11/2025	427 d		Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1472	Section 1 Works	414 d	13/5/2024	30/6/2025	580 d		Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1473	Window Wall/ Glass Wall Fabrication	120 d	13/5/2024	9/9/2024	874 d	1 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1474	Window Wall/ Glass Wall installation	210 d	2/11/2024	30/5/2025	605 d	1 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1475	Aluminium Cladding Installation	167 d	2/1/2025	17/6/2025	593 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1476	Aluminium Louvre Installation	191 d	21/11/2024	30/5/2025	611 d	1 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1477	Water Test for Window, Window Wall	144 d	7/2/2025	30/6/2025	580 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1478	Flat Roof & Roof Screeding & Waterproofing	195 d	21/11/2024	3/6/2025	607 d	0 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1479	Flat Roof & Roof Water Testing	120 d	11/2/2025	10/6/2025	600 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1480	Wall Plastering	153 d	4/12/2024	5/5/2025	636 d	1 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1481	Wall Tiling	164 d	28/11/2024	10/5/2025	631 d	1 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1482	External Wall Painting	158 d	4/12/2024	10/5/2025	631 d	1 d	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
1483	General cleaning / Water Testing	39 d	1/3/2025	8/4/2025	663 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1484	External wall in Towers complete	39 d	8/3/2025	15/4/2025	656 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1485	Dismantle of External Scaffolding	82 d	8/3/2025	28/5/2025	607 d	0 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1486	Section 2 Works	275 d	1/3/2025	30/11/2025	427 d		Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1487	Window Wall/ Curtain Wall Fabrication	90 d	1/3/2025	29/5/2025	612 d	1 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1488	Window Wall/ Curtain Wall installation	135 d	21/6/2025	30/11/2025	355 d	1 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1489	Aluminium Cladding Installation	109 d	4/7/2025	11/11/2025	371 d	1 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026
1490	Aluminium Louvre Installation	99 d	4/7/2025	30/10/2025	381 d	1 d	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025	Qtr 1, 2026

Layout Plan with major construction activities

Legend:

Foundation construction and associated works

- Soil Storage

- E&M installation
- Tree planting works

- Construction of superstructure
- E&M installation

- E&M installation
- Tree planting works

- Open cut excavation
- Soil removal/ Soil Storage
- Backfilling
- U.U. Lead in and Pipe Duct Connection
- Construction of footings
- Construction of fence wall

- E&M installation
- Tree planting works

- E&M installation
- Tree planting works

- Backfilling
- U.U. Lead in and Pipe Duct Connection
- Construction of footings
- Construction of superstructure

- Open cut excavation
- Soil Removal
- U.U. Lead in and Pipe Duct Connection
- Construction of footing
- E&M installation

- E&M installation

- E&M installation
- Construction of substructure

- Construction of footbridge

- Construction of Boundary wall
- E&M installation

Major construction activities carried out in period of July 2025

Legend:



Foundation construction and associated works



- Soil Storage

- E&M installation
- Tree planting works

- E&M installation

- E&M installation
- Tree planting works

- Excavation
- Soil removal
- U.U. Lead in and Pipe Duct Connection
- Construction of fence wall
- Painting
- Installation of structural steelworks for 300m baffle range

- E&M installation
- Tree planting works

- E&M installation
- Tree planting works

- U.U. Lead in and Pipe Duct Connection
- Construction of footing
- E&M installation

- Backfilling
- U.U. Lead in and Pipe Duct Connection
- Construction of footings
- Construction of superstructure

- E&M installation

- E&M installation
- Tree planting works

- Construction of footbridge

- E&M installation
- Tree planting works
- Construction of Boundary Wall

Major construction activities carried out in period of Aug ~ Oct 2025

Proactive Environmental Protection Proforma

Proactive Environmental Protection Proforma

Ref*	Proposed Construction Method	Location/Working Period	Anticipated Major Impacts	Recommended Mitigation Measures
EIA 3.9.1; EM&A Log 2.2	Open cut excavation	Kong Nga Po Site	Dust impact from excavation activities and earth moving	• Use of regular water spraying (once every 1.25 hours or 8 times per day) at all active works area exposed site surfaces and unpaved roads, particularly during dry weather • Deploy water bowser for regular water spraying to enhance dust suppression • Manual water spraying for dusty operation where inaccessible by water bowser • Speed control of site transportation • Stockpile of dusty materials will be covered by tarpaulin sheets to avoid wind-blown dust • Vehicles used for transporting dusty materials/spoils will be covered by mechanical cover before leaving the site • Wheel washing facilities will be provided and cleaning the wheel of all vehicles before leaving the site
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition

				• Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of construction materials to reduce the potential for water pollution • Provide wastewater treatment facilities prior to discharge of wastewater • Regular inspection and maintenance of wastewater treatment facilities • Wastewater pumped out of the excavation areas will be treated to remove suspended solids prior to discharge • Hard paving or well-compact of main haul road to minimize washout of soil • Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged.
EIA 7.5.1.1 &			Waste Generation	• Training of site personnel in proper waste management and

7.5.1.2; EM&A Log 6.2				chemical handling procedures • Proper storage and sorting of excavated inert materials to maximize on site reuse for backfilling • Surplus inert C&D materials will be disposed of at designated Government's PFRF.
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Chemical waste should be stored at chemical waste container and collected by a licensed collector to transport and dispose of at the approved Chemical Waste Treatment Centre • Drip tray and chemical spillage kit will be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to frontline workers for the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Restrict construction area to minimize the impact on existing retained trees
EIA 3.9.1; EM&A Log 2.2	Soil Removal	Kong Nga Po Site	Dust impact from excavation activities and earth	• Use of regular water spraying (once every 1.25 hours or 8 times per day) at all active works area exposed site surfaces and unpaved roads, particularly during dry weather

			moving	• Water spraying during loading and unloading of excavated materials • Vehicles used for transporting dusty materials/spoils will be covered by mechanical cover before leaving the site • Deploy water bowser for regular water spraying to enhance dust suppression • Speed control of site transportation • Stockpile of dusty materials will be covered by tarpaulin sheets to avoid wind-blown dust • Wheel washing facilities will be provided and cleaning the wheel of all vehicles before leaving the site
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition • Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of excavated materials to reduce the potential for water pollution

				• Provide wastewater treatment facilities prior to discharge of wastewater • Regular inspection and maintenance of wastewater treatment facilities • Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged.
EIA 7.5.1.1 & 7.5.1.2; EM&A Log 6.2			Waste Generation	• Training of site personnel in proper waste management and chemical handling procedures • Proper storage and sorting of excavated inert materials to maximize on site reuse for backfilling • Surplus inert C&D materials will be disposed of at designated Government's PFRF.
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Chemical waste should be stored at chemical waste container and collected by a licensed collector to transport and dispose of at the approved Chemical Waste Treatment Centre • Drip tray and chemical spillage kit will be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to frontline workers for the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative

				species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Restrict construction area to minimize the impact on existing retained trees
EIA 3.9.1; EM&A Log 2.2	Construction of footings	Kong Nga Po Site	Air	• Regular inspection and maintenance of plant and equipment in good condition • Regularly clean up stockpiles and debris to avoid accumulation of materials • Dusty materials exceeding 20 bags shall be stored in area sheltered on top and the three sides or covered entirely by impervious sheeting.
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition • Enclose the noisy part of machineries with noise enclosure • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out

EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	- Wheels of all vehicles and plants will be cleaned before leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged. - Designated location for residual concrete washout - Provide wastewater treatment facilities prior to discharge of wastewater
EIA 7.5.1.4; EM&A Log			Chemical Waste	Drip tray and chemical spillage kit shall be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	- Provide training to frontline workers for the conservative species - Provision of protective fence for the conservative species - Regular inspection for concerned vegetation and conservative species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	- Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement - Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts
EIA 3.9.1; EM&A Log 2.2	Construction of substructure and	Kong Nga Po Site	Air	- Regular inspection and maintenance of plant and equipment in good condition - Regularly clean up stockpiles and debris to avoid

	superstructure			accumulation of materials Dusty materials exceeding 20 bags shall be stored in area sheltered on top and the three sides or covered entirely by impervious sheeting.
EIA 4.4.6; EM&A Log 3.2			Noise Control	- Regular inspection and maintenance of plant & equipment in good condition - Enclose the noisy part of machineries with noise enclosure - Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	- Valid construction noise permit should be obtained and displayed on site - In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	- Cover the stockpiles of construction materials to reduce the potential for water pollution - Provide wastewater treatment facilities prior to discharge of wastewater - Wastewater generated from surface runoff shall be treated prior to discharge - Manholes should be temporarily sealed to prevent silt, construction materials or debris from entering the drainage system.

EIA 7.5.1.1; EM&A Log 6.2			Waste Management	• Cover stockpiles of C&D materials by impervious sheets to avoid wind-blown dust. • Spray water on all dusty materials including C&D materials immediately prior to any loading transfer operation • Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Drip tray and chemical spillage kit shall be provided on site
EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to frontline workers for the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative species
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts
EIA 3.9.1; EM&A Log 2.2	Construction of footbridge	Kong Nga Po Site	Air	• Regular inspection and maintenance of plant and equipment in good condition

				• Water spraying during loading and unloading of excavated materials • Regularly clean up stockpiles and debris to avoid accumulation of materials • Dusty materials exceeding 20 bags shall be stored in area sheltered on top and the three sides or covered entirely by impervious sheeting.
EIA 4.4.6; EM&A Log 3.2			Noise Control	• Regular inspection and maintenance of plant & equipment in good condition • Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	• Valid construction noise permit should be obtained and displayed on site • In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	• Cover the stockpiles of construction materials to reduce the potential for water pollution • Provide wastewater treatment facilities prior to discharge of wastewater • Wastewater generated from surface runoff shall be treated prior to discharge
EIA 7.5.1.1;			Waste	• Cover stockpiles of C&D materials by impervious sheets to

EM&A Log 6.2			Management	avoid wind-blown dust. • Spray water on all dusty materials including C&D materials immediately prior to any loading transfer operation • Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal
EIA 7.5.1.4; EM&A Log 6.2			Chemical Waste	• Drip tray and chemical spillage kit shall be provided on site
EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts
EIA 3.9.1; EM&A Log 2.2	Backfilling	Kong Nga Po Site	Air	• Deploy water bowser for regular water spraying to enhance dust suppression • Manual water spraying for dusty operation where inaccessible by water bowser • Speed control of site transportation • Stockpile of dusty materials will be covered by tarpaulin sheets to avoid wind-blown dust • Vehicles used for transporting dusty materials/spoils will be covered by mechanical cover before leaving the site

				Wheel washing facilities will be provided and cleaning the wheel of all vehicles before leaving the site
EIA 4.4.6; EM&A Log 3.2			Noise Control	- Regular inspection and maintenance of plant & equipment in good condition - Enclose the noisy part of machineries with noise enclosure - Adopt of Quality Powered Mechanical Equipment (QPME) if possible
			Working in Restricted Hours	- Valid construction noise permit should be obtained and displayed on site - In case of non-compliance with the construction noise criteria, more frequent monitoring and action should be carried out
EIA 5.6.1.2; EM&A Log 4.2			Water Pollution Control	- Cover the stockpiles of construction materials to reduce the potential for water pollution - Provide wastewater treatment facilities prior to discharge of wastewater - Regular inspection and maintenance of wastewater treatment facilities - Wastewater pumped out of the excavation areas will be treated to remove suspended solids prior to discharge - Hard paving or well-compact of main haul road to minimize washout of soil - Wheels of all vehicles and plants will be cleaned before

				leaving the work areas to remove sediment, soil and debris from the tracked. The wastewater will be treated and reused on site or discharged.
EIA 7.5.1.1 & 7.5.1.2; EM&A Log 6.2			Waste Generation	• Training of site personnel in proper waste management and chemical handling procedures • Proper storage and sorting of excavated inert materials to maximize on site reuse for backfilling • Surplus inert C&D materials will be disposed of at designated Government's PFRF or reuse at other contracts.

**EIA Ref/ EM&A Log/ Design Document Ref*

***Details of equipment, vehicles, plants, processes, technologies for the construction method*

Design and Construction of Kong Nga Po Police Training Facilities
Proactive Environmental Protection Proforma

Working Period: July 2025

Ref*	Proposed Construction Method	Location/Working Period	Anticipated Major Impacts	Recommended Mitigation Measures	Photo Records (Partial)
EIA 3.9.1; EM&A Log 2.2	Open cut excavation	Kong Nga Po Site	Dust impact	- Manual water spraying for dust suppression - Regular inspection and maintenance of plant and equipment in good condition - Cover stockpile with impervious sheets or grout - Provide wheel washing facility at site entrance	 By subcontractor at KNP site

					 28.07.2025 By subcontractor at KNP site  11.07.2025 By subcontractor at KNP site
--	--	--	--	--	---

EIA 4.4.6; EM&A Log 3.2			Noise	• Regular inspection and maintenance of plant & equipment in good condition • Deploy Quality Powered Mechanical Equipment (QPME) if possible • Valid construction noise permit should be displayed at site entrance.	 By main contractor at KNP site  By main contractor at KNP site
--	--	--	--------------	--	---

EIA 9.7.1 and EM&A Log 8.3			Ecology Concern	• Provide training to workers about the conservative species • Provision of protective fence for the conservative species • Regular inspection for concerned vegetation and conservative species	 12.07.2025 By main contractor at KNP site  2025/7/21 By subcontractor at KNP site
---	--	--	------------------------	--	--

EIA 3.9.1; EM&A Log 2.2	Soil Removal	Kong Nga Po Site	Air	• Deploy water bowser for regular water spraying to enhance dust suppression • Cover dusty materials with impervious sheets • Exposed slopes covered with waterproof layers such as tarpaulin sheets or grout to reduce the potential for sediment laden runoff entering the drainage system. • The speed of the trucks within the site should be controlled to about 10km/hour in order to reduce adverse dust impacts and secure the safe movement around the site.	 08.07.2025 By main contractor at KNP site  07.07.2025 By subcontractor at KNP site
--	---------------------	-------------------------	------------	--	---

EIA 4.4.6; EM&A Log 3.2			Noise	- Regular inspection and maintenance of plant & equipment in good condition - Deploy Quality Powered Mechanical Equipment (QPME) if possible	 By main contractor at KNP site
EIA 5.6.1.2 and EM&A Log 4.2			Water Quality	- Cover exposed slopes with impervious sheets or cement grout. - Wastewater pumped out of the excavation areas shall be treated to remove suspended solid prior to discharge. - Provide desilting/ sedimentation devices for wastewater treatment prior to discharge.	 By main contractor at KNP site

- Provide drip tray to prevent spillage of fuels



By main contractor at KNP site



By main contractor at KNP site

EIA Table 10.11; EM&A Table 9.1			Landscape and Visual Impact	• Preservation of existing trees will be undertaken in accordance with DEVB TC(W) 7/2015 and Guidelines for Tree Risk Assessment and Management Arrangement • Implement temporary traffic arrangement which control construction area to minimize landscape and visual impacts • Minimize visual impact during construction stage. Site office not visually prominent from public room and surrounding • Planting will take place as soon the planting area is installed with	 By main contractor at KNP site
--	--	--	------------------------------------	--	--

				subsoil drainage Decorative hoarding is provided	
EIA 3.9.1; EM&A Log 2.2	Construction of footings, substructure and superstructure	Kong Nga Po Site	Air	- Cover dusty materials with impervious sheets - Exposed slopes covered with waterproof layers such as tarpaulin sheets or grout to reduce the potential for sediment laden runoff entering the drainage system. - Provide wheel washing facility at site entrance	 By subcontractor at KNP site  By subcontractor at KNP site

					 28.07.2025 By main contractor at KNP site  07.07.2025 By main contractor at KNP site
--	--	--	--	--	---

EIA 4.4.6; EM&A Log 3.2			Noise	Valid construction noise permit should be obtained and displayed on site	 29.07.2025 By main contractor at KNP site
EIA 5.6.1.3 and EM&A Log 4.2			Water Quality	- Surface water from concrete batching areas and the rest of the site should be separated as far as possible. - Temporary drainage is free of obstruction. - Gullies are sealed to prevent silt or debris from entering the drainage system.	 29.07.2025 By subcontractor at KNP site

					 29.07.2025 By main contractor at KNP site  04.07.2025 By main contractor at KNP site
--	--	--	--	--	---

EIA 7.5.1.2 and EM&A Log 6.2			Waste Management	• Segregation and storage of different types of waste in different containers or skips or stockpiles to enhance reuse or recycling of materials and their proper disposal • Sort non-inert C&D materials to recover any recyclable portions	 By main contractor at KNP site
------------------------------------	--	--	---------------------	--	---

APPENDIX B
ACTION AND LIMIT LEVELS

Appendix B - Action and Limit Levels**Table B-1 Action and Limit Levels for 1-hour TSP**

Monitoring station	Action Level (ug/m ³)	Limit Level (ug/m ³)
AM1	308	500
AM2	311	

Table B-2 Action and Limit Levels for Construction Noise

Time Period	Action Level	Limit Level
0700-1900 hours on normal weekdays	When one documented complaint is received	75 dB(A)

Noted:

If works are to be carried during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.

APPENDIX C
COPIES OF CALIBRATION
CERTIFCATES



東恒測試顧問有限公司

AQUALITY TESTCONSULT LIMITED

香港新界粉嶺坪輦路啟芳園11A&B號

NO.11A&B, KAI FONG GARDEN, PING CHE ROAD, FANLING, N.T., HONG KONG

TEL : 852-2674-0478

FAX : 852-2674-1177

EMAIL : main.aqtl@gmail.com

WEBSITE : www.aqtlgroup.com

CERTIFICATE OF CALIBRATION

Ka Shing Facility Management Ltd. Flat C, 14/F, Jing Ho Industrial Building, 78- 84 Wang Lung Street, Tsuen Wan, N.T.	Test Report No.	250512MCA-1P
	Date of Issue	12-May-25
	Date of Testing	11-May-25
	Page	1 of 1

Item for Calibration

Description : Laser Dust Monitor

Manufacturer : Met One Instruments, Inc.

Model No. : AEROCET-831

Serial No. : D12641

Standard Equipment

Description : High Volume Sampler / Calibration Orifice

Manufacturer : Tisch Environmental, Inc.

Model No. : TE-5170 / TE-5025A

Serial No. : 3476 / 4088

Last Calibration : 24-AUG-24 / 15-OCT-24

Date	Time	Mean Temp (°C)	Mean Pressure (hPa)	Concentration Standard Equipment (mg/m3)	Concentration Calibrated Equipment (mg/m3)
11-May-25	19:00	24.8	1010.1	0.0612	0.0627
11-May-25	20:05	24.8	1010.1	0.0560	0.0563
11-May-25	21:10	24.8	1010.1	0.0582	0.0598


By Linear Regression of Y or X

Slope : 1.2140

Correlation Coefficient : 0.9820

K-Factor : 0.9817

Validity of Calibration : 10-May-26

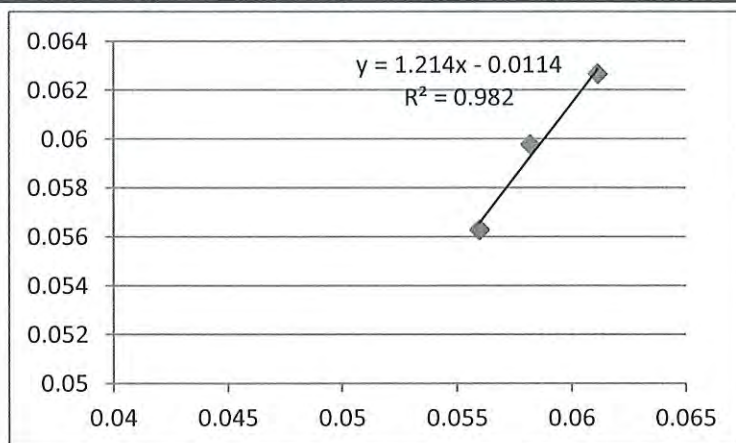

Recorded by : Jessica Liu

Signature:

Date: 11-May-25

Checked by : S Tang

Signature:

Date: 11-May-25

Certificate of Calibration

Calibration Certification Information

Cal. Date: October 15, 2024 Rootsmeter S/N: 438320 Ta: 294 °K
Operator: Jim Tisch Pa: 752.1 mm Hg
Calibration Model #: TE-5025A Calibrator S/N: 4088

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4330	3.2	2.00
2	3	4	1	1.0260	6.4	4.00
3	5	6	1	0.9190	7.9	5.00
4	7	8	1	0.8740	8.8	5.50
5	9	10	1	0.7230	12.7	8.00

Data Tabulation

Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
0.9988	0.6970	1.4164	0.9957	0.6949	0.8842
0.9945	0.9693	2.0031	0.9915	0.9664	1.2505
0.9925	1.0800	2.2395	0.9895	1.0767	1.3980
0.9913	1.1342	2.3488	0.9883	1.1308	1.4663
0.9861	1.3639	2.8328	0.9831	1.3598	1.7684
QSTD	m=	2.12356	QA	m=	1.32974
	b=	-0.05931		b=	-0.03702
	r=	0.99996		r=	0.99996

Calculations

Vstd=	$\Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta)$	Va=	$\Delta Vol((Pa-\Delta P)/Pa)$
Qstd=	$Vstd/\Delta Time$	Qa=	$Va/\Delta Time$
For subsequent flow rate calculations:			
Qstd=	$1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa=	$1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions

Tstd: 298.15 °K

Pstd: 760 mm Hg

Key

ΔH: calibrator manometer reading (in H2O)

ΔP: rootsmeter manometer reading (mm Hg)

Ta: actual absolute temperature (°K)

Pa: actual barometric pressure (mm Hg)

b: intercept

m: slope

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Calibration Certificate No.: CC0072503

Information provided by customer

Customer: Ka Shing Facility Management Ltd
Address: Unit 2, 13/F, Kai Yue Commercial Building, 2C Argyle St, Mong Kok, Kowloon

Equipment Identification provided by customer

Equipment Description	Manufacturer	Model No.	Serial No.	Assigned equipment No.
Aerosol Mass Monitor	Met One Instrument	AEROCET 831	D12641	N/A

Certificate Information

Date of Receipt:	5 March 2025	Calibration Condition:	22.8°C, 57%RH, 1006hPa
Date of Calibration:	13 March 2025	Adjustment:	N/A
Recommended Next Cal. Date:	N/A	Appearance:	Good
Calibration Procedure:	ISO 21501-4:2018	Remark:	N/A

Reference Equipment Identification

Equipment Description	Model	Serial No.	Expiration Date
Aerosol Monitor	8534	8534182605	6 December 2026

**Result of Calibration
Indication**

Dust	Reference Setting (mg/m ³)	Measured reading (mg/m ³)	Error (%)	Uncertainty (%FS)	Technical Requirement	Technical Reference Doc.
TSP	0.099	0.0964	-2.6	14.0	± 10%	Mfr's Spec.
TSP	0.202	0.1951	-3.4	14.0	± 10%	Mfr's Spec.
TSP	0.300	0.2923	-2.6	14.0	± 10%	Mfr's Spec.

CT-GAS-01

- Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.
- Note2: The standard (s) and instrument used in the calibration are traceable to national or international recognized standard and are calibrated on a schedule to maintain the accuracy and good condition.
- Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.
- Note4: The result shows in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.
- Note5: Calibration item/ parameter marked with * is out of scope of Cal Lab Limited (A2LA 3815.01).

Calibrated By:



Wing Cheng

Checked and Approved By:



Warren Yeung

Company Chop:



Certificate Issue Date: 19 March 2025

CT-BEG-04

*** End of Certificate ***

- The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
- The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0072503

Page 1 of 1



Cal Lab Limited 校正實驗室有限公司

Room 2103, Technology Plaza, 29-35 Sha Tsui Road,

Tsuen Wan, NT, Hong Kong

Tel: +852 25680106 Email: info@callab.com.hk

Fax: +852 30116194 Website: www.callab.com.hk

Calibration Certificate No.: CC0782503

Information provided by customer

Customer: Cal Lab Limited

Address: Room 2103, Technology Plaza, 29-35 Sha Tsui Road, Tsuen Wan, NT, Hong Kong

Equipment Identification provided by customer

Equipment Description	Manufacturer	Model No.	Serial No.	Assigned equipment No.
High Volume Sampler	Qingdao Hengyuan	HY-1000E	1406071	N/A

Certificate Information


Date of Receipt:	18 March 2025	Calibration Condition:	24.1°C, 52%RH, 1004hPa
Date of Calibration:	18 March 2025	Adjustment:	N/A
Recommended Next Cal. Date:	N/A	Appearance:	Good
Calibration Procedure:	Performance check	Remark:	N/A

Reference Equipment Identification

Equipment Description	Model	Serial No.	Expiration Date
Calibration Orifices	TE-5025	4088	15 October 2025

Result of Calibration

Test	H ₂ O (in)	Q _{std} (m ³ /min)	I (chart)	IC (corrected)
1	5.0	1.586	49.0	48.76
2	4.5	1.536	47.0	46.77
3	4.0	1.443	45.0	44.78
4	3.5	1.318	40.0	39.80
5	2.5	1.025	34.0	33.83

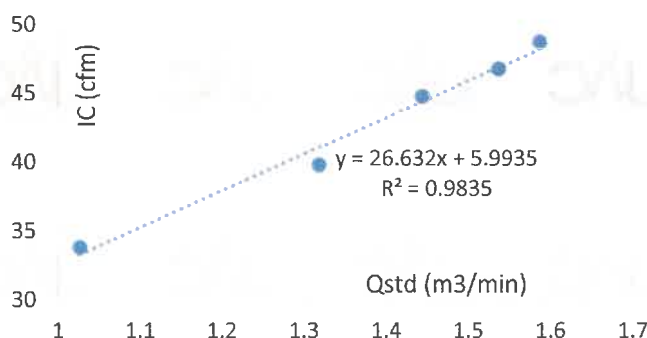

- Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.
- Note2: The standard (s) and instrument used in the calibration are traceable to national or international recognized standard and are calibrated on a schedule to maintain the accuracy and good condition.
- Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.
- Note4: The result shows in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.
- Note5: Calibration item/ parameter marked with * is out of scope of Cal Lab Limited (A2LA 3815.01).

Calibrated By:

Wing Cheng

Checked and Approved By:

Warren Yeung

Company Chop:



Certificate Issue Date: 19 March 2025

CT-BEG-04

*** End of Certificate ***

- The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
- The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0782503

Page 1 of 1



Cal Lab Limited 校正實驗室有限公司

Room 2103, Technology Plaza, 29-35 Sha Tsui Road,

Tsuen Wan, NT, Hong Kong

Tel: +852 25680106 Email: info@callab.com.hk

Fax: +852 30116194 Website: www.callab.com.hk

Appendix of CC0782503

Calibration Certificate of Calibration Orifices



RECALIBRATION
DUE DATE:
October 15, 2025

Certificate of Calibration

Calibration Certification Information			
Cal. Date:	October 15, 2024	Rootsmer S/N:	438320
Operator:	Jim Tisch	Ta:	29.4 °K
Calibration Model #:	TE-5025A	Pa:	752.2 mm Hg
		Calibrator S/N:	4088

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4330	3.2	2.00
2	3	4	1	1.0260	6.4	4.00
3	5	6	1	0.9190	7.9	5.00
4	7	8	1	0.8740	8.8	5.50
5	9	10	1	0.7230	12.7	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
0.9988	0.6970	1.4164	0.9957	0.6949	0.8842
0.9945	0.9693	2.0031	0.9915	0.9664	1.2505
0.9925	1.0800	2.2395	0.9895	1.0767	1.3980
0.9913	1.1342	2.3488	0.9883	1.1308	1.4663
0.9861	1.3639	2.8328	0.9831	1.3598	1.7684
QSTD		m= 2.12356	QA		m= 1.32974
		b= 0.05931			b= 0.03702
		r= 0.99996			r= 0.99996

Calculations	
Vstd= ΔVol[(Pa-ΔP)/Pstd](Tstd/Ta)	Va= ΔVol[(Pa-ΔP)/Pa]
Qstd= Vstd/ΔTime	Qa= Va/ΔTime
For subsequent flow rate calculations:	
Qstd= 1/m $\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) b$	Qa= 1/m $\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) b$

Standard Conditions	
Tstd	298.15 °K
Pstd	760 mm Hg
Key	
ΔH	calibrator manometer reading (in H2O)
ΔP	rootsmeter manometer reading (mm Hg)
Ta	actual absolute temperature (°K)
Pa	actual barometric pressure (mm Hg)
b	intercept
m	slope

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.
45 South Miami Avenue
Cleveland, OH 44102

www.tisch-env.com
TOLL FREE (877)263-7610
FAX: (513)467-9009

*** End of Appendix ***

1. The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
2. The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0782503
Page 1 of 1

Calibration Certificate No.: CC0792503

Information provided by customer

Customer: Ka Shing Facility Management Ltd
Address: Unit 2, 13/F, Kai Yue Commercial Building, 2C Argyle St, Mong Kok, Kowloon

Equipment Identification provided by customer

Equipment Description	Manufacturer	Model No.	Serial No.	Assigned equipment No.
Aerosol Mass Monitor	Met One Instrument	AEROCET 831	D12641	N/A

Certificate Information


Date of Receipt:	5 March 2025	Calibration Condition:	23.2°C, 48%RH, 1004hPa
Date of Calibration:	19 March 2025	Adjustment:	N/A
Recommended Next Cal. Date:	N/A	Appearance:	Good
Calibration Procedure:	In-House Method	Remark:	N/A

Reference Equipment Identification

Equipment Description	Model	Serial No.	Expiration Date
High Volume Sampler	HY-1000E	1406071	17 March 2026

**Result of Calibration
Indication**

Trial	1	2	3	4	5
Equipment	Measurement result (µg/m³)				
High Volume Sampler (HVS)	39.8	32.2	25.4	16.2	10.7
Unit Under Test (UUT)	37.4	31.9	26.0	15.5	9.9

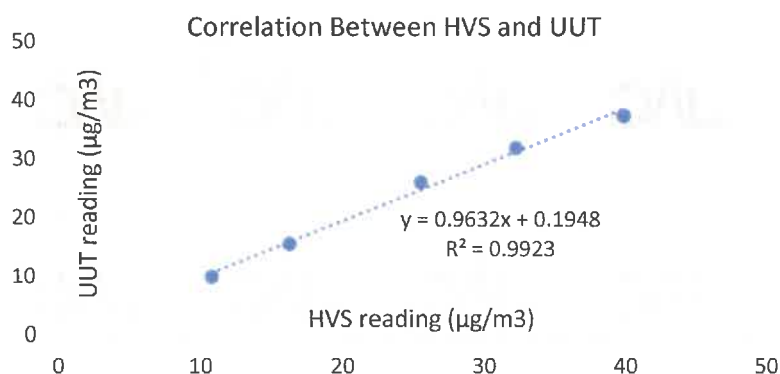

- Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.
- Note2: The standard (s) and instrument used in the calibration are traceable to national or international recognized standard and are calibrated on a schedule to maintain the accuracy and good condition.
- Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.
- Note4: The result shows in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.
- Note5: Calibration item/ parameter marked with * is out of scope of Cal Lab Limited (A2LA 3815.01).

Calibrated By:



Wing Cheng

Checked and Approved By:



Warren Yeung

Company Chop:



Certificate Issue Date: 19 March 2025

CT-BEG-04

***** End of Certificate *****

- The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
- The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0792503
Page 1 of 1



東恒測試顧問有限公司

AQUALITY TESTCONSULT LIMITED

香港新界粉嶺坪輦路啟芳園11A&B號

NO.11A&B, KAI FONG GARDEN, PING CHE ROAD, FANLING, N.T., HONG KONG

TEL : 852-2674-0478

FAX : 852-2674-1177

EMAIL : main.aqtl@gmail.com

WEBSITE : www.aqtlgroup.com

CERTIFICATE OF CALIBRATION

Report Number : 250315MCA-1P
Date of Report : 15-Mar-25
Page Number : 1 of 2
Customer * : Ka Shing Facility Management Ltd.
Customer Address* : Flat C, 14/F, Jing Ho Industrious Building, 78-84 Wang Lung Street, Tsuen Wan, N.T.
Customers Ref. * : K194

Item Under Calibration (IUC)*

Equipment No. : 224534
Manufacturer : Met One Instruments, Inc.
Model No. : AEROCET-831
Serial No. : E11304
Scale Division : 0.001 mg/m³
Range : 0.001 to 1 mg/m³
Condition of Item : Normal

Date Item Received : 14-Mar-25
Date Calibrated : 14-Mar-25
Calibration Location : AQuality Calibration Lab.
Date of Next Calibration : 13-Mar-26
Calibrated By : Jessica Liu

Test Environment

Ambient Temperature : 20.1 °C to 23.5 °C
Relative Humidity : 70 % to 75 %

Calibration Results

Reference True Reading (mg/m ³)	Average IUC Reading (mg/m ³)	Correction (mg/m ³)	Error of IUC Reading (%)	Coverage Factor K
0.215	0.226	0.011	4.9%	2.0
0.481	0.491	0.010	2.1%	2.0
0.830	0.837	0.007	0.9%	2.0

Remarks :

1. * Denotes information supplied by customer.
2. The results relate only to the items calibrated.
3. The results apply to the items as received.
4. Correction = Average of (Ref reading - IUC reading)
5. The technical requirement of laser dust meter. +/- 20% error for the particles concentration.

Approved by: _____

LEE Mei Yee, Julia
Managing Director

The results shown in this certificate are metrologically traceable to the International System of Units (SI) or recognised measurement standards.

The certificate shall not be reproduced except in full without approval of the laboratory.



東恒測試顧問有限公司

AQUALITY TESTCONSULT LIMITED

香港新界粉嶺坪輦路啟芳園11A&B號

NO.11A&B, KAI FONG GARDEN, PING CHE ROAD, FANLING, N.T., HONG KONG

TEL : 852-2674-0478

FAX : 852-2674-1177

EMAIL : main.aqtl@gmail.com

WEBSITE : www.aqtlgroup.com

CERTIFICATE OF CALIBRATION

Report Number : 250315MCA-1P
Date of Report : 15-Mar-25
Page Number : 2 of 2
Customer * : Ka Shing Facility Management Ltd.
Customers Ref. * : K194

Details of Calibration

1. The calibration was performed in accordance with AQuality Testconsult Procedure Number ENV-L-003 (in-house method), by comparison with the laboratory's reference equipment which have traceable international standards of measurement.
2. The item under calibration (IUC) was allowed to stabilize in the laboratory for 0.25 hour before commencement of calibration.
3. A set of readings were made at each calibration concentration. The values quoted in the results are the average of each set of readings.
4. The values given in this calibration certificate only relate to the values measured at the time of calibration. Any uncertainties quoted do not include allowance for the capability of any other laboratory to repeat the measurement. The uncertainty quoted relate only to item at time of calibration. AQuality Testconsult Limited is not liable for any loss or damage resulting from the use of this equipment.
5. The identification, calibration certificate numbers for the reference equipment used were as follows :

<u>Equipment Number</u>	<u>Certificate Number</u>	<u>Description</u>
CH-LDM-1	CC1592412	粉尘测试仪

6. Copies of the Calibration certificates of the reference equipment used in this calibration may be obtained from AQuality Testconsult Limited, if necessary.

- End of Report -



東恒測試顧問有限公司

AQUALITY TESTCONSULT LIMITED

香港新界粉嶺坪輦路啟芳園11A&11B號

No. 11A&11B, KAI FONG GARDEN, PING CHE ROAD, FANLING, N.T., HONG KONG

TEL : 852-3582-9589

FAX : 852-2674-1177

EMAIL : cal.aqtl@gmail.com

WEBSITE: www.aqtlgroup.com

CERTIFICATE OF CALIBRATION

Ka Shing Facility Management Ltd. Flat C, 14/F, Jing Ho Industrial Building, 78-84 Wang Lung Street, Tsuen Wan, N.T.	Test Report No.	250315MCA-1P
	Date of Issue	15-Mar-25
	Date of Testing	14-Mar-25
	Page	1 of 1

Item for Calibration

Description : Laser Dust Monitor

Manufacturer : Met One Instruments, Inc.

Model No. : AEROCET-831

Serial No. : E11304

Standard Equipment

Description : High Volume Sampler / Calibration Orifice

Manufacturer : Tisch Environmental, Inc.

Model No. : TE-5170 / TE-5025A

Serial No. : 3476 / 4088

Last Calibration : 24-AUG-24 / 15-OCT-24

Date	Time	Mean Temp (°C)	Mean Pressure (hPa)	Concentration Standard Equipment (mg/m3)	Concentration Calibrated Equipment (mg/m3)
14-Mar-25	19:00	20.5	1014.4	0.0610	0.0620
14-Mar-25	20:05	20.5	1014.4	0.0581	0.0573
14-Mar-25	21:10	20.5	1014.4	0.0585	0.0577


By Linear Regression of Y or X

Slope : 1.6038

Correlation Coefficient : 0.9982

K-Factor : 1.0037

Validity of Calibration : 13-Mar-26

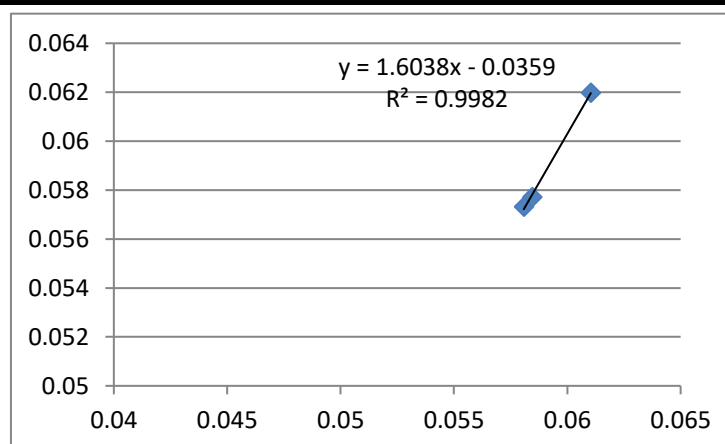

Recorded by : Jessica Liu

Signature:

Date: 14-Mar-25

Checked by : S Tang

Signature:

Date: 14-Mar-25

Certificate of Calibration

Calibration Certification Information

Cal. Date: October 15, 2024 Rootsmeter S/N: 438320 Ta: 294 °K
Operator: Jim Tisch Pa: 752.1 mm Hg
Calibration Model #: TE-5025A Calibrator S/N: 4088

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4330	3.2	2.00
2	3	4	1	1.0260	6.4	4.00
3	5	6	1	0.9190	7.9	5.00
4	7	8	1	0.8740	8.8	5.50
5	9	10	1	0.7230	12.7	8.00

Data Tabulation

Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
0.9988	0.6970	1.4164	0.9957	0.6949	0.8842
0.9945	0.9693	2.0031	0.9915	0.9664	1.2505
0.9925	1.0800	2.2395	0.9895	1.0767	1.3980
0.9913	1.1342	2.3488	0.9883	1.1308	1.4663
0.9861	1.3639	2.8328	0.9831	1.3598	1.7684
QSTD	m=	2.12356	QA	m=	1.32974
	b=	-0.05931		b=	-0.03702
	r=	0.99996		r=	0.99996

Calculations

Vstd=	$\Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta)$	Va=	$\Delta Vol((Pa-\Delta P)/Pa)$
Qstd=	$Vstd/\Delta Time$	Qa=	$Va/\Delta Time$
For subsequent flow rate calculations:			
Qstd=	$1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa=	$1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions

Tstd: 298.15 °K

Pstd: 760 mm Hg

Key

ΔH: calibrator manometer reading (in H2O)

ΔP: rootsmeter manometer reading (mm Hg)

Ta: actual absolute temperature (°K)

Pa: actual barometric pressure (mm Hg)

b: intercept

m: slope

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

FAQ / Information

Mutual Recognition Arrangements (MRA) / Multilateral Recognition Arrangements (MLA)

Mutual Recognition Arrangement (MRA) Partners for HOKLAS ^

Every effort is made to promote acceptance of test data from accredited laboratories, both internationally and locally. HKAS has concluded mutual recognition arrangements with accreditation bodies listed below by being one of the signatories of the [International Laboratory Accreditation Cooperation Mutual Recognition Arrangement \(ILAC MRA\)](#) and the [Asia Pacific Accreditation Cooperation Mutual Recognition Arrangement \(APAC MRA\)](#) for testing, calibration, medical testing, Proficiency Testing Providers (PTP) and Reference Material Producers (RMP). Click [here](#) to view the up-to-date signatories of ILAC and [here](#) to access the up-to-date signatories of APAC.

Visitors checking the names, logos and accreditation symbols shown on an endorsed certificate or report should note that some of our MRA partners may have their names, logos or accreditation symbols changed recently and test reports or certificates endorsed by displaying their old accreditation symbols may still be valid during the change-over period. For details, please visit their websites or contact them directly.

» [Mutual Recognition Arrangement \(MRA\) Partners for HOKLAS](#)

HKAS MRA partners will recognise HOKLAS endorsed test certificates as having the same technical validity as certificates endorsed by their respective schemes.

Multilateral Recognition Arrangements (MLA) for HKCAS v

Mutual Recognition Arrangement (MRA) Partners for HKIAS v

 back

Hong Kong Laboratory Accreditation Scheme (HOKLAS) - Mutual Recognition Arrangement (MRA) Partners

Economy	Logo	Name of Partner	URL	Test Area
United Kingdom of Great Britain and Northern Ireland		United Kingdom Accreditation Service (UKAS)	http://www.ukas.com	Calibration, Medical Testing, Non-medical Testing, Proficiency Testing Provider, Reference Material Producer
United States of America		AIHA Laboratory Accreditation Programs, LLC (AIHA-LAP, LLC)	http://www.aihaaccreditedlabs.org/	Non-medical Testing
United States of America		American Association for Laboratory Accreditation (A2LA)	http://www.a2la.org	Calibration, Medical Testing, Non-medical Testing, Proficiency Testing Provider, Reference Material Producer
United States of America		ANSI National Accreditation Board (ANAB)	http://www.anab.org/	Calibration, Medical Testing, Non-medical Testing, Proficiency Testing Provider, Reference Material Producer
United States of America		International Accreditation Service Inc. (IAS)	http://www.iasonline.org/	Calibration, Medical Testing, Non-medical Testing
United States of America		National Accreditation Center LLC (NAC)		Calibration, Non-medical Testing
United States of America		National Voluntary Laboratory Accreditation Program (NVLAP)	http://www.nist.gov/nvlap	Calibration, Non-medical Testing



INTERNATIONAL
ACCREDITATION
SERVICE®

CERTIFICATE OF ACCREDITATION

This is to attest that

AQUALITY TESTCONSULT LIMITED

11A&B, KAI FONG GARDEN, PING CHE ROAD
FANLING, HONG KONG

Calibration Laboratory CL-207

has met the requirements of AC204, *IAS Accreditation Criteria for Calibration Laboratories*, and has demonstrated compliance with ISO/IEC Standard 17025:2017, *General requirements for the competence of testing and calibration laboratories*. This organization is accredited to provide the services specified in the scope of accreditation.

Effective Date February 19, 2024



A handwritten signature in black ink, reading "Raj Nathan".

President

Visit www.iasonline.org for current accreditation information.

SCOPE OF ACCREDITATION

International Accreditation Service, Inc.

3060 Saturn Street, Suite 100, Brea, California 92821, U.S.A. | www.iasonline.org

MEASURED QUANTITY or DEVICE TYPE CALIBRATED	RANGE	UNCERTAINTY ^{1,2} (±)	CALIBRATION PROCEDURE AND/OR STANDARD EQUIPMENT USED
			dimensional requirements as specified in BS 1881- Part 105: 1984)
Test Sieve ³	4 mm to 50 mm	50 µm	Reference Caliper by direct measurement as per BS 410 : 1986
Elongation Gauge ³	Gap between Pins of Gauge 10 mm to 100 mm	0.29 mm	Reference Caliper by direct measurement (Verification in accordance with in-house method for the dimensional requirements as specified in BS 812- Part 1:1975; BS 812- Part 105.2: 1990)
Flakiness Gauge ³	Length of Slot of Gauge 4.9 mm to 33.9 mm	0.06 mm	Reference Caliper by direct measurement ((Verification in accordance with in-house method for the dimensional requirements as specified in BS 812- Part 1:1975; BS 812- Part105.1:1985; BS 812- Part105.1:1989)
Riffle Box ³	Width 6 mm to 100 mm	0.06 mm	Reference Caliper by direct measurement (Verification in accordance with in-house method for the dimensional requirements as specified in BS 812- Part 1:1975)
Mechanical			
Force Measuring Machine ³ (Compression Mode)	1 kN to 3000 kN	0.4 %	Reference Load cell by direct measurement (Based on BS 1610: Part 1:1985; BS 1610: Part 1:1992; BS EN ISO 12390-4:2000 Annex B; BS EN 12390-4: 2019; BS EN ISO 7500-1:2004, BS EN ISO 7500-1: 2015, BS EN ISO 7500-1: 2018)
Laser Dust Meter ³	Dust particles 0.1 mg/m ³ to 3 mg/m ³ 3 mg/m ³ to 8 mg/m ³	0.006 mg/m ³ 0.39 mg/m ³	By comparison method by using reference laser dust meter (Based on ISO 12103-1:2016)
Rebound Hammer ³	80 unit (hardness)	1.6 rebound count	Reference Rebound count by comparison method (Based on BS1881: Part 202:1986; BS EN 12504-2:2001; BS EN

Certificate of Calibration

Certificate No. ATS25-008-CC001

Customer: Ka Shing Facilities Management Limited

Flat C, 14/F., Jing Ho Industrial Building,
78-84 Wing Lung Street, Tsuen Wan,
N.T., Hong Kong

Unit-under-test (UUT):

Description:	Sound Analyzer	,	Microphone	,	Pre-amplifier
Manufacturer:	Rion				
Type No.:	NL-53	,	UC-59	,	NH-25
Serial No.:	01130782	,	24906	,	33673

Conditions during calibration:

Temperature:	23°C
Relative Humidity:	65%

Test Specifications: Calibration Check

Date of Calibration: 23 January 2025

Test Results: All calibration points are within manufacturer's specification.

Certified by:



Mr. Ching Mau LAM / Quality Manager
MIOA, MHKIOA



Issue Date: 24 January 2025

1. The instrument under test was allowed to stabilize in the laboratory for over 24 hours.
2. Calibration equipment:

Description: Sound Calibrator
Manufacturer & Type: Brüel & Kjær 4231
Serial No.: 2478237
Last Calibration Date: 27 February 2024
Certificate No.: AV240026

The calibration equipment used for calibration is traceable to National Standards via Standards and Calibration Laboratory, the Government of the HKSAR.

3. The Sound Analyzer has been calibrated in accordance with the requirements as specified in IEC 61672-1 Class 1, and vendor specific procedures.
4. The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted, if any, will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. Acoustic Testing Services Limited shall not be liable for any loss or damage resulting from the use of the equipment.
5. Calibration Results

Setting of unit-under-test (UUT)				Applied value		UUT Reading, dB	IEC 61672-1 Class 1 Tolerance Limits, dB	Conclusion
Range, dB	Parameter	Frequency Weighting	Response	Level, dB	Frequency, Hz			
30-130	SPL	A	F	94.00	1000	94.0	± 0.7	PASS
			S			94.0	± 0.7	PASS
			I			94.0	± 0.7	PASS
		C	F			94.0	± 0.7	PASS
			S			94.0	± 0.7	PASS
			I			94.0	± 0.7	PASS
		L	F			94.0	± 0.7	PASS
			S			94.0	± 0.7	PASS
			I			94.0	± 0.7	PASS
		A	F	114.00	1000	114.0	± 0.7	PASS
			S			114.0	± 0.7	PASS
			I			114.0	± 0.7	PASS

All calibration points are within manufacturer's specification.

Certificate of Calibration

Certificate No. ATS25-008-CC002

Customer: **Ka Shing Facility Management Limited**

Flat C, 14/F., Jing Ho Industrial Building,
78-84 Wing Lung Street, Tsuen Wan,
N.T., Hong Kong

Unit-under-test (UUT):

Description:	Sound Level Meter	,	Microphone	,	Pre-amplifier
Manufacturer:	BSWA Technology				
Type No.:	BSWA 308	,	231	,	MA231T
Serial No.:	610062	,	591574	,	610373

Conditions during calibration:

Temperature: 26°C


Relative Humidity: 58%

Test Specifications: Calibration Check

Date of calibration: 24 April 2025

Test Results: All calibration points are within manufacturer's specification.

Certified by:


Mr. Ching Mau LAM / Quality Manager
MIOA, MHKIOA



Issue Date: 24 April 2025

1. The instrument under test was allowed to stabilize in the laboratory for over 24 hours.

2. Calibration equipment:

Description:	Multifunction Acoustical Calibrator
Manufacturer & Type:	Brüel & Kjær 4226
Serial No.:	2919264
Last Calibration Date:	11 September 2024
Certificate No.:	2GB24018355-0001

The calibration equipment used for calibration is traceable to National Standards via China Ceprei Laboratory Calibration & Testing Centre. The Multifunction Acoustical Calibrator Brüel & Kjær 4226 has been accredited calibrated by other laboratory and it is found that it cannot fulfill the tolerance limits for frequency at 2000 Hz only, since the Brüel & Kjær 4226 is designed for old year version of IEC 60942 (or JJG 176), but the tolerance limits for frequency as well as sound pressure level, are updated in the most updated version of standards. However, it can still fulfill the requirements for sound pressure level from 31.5 Hz to 8000 Hz.

3. The Sound Analyzer has been calibrated in accordance with the requirements as specified in IEC 61672-1 Class 1, and vendor specific procedures.

4. The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted, if any, will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. Acoustic Testing Services Limited shall not be liable for any loss or damage resulting from the use of the equipment.

5. Calibration Results

5.1 Sound Pressure Level

Reference Sound Pressure Level

Setting of unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672-1 Class 1 Tolerance Limits, dB	Conclusion
Range, dB	Parameter	Time Weighting	Level, dB	Frequency, Hz			
22-136	dBA SPL	Fast	94.0	1000	94.0	± 0.7	PASS

Linearity

Setting of unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672-1 Class 1 Tolerance Limits, dB	Conclusion
Range, dB	Parameter	Time Weighting	Level, dB	Frequency, Hz			
22-136	dBA SPL	Fast	94.0	1000	94.0	± 0.7	PASS
			104.0		104.0	± 0.7	PASS
			114.0		114.0	± 0.7	PASS

Time Weighting

Setting of unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672-1 Class 1 Tolerance Limits, dB	Conclusion
Range, dB	Parameter	Time Weighting	Level, dB	Frequency, Hz			
22-136	dBA SPL	Fast	94.0	1000	94.0	± 0.7	PASS
		Slow			94.0	± 0.7	PASS



Frequency Response

A-weighting:

Setting of unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672-1 Class 1 Tolerance Limits, dB	Conclusion
Range, dB	Parameter	Time Weighting	Level, dB	Frequency, Hz			
22-136	SPL	Fast	54.6	31.5	54.7	± 1.5	PASS
			67.8	63	67.9	± 1.0	PASS
			77.9	125	77.9	± 1.0	PASS
			85.4	250	85.4	± 1.0	PASS
			90.8	500	90.8	± 1.0	PASS
			94.0	1000	94.0	± 0.7	PASS
			95.2	2000	95.0	± 1.0	PASS
			95.0	4000	94.1	± 1.0	PASS
			92.9	8000	90.4	+1.5; -2.5	PASS

C-weighting:

Setting of unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672-1 Class 1 Tolerance Limits, dB	Conclusion
Range, dB	Parameter	Time Weighting	Level, dB	Frequency, Hz			
22-136	SPL	Fast	91.0	31.5	91.1	± 1.5	PASS
			93.2	63	93.3	± 1.0	PASS
			93.8	125	93.9	± 1.0	PASS
			94.0	250	94.0	± 1.0	PASS
			94.0	500	94.0	± 1.0	PASS
			94.0	1000	94.0	± 0.7	PASS
			93.8	2000	93.6	± 1.0	PASS
			93.2	4000	92.4	± 1.0	PASS
			91.0	8000	88.5	+1.5; -2.5	PASS

Linear:

Setting of unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672-1 Class 1 Tolerance Limits, dB	Conclusion
Range, dB	Parameter	Time Weighting	Level, dB	Frequency, Hz			
22-136	SPL	Fast	94.0	31.5	94.2	± 1.5	PASS
				63	94.1	± 1.0	PASS
				125	94.0	± 1.0	PASS
				250	94.0	± 1.0	PASS
				500	94.0	± 1.0	PASS
				1000	94.0	± 0.7	PASS
				2000	93.8	± 1.0	PASS
				4000	93.2	± 1.0	PASS
				8000	91.8	+1.5; -2.5	PASS

All calibration points are within manufacturer's specification.



CERTIFICATE OF CALIBRATION

Class 1



京制01020122号

TYPE: BSWA 308

S/N: 630146

1. APPEARANCE Pass

2. CALIBRATION (sound)

Calibrator: BK4231 Sound Level: 93.8 dB

Frequency: 1000 Hz

Microphone Model / SN: MP231 / 610759

Filter	Nominal[dB]	Indication[dB]	Error[dB]
A	93.8	93.8	0.0
C	93.8	93.8	0.0
Z	93.8	93.8	0.0

3. FREQUENCY WEIGHTINGS (sound & electrical)

Z-weighting (sound & electrical); A/C-weighting (electrical) plus Z-weighting error

Frequency [Hz]	Attenuation[dB]		
	A	C	Z
10	-69.0	-14.3	0.0
20	-50.3	-6.2	0.0
31.5	-39.6	-3.1	0.0
63	-26.2	-0.8	0.0
125	-16.2	-0.2	0.0
250	-8.7	0.0	0.0
500	-3.3	0.0	0.0
1000	0.1	0.1	0.1
2000	1.3	-0.1	0.1
4000	0.7	-1.1	-0.2
8000	-1.1	-3.0	0.5
16000	-13.5	-15.5	-0.6
20000	-28.0	-30.0	-3.1

4. LEVEL LINEARITY (electrical)

Filter=A; Fsin=1kHz

Nominal[dB]	20	21	22	23	24	25	30	40	50	60	70	80	89
Indication[dB]	20.1	21.2	22.2	23.2	24.2	25.2	30.1	39.9	49.9	59.9	70.0	80.0	89.0
Error[dB]	0.1	0.2	0.2	0.2	0.2	0.2	0.1	-0.1	-0.1	-0.1	0.0	0.0	0.0
Nominal[dB]	90	91	92	93	94	95	96	97	98	99	100	110	120
Indication[dB]	90.0	91.0	92.0	93.0	94.0	95.0	96.0	97.0	98.0	99.0	100.0	110.0	120.0
Error[dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Nominal[dB]	129	130	131	132	133	134							
Indication[dB]	129.0	130.0	131.0	132.0	133.0	134.0							
Error[dB]	0.0	0.0	0.0	0.0	0.0	0.0							

5. SELF-GENERATED NOISE LEVEL (sound)

Measured in anechoic chamber with microphone; Backlight Off; Electrical noise please refer user manual

Filter	A	C	Z
Indication[dB]	~ 18	~ 23	~ 31

6. TIME WEIGHTINGS (electrical)

Filter=A; Fsin=4kHz; Steady Level=132dB

Detector	F	S
Rate of Decay[dB/s]	34.7	4.4
Delta of F/S[dB]	0.0	

7. TONEBURST RESPONSE (electrical)

Filter=A; Fsin=4kHz

Steady Level L_A = 132.0 dB

Tone Burst Duration [ms]	Response[dB]		
	$L_{AFmax}-L_A$	$L_{ASmax}-L_A$	$L_{AE}-L_A$
500	-0.1	-4.1	-3.1
200	-1.0	-7.5	-7.1
50	-4.9	-13.2	-13.1
10	-11.2	-20.1	-20.1

8. REPEATED TONEBURST RESPONSE (electrical)

Filter=A; Fsin=4kHz

Steady Level L_A = 132.0 dB

Tone Burst Duration [ms]	Tone Burst Interval [ms]	Response[dB]
		$L_{AeqT}-L_A$
500	2000	-7.0
200	800	-7.1
50	200	-7.1
10	40	-7.1

9. OVERLOAD INDICATION (electrical)

Filter=A; Fsin=1000Hz

Nominal[dB]	Error[dB]			Delta of Positive and Negative[dB]
	Steady	Positive Half Cycle	Negative Half Cycle	
134.1	0.0	0.1	0.1	0.0

10. C-WEIGHTED PEAK SOUND LEVEL (electrical)

Filter=C; Peak; Fsin=500Hz

Steady Signal Level	$(L_{Cpeak}-L_C)$ [dB]		
	Single Cycle	Positive Half Cycle	Negative Half Cycle
4dB Below Top	3.5	2.3	2.3
Middle	3.6	2.3	2.3
1dB Above Floor	3.6	2.4	2.4

CONDITIONS

Temperature	18	°C
Relative Humidity	36	%
Static Pressure	101.4	kPa

TEST EQUIPMENT

Item	Manufacturer	Model	S/N	Description
1	B&K	4231	3008422	Sound Calibrator
2	Agilent	33220A	MY44038043	Signal Generator
3	Agilent	34401A	SG47000236	Digital Multimeter
4	NJZY	ZY5142D	0425	Step Attenuator
5	B&K	4180	2412874	Standard Microphone

TEST PROCEDURES IN ACCORDANCE WITH
IEC 61672-3:2013Class 1 Performance Verified.
Test Qualified.

DATE: 2025.05.13

TEST (sig.):

LZH

APVD (sig.):





CERTIFICATE OF CALIBRATION



京制01020122号

Class 1

TYPE: BSWA 308

S/N: 630178

1. APPEARANCE Pass

2. CALIBRATION (sound)

Calibrator: BK4231 Sound Level: 93.8 dB Frequency: 1000 Hz

Microphone Model / SN: MP231 / 591159

Filter	Nominal[dB]	Indication[dB]	Error[dB]
A	93.8	93.8	0.0
C	93.8	93.8	0.0
Z	93.8	93.8	0.0

3. FREQUENCY WEIGHTINGS (sound & electrical)

Z-weighting (sound & electrical); A/C-weighting (electrical, plus Z-weighting error)

Frequency [Hz]	Attenuation[dB]		
	A	C	Z
10	-69.0	-14.3	0.0
20	-50.3	-6.2	0.0
31.5	-39.5	-3.1	0.0
63	-26.2	-0.8	0.0
125	-16.1	-0.2	0.0
250	-8.6	0.0	0.0
500	-3.3	0.0	0.0
1000	0.1	0.1	0.1
2000	1.4	0.0	0.2
4000	0.8	-1.0	-0.1
8000	-1.4	-3.3	0.1
16000	-12.2	-14.2	0.7
20000	-25.3	-27.3	-0.4

4. LEVEL LINEARITY (electrical)

Filter=A; Fsin=1kHz

Nominal[dB]	20	21	22	23	24	25	30	40	50	60	70	80	89
Indication[dB]	19.9	20.9	21.9	22.9	23.9	24.9	30.0	39.8	49.8	59.9	69.9	79.9	88.9
Error[dB]	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	0.0	-0.2	-0.2	-0.1	-0.1	-0.1	-0.1
Nominal[dB]	90	91	92	93	94	95	96	97	98	99	100	110	120
Indication[dB]	89.9	90.9	91.9	92.9	94.0	95.0	96.0	97.0	98.0	99.0	100.0	110.0	120.0
Error[dB]	-0.1	-0.1	-0.1	-0.1	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Nominal[dB]	129	130	131	132	133	134							
Indication[dB]	129.0	130.0	131.0	132.0	133.0	134.0							
Error[dB]	0.0	0.0	0.0	0.0	0.0	0.0							

5. SELF-GENERATED NOISE LEVEL (sound)

Measured in anechoic chamber with microphone; Backlight Off; Electrical noise please refer user manual

Filter	A	C	Z
Indication[dB]	~ 18	~ 23	~ 31

6. TIME WEIGHTINGS (electrical)

Filter=A; Fsin=4kHz; Steady Level=132dBa

Detector	F	S
Rate of Decay[dB/s]	30.4	4.4
Delta of F/S[dB]	0.0	

7. TONEBURST RESPONSE (electrical)

Filter=A; Fsin=4kHz

Steady Level L_A = 132.0 dB

Tone Burst Duration [ms]	Response[dB]		
	$L_{AFmax} - L_A$	$L_{ASmax} - L_A$	$L_{AE} - L_A$
500	-0.1	-4.1	-3.1
200	-1.0	-7.5	-7.0
50	-4.9	-13.2	-13.1
10	-11.2	-20.1	-20.1

8. REPEATED TONEBURST RESPONSE (electrical)

Filter=A; Fsin=4kHz

Steady Level L_A = 132.0 dB

Tone Burst Duration [ms]	Tone Burst Interval [ms]	Response[dB]
		$L_{AeqT} - L_A$
500	2000	-7.0
200	800	-7.0
50	200	-7.0
10	40	-7.0

9. OVERLOAD INDICATION (electrical)

Filter=A; Fsin=1000Hz

Nominal[dB]	Error[dB]			Delta of Positive and Negative[dB]
	Steady	Positive Half Cycle	Negative Half Cycle	
134.1	0.1	0.1	0.1	0.0

10. C-WEIGHTED PEAK SOUND LEVEL (electrical)

Filter=C; Peak; Fsin=500Hz

Steady Signal Level	$(L_{Cpeak} - L_c)$ [dB]		
	Single Cycle	Positive Half Cycle	Negative Half Cycle
4dB Below Top	3.6	2.3	2.3
Middle	3.5	2.3	2.3
1dB Above Floor	3.2	2.3	2.5

CONDITIONS

Temperature	23	°C
Relative Humidity	36	%
Static Pressure	100.7	kPa

TEST EQUIPMENT

Item	Manufacturer	Model	S/N	Description
1	B&K	4231	3008422	Sound Calibrator
2	Agilent	33220A	MY44038043	Signal Generator
3	Agilent	34401A	SG47000236	Digital Multimeter
4	NJZY	ZY5142D	0425	Step Attenuator
5	B&K	4180	2412874	Standard Microphone

TEST PROCEDURES IN ACCORDANCE WITH
IEC 61672-3:2013Class 1 Performance Verified.
Test Qualified.

DATE: 2025.07M0 1D TEST (sig.):

LZH

APVD (sig.):



BSWA308 (SN#630178)

Calibrated by manufacturer

Calibration Date: 01 July 2025

Call. Due Day: 30 June 2026



CERTIFICATE OF CALIBRATION

Class 1



京制01020122号

TYPE: BSWA 308

S/N: 630179

1. APPEARANCE Pass

2. CALIBRATION (sound)

Calibrator: BK4231 Sound Level: 93.8 dB Frequency: 1000 Hz

Microphone Model / SN: MP231 / 591340

Filter	Nominal[dB]	Indication[dB]	Error[dB]
A	93.8	93.8	0.0
C	93.8	93.8	0.0
Z	93.8	93.8	0.0

3. FREQUENCY WEIGHTINGS (sound & electrical)

Z-weighting (sound & electrical); A/C-weighting (electrical, plus Z-weighting error)

Frequency [Hz]	Attenuation[dB]		
	A	C	Z
10	-69.0	-14.3	0.0
20	-50.3	-6.2	0.0
31.5	-39.5	-3.1	0.0
63	-26.2	-0.8	0.0
125	-16.1	-0.2	0.0
250	-8.6	0.0	0.0
500	-3.2	0.0	0.0
1000	0.2	0.2	0.2
2000	1.5	0.1	0.3
4000	1.1	-0.7	0.2
8000	-0.7	-2.6	0.8
16000	-12.0	-14.0	0.9
20000	-25.9	-27.9	-1.0

4. LEVEL LINEARITY (electrical)

Filter=A; Fsin=1kHz

Nominal[dB]	20	21	22	23	24	25	30	40	50	60	70	80	89
Indication[dB]	20.0	21.0	22.0	23.0	24.0	25.0	30.0	39.8	49.8	59.9	69.9	80.0	89.0
Error[dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-0.2	-0.2	-0.1	-0.1	0.0	0.0
Nominal[dB]	90	91	92	93	94	95	96	97	98	99	100	110	120
Indication[dB]	90.0	91.0	92.0	93.0	94.0	95.0	96.0	97.0	98.0	99.0	100.0	110.0	120.0
Error[dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Nominal[dB]	129	130	131	132	133	134							
Indication[dB]	129.0	130.0	131.0	132.0	133.0	134.0							
Error[dB]	0.0	0.0	0.0	0.0	0.0	0.0							

5. SELF-GENERATED NOISE LEVEL (sound)

Measured in anechoic chamber with microphone; Backlight Off; Electrical noise please refer user manual

Filter	A	C	Z
Indication[dB]	~ 18	~ 23	~ 31

6. TIME WEIGHTINGS (electrical)

Filter=A; Fsin=4kHz; Steady Level=132dBA

Detector	F	S
Rate of Decay[dB/s]	32.2	4.4
Delta of F/S[dB]	0.0	

7. TONEBURST RESPONSE (electrical)

Filter=A; Fsin=4kHz

Steady Level L_A = 132.0 dB

Tone Burst Duration [ms]	Response[dB]		
	$L_{AFmax}-L_A$	$L_{ASmax}-L_A$	$L_{AE}-L_A$
500	-0.1	-4.1	-3.1
200	-1.0	-7.5	-7.0
50	-4.9	-13.2	-13.1
10	-11.2	-20.1	-20.1

8. REPEATED TONEBURST RESPONSE (electrical)

Filter=A; Fsin=4kHz

Steady Level L_A = 132.0 dB

Tone Burst Duration [ms]	Tone Burst Interval [ms]	Response[dB]
		$L_{AeqT}-L_A$
500	2000	-7.0
200	800	-7.0
50	200	-7.0
10	40	-7.0

9. OVERLOAD INDICATION (electrical)

Filter=A; Fsin=1000Hz

Nominal[dB]	Error[dB]			Delta of Positive and Negative[dB]
	Steady	Positive Half Cycle	Negative Half Cycle	
134.1	0.1	0.1	0.1	0.0

10. C-WEIGHTED PEAK SOUND LEVEL (electrical)

Filter=C; Peak; Fsin=500Hz

Steady Signal Level	$(L_{Cpeak}-L_C)[dB]$		
	Single Cycle	Positive Half Cycle	Negative Half Cycle
4dB Below Top	3.6	2.3	2.3
Middle	3.5	2.3	2.3
1dB Above Floor	3.9	2.3	2.3

CONDITIONS

Temperature	23	°C
Relative Humidity	36	%
Static Pressure	100.7	kPa

TEST EQUIPMENT

Item	Manufacturer	Model	S/N	Description
1	B&K	4231	3008422	Sound Calibrator
2	Agilent	33220A	MY44038043	Signal Generator
3	Agilent	34401A	SG47000236	Digital Multimeter
4	NJZY	ZY5142D	0425	Step Attenuator
5	B&K	4180	2412874	Standard Microphone

TEST PROCEDURES IN ACCORDANCE WITH
IEC 61672-3:2013Class 1 Performance Verified.
Test Qualified.

DATE: 2025-07-01 TEST (sig.): LZH APVD (sig.):



BSWA308 (SN#630179)

Calibrated by manufacturer

Calibration Date: 01 July 2025

Cal. Due Day: 30 June 2026



CERTIFICATE OF CALIBRATION



京制01020122号

Class 1

TYPE: BSWA 308

S/N: 630177

1. APPEARANCE Pass

2. CALIBRATION (sound)

Calibrator: BK4231 Sound Level: 93.8 dB Frequency: 1000 Hz

Microphone Model / SN: MP231/591089

Filter	Nominal[dB]	Indication[dB]	Error[dB]
A	93.8	93.8	0.0
C	93.8	93.8	0.0
Z	93.8	93.8	0.0

3. FREQUENCY WEIGHTINGS (sound & electrical)

Z-weighting (sound & electrical); A/C-weighting (electrical, plus Z-weighting error)

Frequency [Hz]	A	C	Z
10	-69.0	-14.3	0.0
20	-50.4	-6.2	0.0
31.5	-39.5	-3.0	0.0
63	-26.2	-0.9	0.0
125	-16.1	-0.2	0.0
250	-8.6	0.0	0.0
500	-3.2	0.0	0.0
1000	0.1	0.1	0.1
2000	1.3	-0.1	0.1
4000	0.5	-1.3	-0.4
8000	-1.6	-3.5	-0.1
16000	-13.2	-15.1	-0.2
20000	-27.2	-29.1	-2.2

4. LEVEL LINEARITY (electrical)

Filter=A; Fsin=1kHz

Nominal[dB]	20	21	22	23	24	25	30	40	50	60	70	80	89
Indication[dB]	20.2	21.2	22.2	23.1	24.2	25.1	30.0	39.9	49.8	59.8	69.9	79.9	88.9
Error[dB]	0.2	0.2	0.2	0.1	0.2	0.1	0.0	-0.1	-0.2	-0.2	-0.1	-0.1	-0.1
Nominal[dB]	90	91	92	93	94	95	96	97	98	99	100	110	120
Indication[dB]	89.9	90.9	91.9	92.9	94.0	95.0	96.0	96.9	97.9	98.9	100.0	110.0	120.0
Error[dB]	-0.1	-0.1	-0.1	-0.1	0.0	0.0	0.0	-0.1	-0.1	-0.1	0.0	0.0	0.0
Nominal[dB]	129	130	131	132	133	134							
Indication[dB]	129.0	130.0	131.0	132.0	133.0	134.0							
Error[dB]	0.0	0.0	0.0	0.0	0.0	0.0							

5. SELF-GENERATED NOISE LEVEL (sound)

Measured in anechoic chamber with microphone; Backlight Off; Electrical noise please refer user manual

Filter	A	C	Z
Indication[dB]	~ 18	~ 23	~ 31

6. TIME WEIGHTINGS (electrical)

Filter=A; Fsin=4kHz; Steady Level=132dBA

Detector	F	S
Rate of Decay[dB/s]	32.3	4.4
Delta of F/S[dB]	0.0	

7. TONEBURST RESPONSE (electrical)

Filter=A; Fsin=4kHz

Steady Level L_A = 132.0 dB

Tone Burst Duration [ms]	Response[dB]		
	$L_{AFmax} - L_A$	$L_{ASmax} - L_A$	$L_{AE} - L_A$
500	-0.2	-4.1	-3.1
200	-1.1	-7.5	-7.0
50	-4.9	-13.2	-13.1
10	-11.3	-20.1	-20.1

8. REPEATED TONEBURST RESPONSE (electrical)

Filter=A; Fsin=4kHz

Steady Level L_A = 132.0 dB

Tone Burst Duration [ms]	Tone Burst Interval [ms]	Response[dB]
		$L_{Aavg} - L_A$
500	2000	-7.1
200	800	-7.1
50	200	-7.1
10	40	-7.1

9. OVERLOAD INDICATION (electrical)

Filter=A; Fsin=1000Hz

Nominal[dB]	Error[dB]			Delta of Positive and Negative[dB]
	Steady	Positive Half Cycle	Negative Half Cycle	
134.1	0.0	0.1	0.1	0.0

10. C-WEIGHTED PEAK SOUND LEVEL (electrical)

Filter=C; Peak; Fsin=500Hz

Steady Signal Level	$(L_{Cpeak} - L_C)$ [dB]		
	Single Cycle	Positive Half Cycle	Negative Half Cycle
4dB Below Top	3.5	2.3	2.3
Middle	3.5	2.2	2.2
1dB Above Floor	3.7	2.2	2.6

CONDITIONS

Temperature	23	°C
Relative Humidity	36	%
Static Pressure	100.7	kPa

TEST EQUIPMENT

Item	Manufacturer	Model	S/N	Description
1	B&K	4231	3008422	Sound Calibrator
2	Agilent	33220A	MY44038043	Signal Generator
3	Agilent	34401A	SG47000236	Digital Multimeter
4	NJZY	ZY5142D	0425	Step Attenuator
5	B&K	4180	2412874	Standard Microphone

TEST PROCEDURES IN ACCORDANCE WITH
IEC 61672-3:2013Class 1 Performance Verified.
Test Qualified.

DATE: 2025.07.01 TEST (sig.): LZH APVD (sig.):

BSWA 308 (SN#630177)

Calibration by manufacturer

Calibration Date: 01 July 2025

Cal. Due Day: 30 June 2026

Certificate of Calibration

Certificate No. ATS24-112-CC001

Customer: **Ka Shing Facilities Management Limited**
Flat C, 14/F., Jing Ho Industrial Building,
78-84 Wing Lung Street, Tsuen Wan,
N.T., Hong Kong

Unit-under-test (UUT):

Description: Sound Calibrator
Manufacturer: SoundTEK
Type No.: ST-120
Serial No.: 210102628

Conditions during calibration:

Temperature: 25°C
Relative Humidity: 50%

Test Specifications: Calibration Check

Date of Calibration: 11 November 2024

Test Results: All calibration points are within manufacturer's specification.

Certified by:


Mr. Ching Mau LAM / Quality Manager
MIOA, MHKIOA



Issue Date: 11 November 2024

1. The instrument under test was allowed to stabilize in the laboratory for over 24 hours.
2. Calibration equipment:

Description:	Sound Analyzer	Reference Microphone
Manufacturer:	Brüel & Kjær	Brüel & Kjær
Type No.:	2270	4189
Serial No.:	3001883	2662797
Last Calibration Date:	14 March 2024	14 March 2024
Certificate No.:	AV240037	AV240037

The calibration equipment used for calibration is traceable to National Standards via Standards and Calibration Laboratory, the Government of the HKSAR.

3. The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted, if any, will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. Acoustic Testing Services Limited shall not be liable for any loss or damage resulting from the use of the equipment.
4. Calibration Results

Nominal value dB	Measured value dB	IEC 60942 Class 1 Tolerance Limits dB	Conclusion	Expanded Measurement Uncertainty of Reference Microphone B&K 4189 at 1000 Hz dB
94.00	93.82	± 0.25	PASS	0.20
114.0	113.76	± 0.25	PASS	0.20

All calibration points are within manufacturer's specification.



APPENDIX D
ENVIRONMENTAL MONITORING
SCHEDULES

Environmental Team for Police Facilities in Kong Nga Po
Impact Air Quality and Noise Monitoring Schedule
July-2025

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-Jul	2-Jul	3-Jul	4-Jul	5-Jul
						1-hr TSPx3 (AM1, AM2)
6-Jul	7-Jul	8-Jul	9-Jul	10-Jul	11-Jul	12-Jul
					1-hr TSPx3 (AM1, AM2) NM (NM9 to NM14)	
13-Jul	14-Jul	15-Jul	16-Jul	17-Jul	18-Jul	19-Jul
				1-hr TSPx3 (AM1, AM2) NM (NM9 to NM14)		
20-Jul	21-Jul	22-Jul	23-Jul	24-Jul	25-Jul	26-Jul
			1-hr TSPx3 (AM1, AM2) NM (NM9 to NM14)			
27-Jul	28-Jul	29-Jul	30-Jul	31-Jul		
		1-hr TSPx3 (AM1, AM2) NM (NM9 to NM14)				

Environmental Team for Police Facilities in Kong Nga Po
Impact Air Quality and Noise Monitoring Schedule
August-2025

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					1-Aug	2-Aug
3-Aug	4-Aug	5-Aug	6-Aug	7-Aug	8-Aug	9-Aug
			1-hr TSPx3 (AM1, AM2) NM (NM9 to NM14)			
10-Aug	11-Aug	12-Aug	13-Aug	14-Aug	15-Aug	16-Aug
		1-hr TSPx3 (AM1, AM2) NM (NM9 to NM14)				
17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug
	1-hr TSPx3 (AM1, AM2) NM (NM9 to NM14)					1-hr TSPx3 (AM1, AM2)
24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug
					1-hr TSPx3 (AM1, AM2) NM (NM9 to NM14)	
31-Aug						



APPENDIX E
AIR QUALITY MONITORING RESULTS
AND GRAPHICAL PRESENTATION

Appendix E - 1-hour TSP Monitoring Results

Location AM1 - Village House, Kong Nga Po			
Date	Time	Weather	Particulate Concentration ($\mu\text{g}/\text{m}^3$)
05-Jul-25	7:57	Sunny	128
	8:57		77
	9:57		89
11-Jul-25	13:07	Cloudy	65
	14:07		121
	15:07		88
17-Jul-25	13:00	Sunny	53
	14:00		156
	15:00		33
23-Jul-25	8:58	Sunny	127
	9:58		29
	10:58		57
29-Jul-25	13:15	Cloudy	35
	14:15		43
	15:15		58
		Minimum	29
		Maximum	156
		Average	77

Location AM2 - Village House, Kong Nga Po			
Date	Time	Weather	Particulate Concentration ($\mu\text{g}/\text{m}^3$)
05-Jul-25	8:07	Sunny	48
	9:07		62
	10:07		78
11-Jul-25	13:12	Cloudy	71
	14:12		9
	15:12		93
17-Jul-25	13:10	Sunny	101
	14:10		94
	15:10		69
23-Jul-25	8:44	Sunny	59
	9:44		56
	10:44		53
29-Jul-25	13:13	Cloudy	23
	14:13		69
	15:13		67
		Minimum	9
		Maximum	101
		Average	64

1-hr TSP Concentration Levels

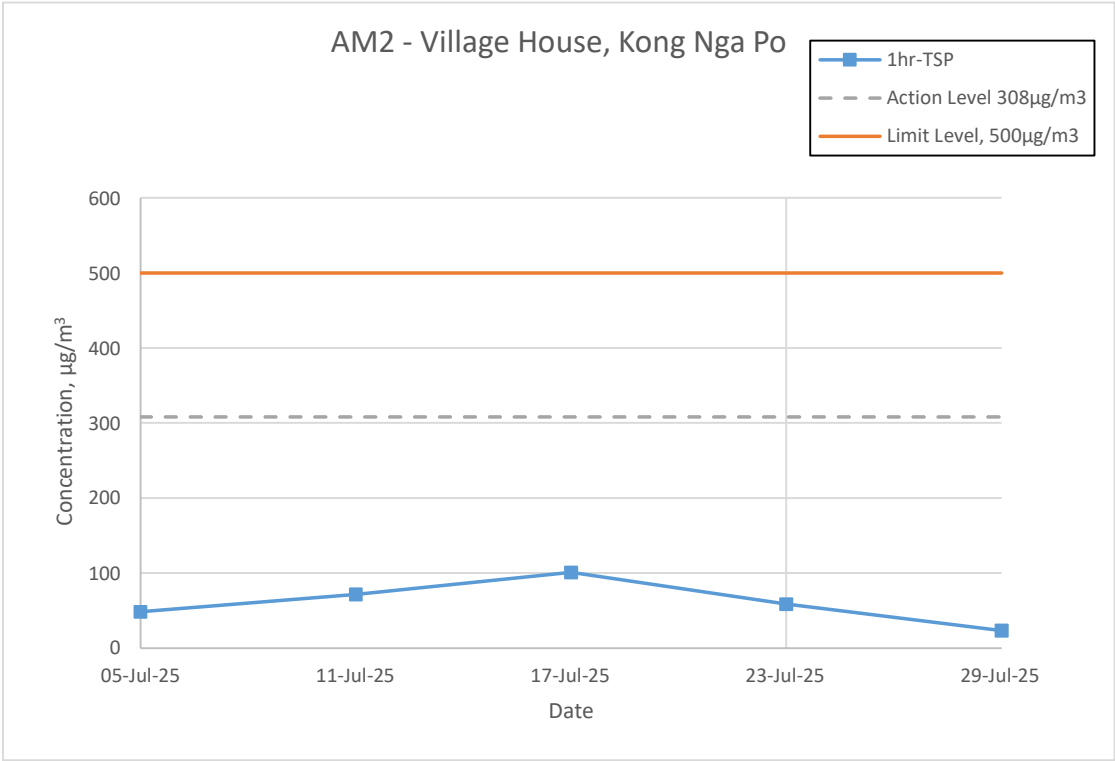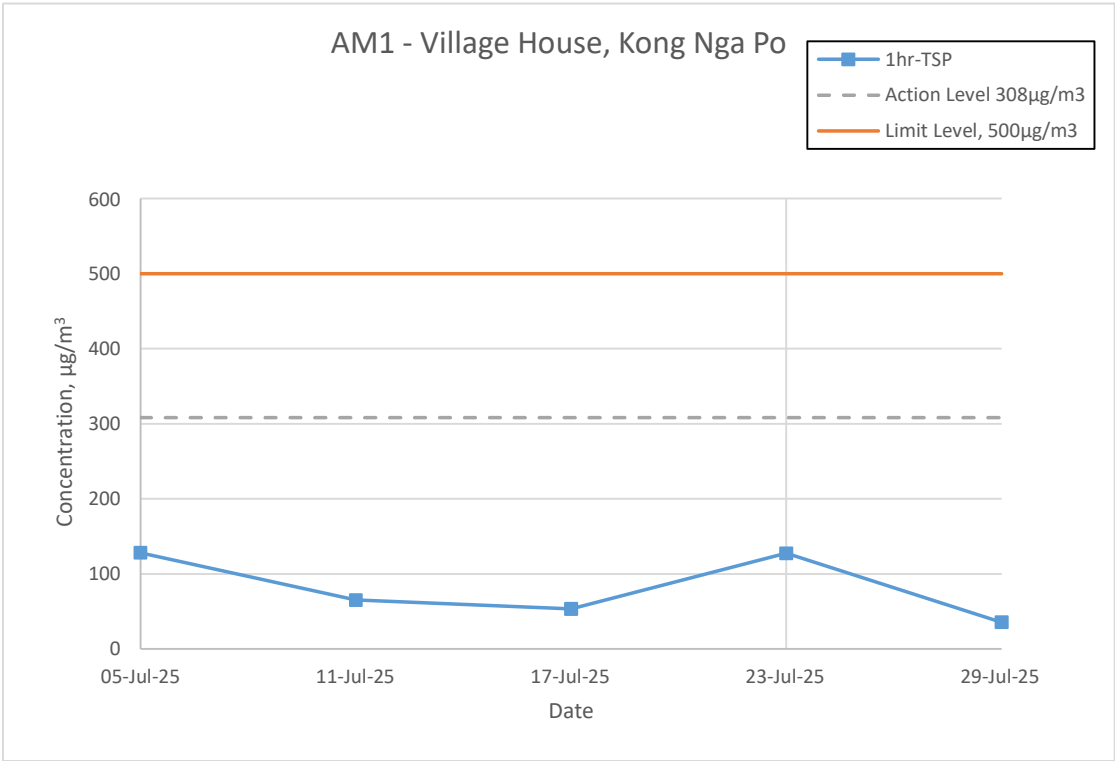

APPENDIX F
NOISE MONITORING RESULTS AND
GRAPHICAL PRESENTATION

Appendix F -Noise Monitoring Results

Location NM9 - Village House, Kong Nga Po									
Date	Weather	Wind Speed (m/s)	Time	Unit: dB(A) (5-min)			Average	Limit Level	Baseline
				L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	L _{eq}
11-Jun-25	Cloudy	0.00	13:15	63.3	61.8	53.4	60.9	75.0	55.9
				54.5	54.9	53.8			
				61.5	60.1	53.8			
				61.1	58.9	53.9			
				55.9	60.3	53.2			
				62.7	63.6	52.8			
17-Jul-25	Sunny	0.05	13:10	59.5	64.1	43.9	57.0	75.0	55.9
				47.0	49.0	44.4			
				48.3	50.2	43.7			
				50.2	55.0	46.1			
				49.0	50.2	44.7			
				62.6	64.4	44.0			
23-Jul-25	Sunny	0.00	9:00	62.4	59.9	50.1	60.7	75.0	55.9
				58.8	57.7	54.0			
				53.8	57.1	52.0			
				60.3	54.1	48.7			
				60.8	62.3	51.5			
				63.2	65.9	50.1			
29-Jul-25	Cloudy	0.44	13:14	66.1	68.4	54.2	65.3	75.0	55.9
				65.2	66.1	57.1			
				64.3	66.0	57.3			
				68.3	70.7	56.4			
				62.7	58.8	56.0			
				61.9	61.5	56.8			

Location NM10 - Village House, Kong Nga Po									
Date	Weather	Wind Speed (m/s)	Time	Unit: dB(A) (5-min)			Average	Limit Level	Baseline
				L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	L _{eq}
11-Jun-25	Cloudy	0.28	13:16	56.6	49.2	47.4	58.0	75.0	52.8
				56.8	55.0	47.6			
				50.7	52.3	47.8			
				56.7	56.8	48.1			
				58.9	60.4	47.9			
				61.6	63.1	46.7			
17-Jul-25	Sunny	0.00	13:12	64.1	59.2	44.9	57.0	75.0	52.8
				46.4	48.3	44.1			
				47.8	49.8	44.5			
				49.0	50.7	45.1			
				50.2	53.0	46.0			
				51.4	53.7	47.3			
23-Jul-25	Sunny	0.30	9:16	61.7	58.1	51.1	66.3	75.0	52.8
				65.9	70.6	52.0			
				70.8	74.7	61.8			
				65.0	69.2	53.7			
				66.0	66.3	52.7			
				61.3	62.0	52.2			
29-Jul-25	Cloudy	0.12	13:19	61.1	59.1	44.6	58.3	75.0	52.8
				47.5	50.0	45.0			
				53.0	56.0	47.8			
				49.6	51.9	45.3			
				54.3	58.2	45.6			
				63.3	67.2	58.7			




Location NM11 - Village House, Kong Nga Po									
Date	Weather	Wind Speed (m/s)	Time	Unit: dB(A) (5-min)			Average	Limit Level	Baseline
				L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	L _{eq}
11-Jun-25	Cloudy	0.00	13:40	54.6	56.2	43.7	52.5	75.0	46.4
				50.0	52.9	43.9			
				51.7	55.5	45.5			
				52.4	56.0	45.4			
				49.7	52.9	44.2			
				54.3	58.1	45.5			
17-Jul-25	Sunny	0.00	13:37	54.5	54.4	43.0	53.9	75.0	46.4
				55.4	61.9	42.9			
				50.8	50.6	42.3			
				46.0	48.6	42.3			
				51.4	49.1	43.1			
				57.5	60.6	43.3			
23-Jul-25	Sunny	0.00	9:35	57.5	52.1	48.1	59.8	75.0	46.4
				63.8	63.3	48.6			
				49.5	50.2	48.7			
				61.0	58.1	48.5			
				56.6	52.5	48.6			
				59.6	60.4	48.6			
29-Jul-25	Cloudy	0.16	13:19	60.2	58.0	47.7	62.1	75.0	46.4
				52.0	53.2	50.1			
				50.8	51.7	49.4			
				56.3	60.8	49.4			
				63.2	64.9	59.0			
				67.7	69.3	64.9			




Location NM12 - Village House, Kong Nga Po									
Date	Weather	Wind Speed (m/s)	Time	Unit: dB(A) (5-min)			Average	Limit Level	Baseline
				L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	L _{eq}
11-Jun-25	Cloudy	0.00	13:05	63.5	67.2	39.8	60.4	75.0	54.7
				64.2	62.0	49.2			
				50.8	51.7	49.2			
				57.7	56.3	49.3			
				57.4	58.7	50.9			
				55.9	62.5	50.2			
17-Jul-25	Sunny	0.00	12:59	54.4	47.6	44.1	55.5	75.0	54.7
				55.0	59.7	43.5			
				60.7	50.3	44.4			
				46.1	46.3	44.2			
				47.0	46.6	43.7			
				54.6	50.1	43.9			
23-Jul-25	Sunny	0.21	8:42	64.6	62.4	46.8	63.6	75.0	54.7
				62.9	58.2	48.3			
				66.9	69.1	59.4			
				64.8	64.4	51.5			
				55.4	56.1	51.8			
				58.0	58.7	51.5			
29-Jul-25	Cloudy	0.18	13:13	61.1	60.6	45.5	55.7	75.0	54.7
				50.1	53.0	45.7			
				54.9	54.5	46.6			
				55.0	59.8	46.4			
				50.7	52.1	48.8			
				50.1	51.9	47.5			

Location NM13 - Village House, Kong Nga Po									
Date	Weather	Wind Speed (m/s)	Time	Unit: dB(A) (5-min)			Average	Limit Level	Baseline
				L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	L _{eq}
11-Jun-25	Cloudy	0.00	13:51	62.5	55.7	47.2	56.0	75.0	61.3
				50.1	50.9	47.2			
				49.2	50.8	46.8			
				49.4	51.1	46.9			
				50.0	52.0	46.7			
				54.1	55.0	46.7			
17-Jul-25	Sunny	0.00	13:45	61.7	58.4	45.8	55.8	75.0	61.3
				50.2	51.0	46.2			
				48.5	50.4	46.3			
				56.8	55.1	46.0			
				48.8	49.2	46.1			
				47.7	49.6	46.3			
23-Jul-25	Sunny	0.25	9:56	61.1	56.2	50.3	62.4	75.0	61.3
				62.4	65.6	52.8			
				64.2	66.1	51.1			
				60.4	62.4	50.7			
				58.9	59.3	50.2			
				64.7	67.6	51.5			
29-Jul-25	Cloudy	0.25	13:27	60.4	58.9	44.1	60.7	75.0	61.3
				51.8	54.4	43.0			
				57.8	62.7	43.5			
				59.5	61.3	54.7			
				64.4	66.8	59.2			
				61.9	64.6	55.0			

Location NM14 - Village House, near Man Kam To Road									
Date	Weather	Wind Speed (m/s)	Time	Unit: dB(A) (5-min)			Average	Limit Level	Baseline
				L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	L _{eq}
11-Jun-25	Cloudy	0.32	13:56	63.2	61.3	45.2	57.0	75.0	59.6
				50.7	53.3	43.5			
				53.8	57.4	45.6			
				53.8	57.1	47.3			
				52.2	55.2	47.2			
				52.7	55.4	47.9			
17-Jul-25	Sunny	0.13	13:56	62.1	58.8	44.3	59.3	75.0	59.6
				59.9	67.8	44.9			
				49.9	52.8	43.6			
				47.9	51.5	40.5			
				50.8	53.7	42.0			
				63.4	64.9	43.7			
23-Jul-25	Sunny	0.00	10:11	58.1	55.8	48.6	58.9	75.0	59.6
				58.0	59.1	48.8			
				59.3	63.2	49.3			
				59.0	62.8	48.0			
				60.3	64.0	47.7			
				58.1	52.5	49.9			
29-Jul-25	Cloudy	0.14	13:47	66.4	67.9	57.2	67.3	75.0	59.6
				69.1	68.2	62.2			
				69.1	69.1	54.3			
				68.5	68.8	46.8			
				65.4	66.3	47.8			
				60.4	49.9	48.0			

Noise Levels

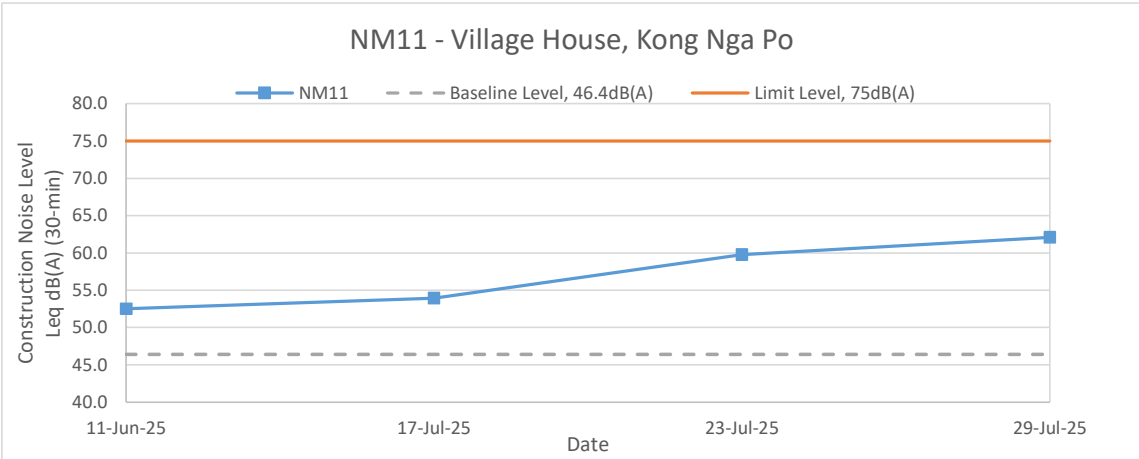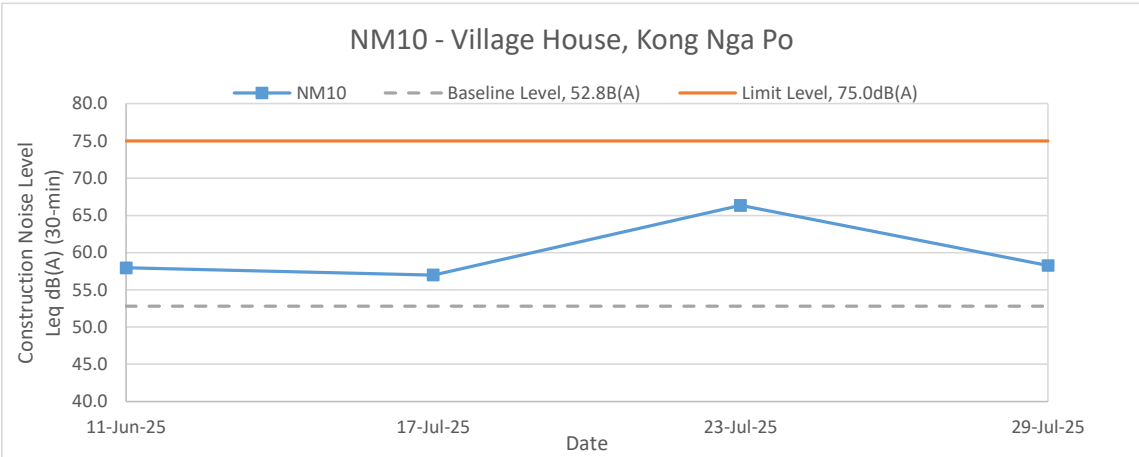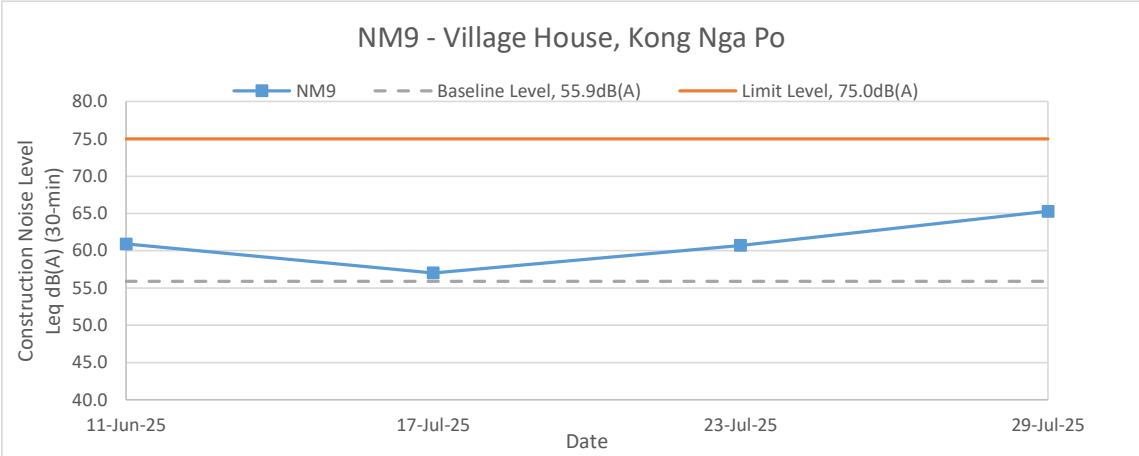

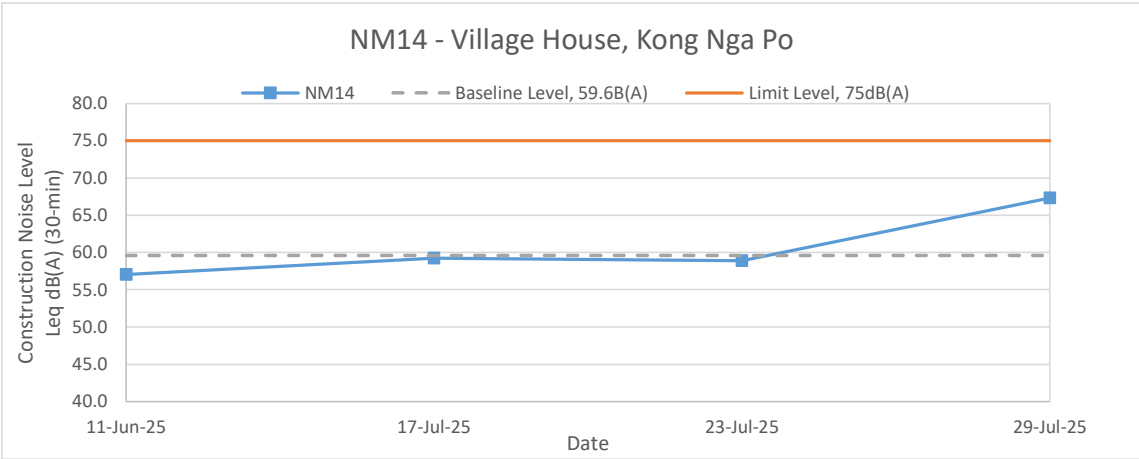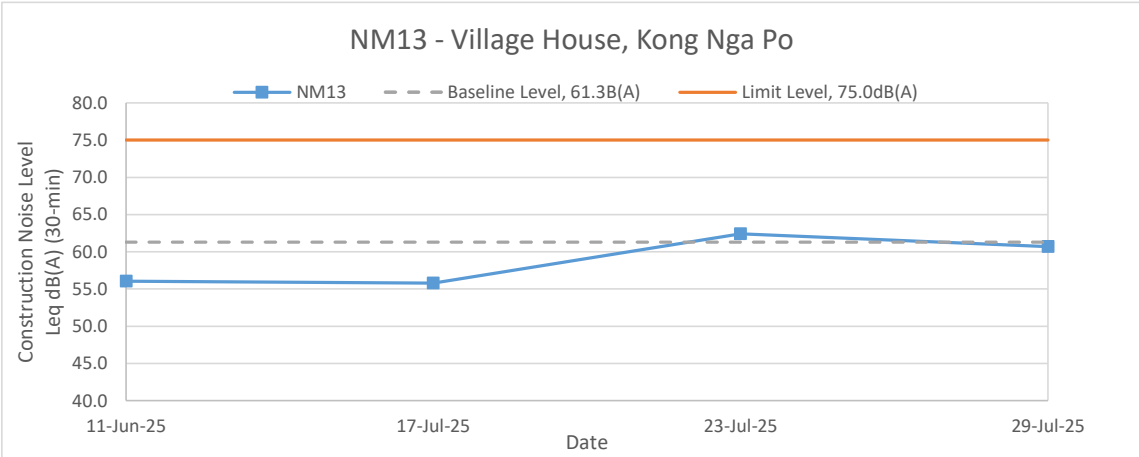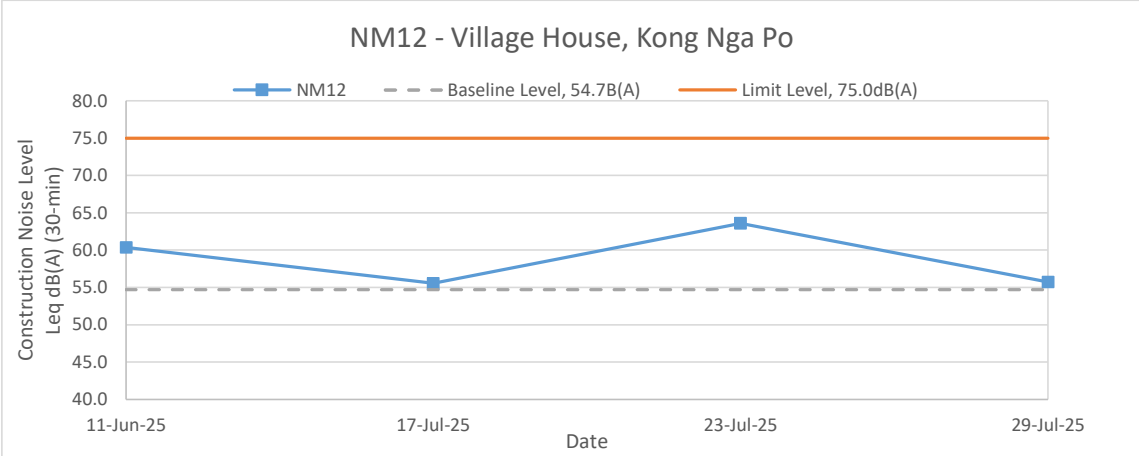

APPENDIX G
WEATHER CONDITION

**Appendix G –
General Weather Conditions during the Monitoring Period July 2025**

Date July	Mean Pressure (hPa)	Air Temperature			Mean Dew Point Temperature (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)
		Maximum (deg. C)	Mean (deg. C)	Minimum (deg. C)				
1	1008	29.8	28.2	26.4	25.7	87	86	5.5
2	1008.8	33.3	30	27.4	26.1	80	80	0.5
3	1007.5	33.6	30.3	28.4	25.6	76	82	-
4	1005.4	34.5	30.8	28.5	24.8	71	67	-
5	1003.3	34.8	30.6	29	24.6	71	80	3.7
6	1002.8	33.5	30.3	28.2	24.5	71	84	-
7	1003.1	34.3	31.2	29.1	26.5	77	70	-
8	1002.7	33.3	30.9	29.7	26.2	76	82	-
9	1000	33.6	30.7	25.8	26.3	77	84	15.2
10	996.7	29	26.3	25	25.1	93	91	126.4
11	998.9	29.9	27.9	25.9	24.9	84	88	-
12	1004.8	31.3	28.7	26.4	26.1	87	88	38.4
13	1006.2	33.3	30.1	27.8	26.3	81	88	1.9
14	1004.5	33.2	30.2	27.8	26	79	87	9.2
15	1003.5	32.7	30.3	28.3	26.4	79	85	3.2
16	1004.1	34	31.1	29	26	75	58	-
17	1003.1	34.2	31.3	29.2	26.5	76	74	-
18	1000	31.3	28.6	26.1	25.8	85	85	19
19	994.3	33.5	29.5	27	25.2	78	81	10
20	988.5	28	27	25.9	25.4	91	94	87.6
21	997.4	27.9	27.1	26.4	25.7	92	92	42.4
22	1002	30.5	28	25.8	25.8	88	88	95.7
23	1003.2	33.3	29	26.4	25.2	81	88	2.6
24	1002	32	29.4	27.5	24.8	77	80	Trace
25	1000.1	33.6	29.2	25.4	24.8	78	62	31.8
26	1000	35.2	30.2	26.1	24.9	74	36	-
27	1000.1	33.1	30.4	28.8	25.7	76	52	-
28	998.1	32.8	30.1	28.3	26.2	80	87	0.6
29	996.9	29.1	27.8	25.8	26	90	91	106.5
30	997.4	32.6	29.8	28.5	26.8	84	88	-
31	998.6	31.8	29.9	28.2	26.6	83	88	1.5
Mean/Total	1001.3	32.4	29.5	27.4	25.7	81	80	601.7
Normal*	1005.6	31.6	28.9	26.9	25.2	81	72	385.8

* The above information was extracted from the daily weather summary by Hong Kong Observatory.

APPENDIX H
ECOLOGICAL MONITORING RESULTS

Contract No.: SS K509
Design and Construction of
Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works Report

INSPECTION DATE: 28 JULY 2025
REPORT DATE: 31 JULY 2025



PREPARED BY:
Lau Siu Yeung, Andy
(UKAA PR5206)

Template of Post-transplantation Monitoring Checklist
Design and Construction of Kong Nga Po Police Training Facilities

Audit Ref. No. _____

Contract SS K509

Inspected By Lau Siu Yeung

Inspection Date 28/07/2025

Time Period 08:30 to 12:00

Part A Weather

Condition ☐ Sunny ☐ Fine ☐ Overcast ☐ Drizzle ☒ Rain ☐ Storm ☐ Hazy

Temperature 30.1 °C

Humidity ☐ High (RH>90%) ☒ Moderate (90%>RH>50%) ☐ Low (RH<50%)

Wind ☐ Calm ☐ Light ☒ Breeze ☐ Strong

Part B

1. Cycadfern *Brainea insignis*

	N/A or not observed	Yes	No	Follow-up	N/C	Remarks
1.1 Are the plants' health conditions satisfactory?	☐	☒	☐	☐	☐	
1.2 Are transplanted plants on site protected carefully?	☐	☒	☐	☐	☐	
1.3 Are the temporary protective fence properly erected and maintained?	☐	☒	☐	☐	☐	
1.4 Are the plant protection zone set 1m from the plants?	☐	☒	☐	☐	☐	
1.5 Are all grassed and planted area kept free from weeds/unwanted plants?	☐	☒	☐	☐	☐	
1.6 Is compaction of the soil avoided for the plants?	☐	☒	☐	☐	☐	
1.7 Are litter/ unwanted material removed within the planting area?	☐	☒	☐	☐	☐	
1.8 Are equipment or stockpile placed outside the protection zone?	☐	☒	☐	☐	☐	
1.9 Are soil, debris or construction materials deposited around and against the trunk of a plant as this causes bark damage avoided?	☐	☒	☐	☐	☐	
1.10 Are fixings driven into plants avoided?	☐	☒	☐	☐	☐	
1.11 Are the plants used for anchoring or winching purposes or for the display of signs avoided?	☐	☒	☐	☐	☐	
1.12 Are the fire lit below the branches and petrol, oil or caustic substances stored near the plants avoided?	☐	☒	☐	☐	☐	
1.13 Are all plants kept free from pest, disease or fungal infection?	☐	☒	☐	☐	☐	
1.14 Are there enough area for growth and development of plant roots?	☐	☒	☐	☐	☐	
1.15a Is exposure of plant roots avoided?	☐	☒	☐	☐	☐	
1.15b If not, were broken off or rotting of roots avoided?	☐	☒	☐	☐	☐	

2. Ladies Tresses *Spiranthes sinensis*

	N/A or not observed	Yes	No	Follow-up	N/C	Remarks
2.1 Are the plants' health conditions satisfactory?	☐	☒	☐	☐	☐	
2.2 Are transplanted plants on site protected carefully?	☐	☒	☐	☐	☐	
2.3 Are the temporary protective fence properly erected and maintained?	☐	☒	☐	☐	☐	
2.4 Are the plant protection zone set 1m from the plants?	☐	☒	☐	☐	☐	
2.5 Are all grassed and planted area kept free from weeds/unwanted plants?	☐	☒	☐	☐	☐	
2.6 Is compaction of the soil avoided for the plants?	☐	☒	☐	☐	☐	
2.7 Are litter/ unwanted material removed within the planting area?	☐	☒	☐	☐	☐	

Template of Post-transplantation Monitoring Checklist
Design and Construction of Kong Nga Po Police Training Facilities

	N/A or not observed	Yes	No	Follow-up	N/C	Remarks
2.8 Are equipment or stockpile placed outside the protection zone?	☐	☒	☐	☐	☐	
2.9 Are soil, debris or construction materials deposited around and against the trunk of a plant as this causes bark damage avoided?	☐	☒	☐	☐	☐	
2.10 Are fixings driven into plants avoided?	☐	☒	☐	☐	☐	
2.11 Are the plants used for anchoring or winching purposes or for the display of signs avoided?	☐	☒	☐	☐	☐	
2.12 Are the fire lit below the branches and petrol, oil or caustic substances stored near the plants avoided?	☐	☒	☐	☐	☐	
2.13 Are all plants kept free from pest, disease or fungal infection?	☐	☒	☐	☐	☐	
2.14 Are there enough area for growth and development of plant roots?	☐	☒	☐	☐	☐	
2.15a Is exposure of plant roots avoided?	☐	☒	☐	☐	☐	
2.15b If not, were broken off or rotting of roots avoided?	☐	☒	☐	☐	☐	
<u>Incense Trees <i>Aquilaria sinensis</i></u>						
3.1 Are the trees's health conditions satisfactory?	☐	☐	☐	☐	☐	
3.2 Are transplanted trees on site protected carefully?	☐	☐	☐	☐	☐	
3.3 Are the temporary protective fence properly erected and maintained?	☐	☐	☐	☐	☐	
3.4 Are the tree protection zone set 1m from the trees?	☐	☐	☐	☐	☐	
3.5 Are all grassed and planted area kept free from weeds/unwanted plants?	☐	☐	☐	☐	☐	
3.6 Is compaction of the soil avoided for the trees	☐	☐	☐	☐	☐	
3.7 Are litter/ unwanted material removed within the planting area?	☐	☐	☐	☐	☐	
3.8 Are equipment or stockpile placed outside the protection zone?	☐	☐	☐	☐	☐	
3.9 Are soil, debris or construction materials deposited around and against the trunk of a tree as this causes bark damage avoided?	☐	☐	☐	☐	☐	
3.10 Are fixings driven into trees avoided?	☐	☐	☐	☐	☐	
3.11 Are the trees used for anchoring or winching purposes or for the display of signs avoided?	☐	☐	☐	☐	☐	
3.12 Are the fire lit below the branches and petrol, oil or caustic substances stored near the trees avoided?	☐	☐	☐	☐	☐	
3.13 Are all trees kept free from pest, disease or fungal infection?	☐	☐	☐	☐	☐	
3.14 Are there enough area for growth and development of tree roots?	☐	☐	☐	☐	☐	
3.15a Is exposure of tree roots avoided?	☐	☐	☐	☐	☐	
3.15b If not, were broken off or rotting of roots avoided?	☐	☐	☐	☐	☐	
3.16 Are wounds/mechanical injuries avoided on tree trunk?	☐	☐	☐	☐	☐	
3.17 Are leaning of trees avoided?	☐	☐	☐	☐	☐	
3.18 Are dead/detached branches avoided?	☐	☐	☐	☐	☐	
3.19 Are decay/cavity avoided on tree trunks?	☐	☐	☐	☐	☐	

Template of Post-transplantation Monitoring Checklist
Design and Construction of Kong Nga Po Police Training Facilities

Part C Follow-up for the Previous Site Audit on Date: _____ (Ref. No. _____)		N/A or not observed	Yes	No	Follow-up	N/C	Remarks
1.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____
2.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____
3.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____
4.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____
5.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____
6.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____
7.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____
8.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____
9.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____
10.	Is the situation in item _____ improved/rectified?	☐	☐	☐	☐	☐	_____

Remarks/Observations

Signatures:

Contractor's Representative

(Name: Lau Siu Yeung)
(Date: 28/07/2025)

Supervisor's Rep.

(Name: _____)
(Date: _____)

Tree/Plant/ Colony No.	Number of Individuals	Species Name	Form (Good/Fair/Poor)	Health (Good/Fair/Poor)	Remark
C-0001	01	<i>Brainea insignis</i>	F	F	Young leaves observed
	02	<i>Brainea insignis</i>	F	F	Young leaves observed
	03	<i>Brainea insignis</i>	F	F	Young leaves observed
	04	<i>Brainea insignis</i>	F	F	Young leaves observed
	05	<i>Brainea insignis</i>	F	F	Young leaves observed
	06	<i>Brainea insignis</i>	F	F	Young leaves observed
	07	<i>Brainea insignis</i>	F	F	Young leaves observed
	08	<i>Brainea insignis</i>	F	F	Young leaves observed
C-0002	01	<i>Brainea insignis</i>	F	F	Young leaves observed
	02	<i>Brainea insignis</i>	F	F	Young leaves observed
	03	<i>Brainea insignis</i>	F	P	Young leaves observed
	04	<i>Brainea insignis</i>	F	P	Young leaves observed
	05	<i>Brainea insignis</i>	F	F	Young leaves observed
	06	<i>Brainea insignis</i>	F	F	Young leaves observed
	07	<i>Brainea insignis</i>	F	F	Young leaves observed
	08	<i>Brainea insignis</i>	F	F	Young leaves observed
C-0003	01	<i>Brainea insignis</i>	F	F	Young leaves observed
C-0004	01	<i>Brainea insignis</i>	P	P	Young leaves at base; Dry out caused by bushfire initially outside site boundary and high temperature on 2 Feb 2021
	02	<i>Brainea insignis</i>	F	F	Young leaves observed
	03	<i>Brainea insignis</i>	F	F	Young leaves observed
	04	<i>Brainea insignis</i>	F	F	Young leaves observed
	05	<i>Brainea insignis</i>	F	F	Young leaves observed
	06	<i>Brainea insignis</i>	F	F	Young leaves observed
	07	<i>Brainea insignis</i>	F	F	Young leaves observed
	08	<i>Brainea insignis</i>	F	F	Young leaves observed
	09	<i>Brainea insignis</i>	P	P	Dry out caused by bushfire initially outside site boundary and high temperature on 2 Feb 2021
	10	<i>Brainea insignis</i>	F	P	Young leaves at base
	11	<i>Brainea insignis</i>	F	F	Young leaves observed
	12	<i>Brainea insignis</i>	F	P	Young leaves observed
	13	<i>Brainea insignis</i>	-	-	Stem not found Dry out caused by bushfire initially outside site boundary and high temperature on 2 Feb 2021
	14	<i>Brainea insignis</i>	F	F	Young leaves observed
	15	<i>Brainea insignis</i>	P	P	Young leaves at base; Dry out caused by bushfire initially outside site boundary and high temperature on 2 Feb 2021
	16	<i>Brainea insignis</i>	P	P	Dry out caused by bushfire initially outside site boundary and high temperature on 2 Feb 2021
	17	<i>Brainea insignis</i>	P	P	Young leaves observed
	18	<i>Brainea insignis</i>	-	-	Burned by bushfire initially outside the site boundary on 2 Feb 2021.
	19	<i>Brainea insignis</i>	F	P	-
	20	<i>Brainea insignis</i>	F	F	Young leaves observed

Tree/Plant/ Colony No.	Number of Individuals	Species Name	Form (Good/Fair/Poor)	Health (Good/Fair/Poor)	Remark
C-0005	01	<i>Brainea insignis</i>	F	F	Young leaves observed
	02	<i>Brainea insignis</i>	F	F	Young leaves observed
	03	<i>Brainea insignis</i>	F	F	Young leaves observed
	04	<i>Brainea insignis</i>	F	F	Young leaves observed
	05	<i>Brainea insignis</i>	F	P	Young leaves observed
	06	<i>Brainea insignis</i>	F	F	Young leaves observed
	07	<i>Brainea insignis</i>	F	F	Young leaves observed
C-0006	01	<i>Brainea insignis</i>	F	F	Young leaves observed
C-0007	01	<i>Brainea insignis</i>	F	F	Young leaves observed
	02	<i>Brainea insignis</i>	F	P	-
C-0008	01	<i>Brainea insignis</i>	F	F	Young leaves observed
	02	<i>Brainea insignis</i>	F	F	Young leaves observed
	03	<i>Brainea insignis</i>	P	P	Young leaves observed
	04	<i>Brainea insignis</i>	F	F	Young leaves observed
	05	<i>Brainea insignis</i>	F	F	Young leaves observed
	06	<i>Brainea insignis</i>	F	P	-
	07	<i>Brainea insignis</i>	F	P	Young leaves at base
C-0009	01	<i>Brainea insignis</i>	F	F	Young leaves observed
C-0010	01	<i>Brainea insignis</i>	F	F	Young leaves observed
	02	<i>Brainea insignis</i>	F	F	Young leaves observed
	03	<i>Brainea insignis</i>	F	F	Young leaves observed
C-0011	01	<i>Brainea insignis</i>	P	P	Dry out caused by bushfire initially outside site boundary and high temperature on 2 Feb 2021
	02	<i>Brainea insignis</i>	F	P	-
	03	<i>Brainea insignis</i>	P	P	Young leaves at base
	04	<i>Brainea insignis</i>	F	F	Young leaves at base
	05	<i>Brainea insignis</i>	F	P	Young leaves at base
	06	<i>Brainea insignis</i>	F	F	Young leaves at base
	07	<i>Brainea insignis</i>	P	P	Young leaves at base
	08	<i>Brainea insignis</i>	F	F	Young leaves observed
	09	<i>Brainea insignis</i>	P	P	-
	10	<i>Brainea insignis</i>	F	F	Young leaves observed
	11	<i>Brainea insignis</i>	F	F	Young leaves observed
	12	<i>Brainea insignis</i>	P	P	-
	13	<i>Brainea insignis</i>	F	F	Young leaves observed

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0001(Patch)_01



C-0001(Patch)_02



C-0001(Patch)_03



C-0001(Patch)_04



C-0001(Patch)_05



C-0001(Patch)_06

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0001(Patch)_07



C-0001(Patch)_08



C-0002(Patch)_01



C-0002(Patch)_02



C-0002(Patch)_03



C-0002(Patch)_04



C-0002(Patch)_05



C-0002(Patch)_06



C-0002(Patch)_07



C-0002(Patch)_08

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0003



C-0004(Patch)_01



C-0004(Patch)_02



C-0004(Patch)_03



C-0004(Patch)_04



C-0004(Patch)_05



C-0004(Patch)_06



C-0004(Patch)_07



C-0004(Patch)_08



C-0004(Patch)_09



C-0004(Patch)_10



C-0004(Patch)_11



C-0004(Patch)_12



C-0004(Patch)_13



C-0004(Patch)_14



C-0004(Patch)_15



C-0004(Patch)_16



C-0004(Patch)_17



C-0004(Patch)_18



C-0004(Patch)_19



C-0004(Patch)_20



C-0005(Patch)_01



C-0005(Patch)_02



C-0005(Patch)_03



C-0005(Patch)_04



C-0005(Patch)_05



C-0005(Patch)_06

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0005(Patch)_07

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0006

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0007(Patch)_01



C-0007(Patch)_02

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0008(Patch)_01



C-0008(Patch)_02



C-0008(Patch)_03



C-0008(Patch)_04



C-0008(Patch)_05



C-0008(Patch)_06

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0008(patch)_07

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0009



C-0010(Patch)_01



C-0010(Patch)_02

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0010(Patch)_03



C-0011(Patch)_01



C-0011(Patch)_02

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0011(Patch)_03



C-0011(Patch)_04



C-0011(Patch)_05



C-0011(Patch)_06



C-0011(Patch)_07



C-0011(Patch)_08



C-0011(Patch)_09



C-0011(Patch)_10



C-0011(Patch)_11



C-0011(Patch)_12

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



C-0011(Patch)_13

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest

Inspection Date:

28/7/2025

Tree/Plant/ Colony No.	Species Name	Form (Good/Fair/Poor)	Health (Good/Fair/Poor)	Remark
L-0001	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0002	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0003	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0004	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0005	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0006	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0007	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0008	<i>Spiranthes sinensis</i>	F	F	Leaf observed
L-0009	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0010	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0011	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0012	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0013	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0014	<i>Spiranthes sinensis</i>	P	P	Leaf observed
L-0015	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0016	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0018	<i>Spiranthes sinensis</i>	F	F	Leaf observed
L-0019	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0020	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0021	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0022	<i>Spiranthes sinensis</i>	P	P	Leaf observed
L-0023	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0024	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0025	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0026	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0027	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0028	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0029	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0030	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0031	<i>Spiranthes sinensis</i>	F	F	Leaf observed
L-0032	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0033	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0034	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0035	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0036	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0037	<i>Spiranthes sinensis</i>	F	F	Leaf observed
L-0038	<i>Spiranthes sinensis</i>	P	P	Leaf observed
L-0039	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0040	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0041	<i>Spiranthes sinensis</i>	-	-	Not observed
L-0042	<i>Spiranthes sinensis</i>	-	-	Not observed



L-0001



L-0002



L-0003



L-0004



L-0005



L-0006



L-0007




L-0008



L-0009



L-0010

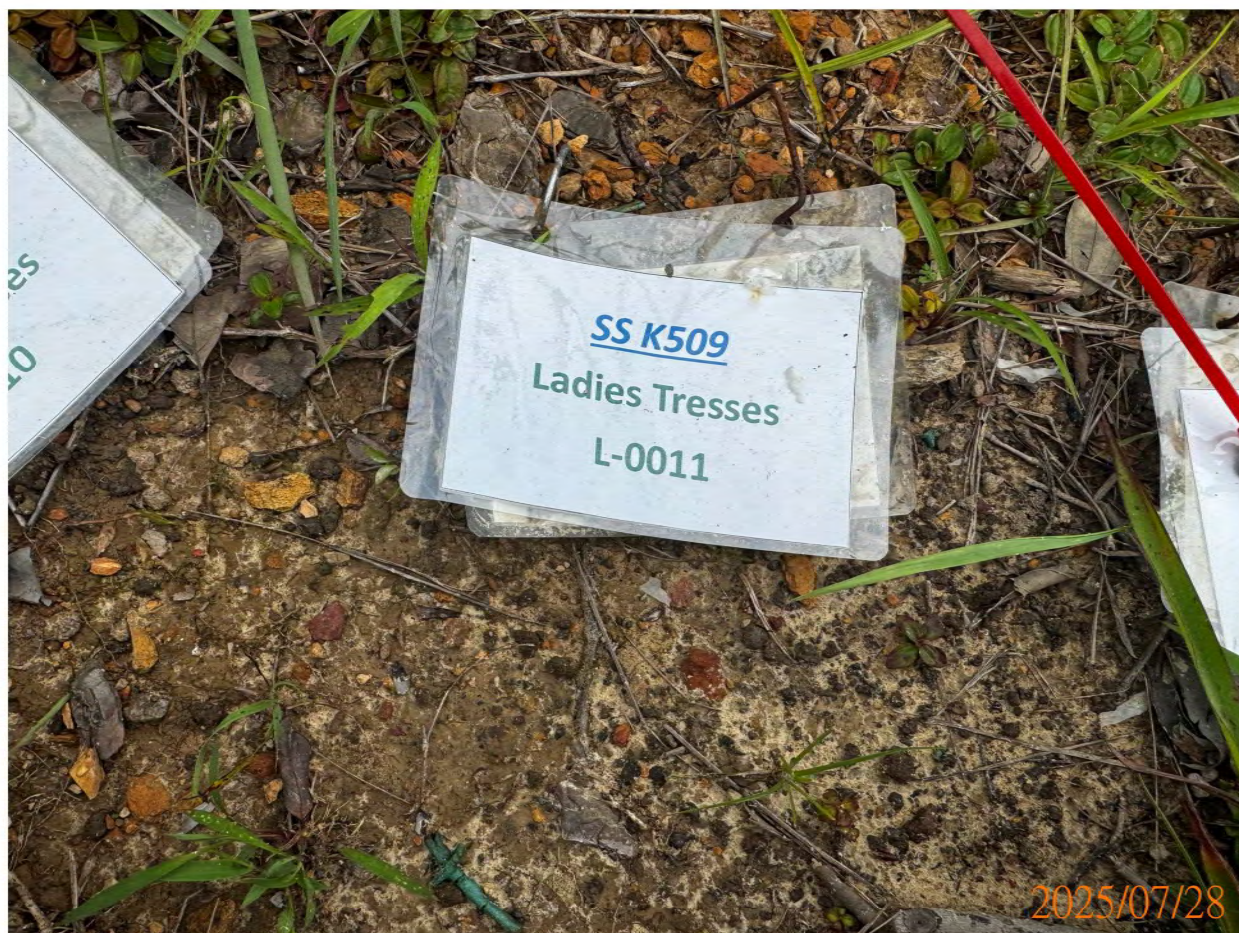

L-0011



L-0012



L-0013



L-0014



L-0015



L-0016



L-0018



L-0019



L-0020



L-0021



L-0022



L-0023



L-0024



L-0025



L-0026



L-0027



L-0028



L-0029



L-0030



L-0031



L-0032



L-0033



L-0034



L-0035



L-0036



L-0037



L-0038



L-0039



L-0040



L-0041

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



L-0042

Monitoring and Maintenance Works for Flora Species of Conservation Interest

Vegetation Maintenance Record Sheet (July 2025)

	Public Holiday		H-Hot	D-Drizzle		R-Rainy		W-Windy		RH-High Humidity	MH-Medium Humidity	LH-Low Humidity			
--	----------------	--	-------	-----------	--	---------	--	---------	--	------------------	--------------------	-----------------	--	--	--



firming up protection zone



weeding (1)

Contract No.: SS K509

Design and Construction of Kong Nga Po Police Training Facilities

Monitoring and Maintenance Works for Flora Species of Conservation Interest



weeding (2)

Post-transplantation Monitoring Checklist

Police Facilities in Kong Nga Po

Contract Provision of Environmental Team
Consultancy for Design and Construction
of Kong Nga Po Police Training Facilities
(Programme no. 279LP)

Inspected By ETL

Inspection Date 23-7-2025

Part A Weather

Condition ☒ Sunny ☐ Fine ☐ Overcast ☐ Drizzle
☐ Rain ☐ Hazy

Wind ☐ Calm ☒ Light ☐ Breeze ☐ Strong

Part B

N/A or
not observed Yes NO Remarks

1 Cycadfern Brainea insignis

1.1	Is the general well-being of the plants deemed satisfactory?	☒	☐	☐	
1.2	Are appropriate measures being taken to ensure the careful protection of the transplanted plants on site?	☒	☐	☐	
1.3	Has the temporary protective fence been correctly installed and is it being properly maintained?	☐	☒	☐	
1.4	Has the plant protection zone been established at a distance of 1m from the plants as required?	☒	☐	☐	
1.5	Are all areas covered with grass and plants consistently maintained free from weeds and unwanted vegetation?	☒	☐	☐	
1.6	Are measures taken to prevent soil compaction and protect the plants?	☒	☐	☐	
1.7	Is prompt removal of litter and unwanted materials maintained in the planting area?	☐	☒	☐	
1.8	Are fixings being prevented from being driven into the plants?	☒	☐	☐	
1.9	Are the plants being intentionally avoided for the purpose of anchoring, winching, or displaying signs?	☒	☐	☐	
1.10	Are all plants consistently maintained free from pests, diseases, or fungal infections?	☒	☐	☐	
1.11	Is there sufficient space provided for the growth and development of plant roots?	☒	☐	☐	
1.12a	Is the exposure of plant roots being prevented?	☒	☐	☐	
1.12b	If not, are broken or rotting roots being avoided?	☒	☐	☐	

2 Ladies Tresses Spiranthes sinensis

2.1	Is the general well-being of the plants deemed satisfactory?	☒	☐	☐	
2.2	Are appropriate measures being taken to ensure the careful protection of the transplanted plants on site?	☒	☐	☐	
2.3	Has the temporary protective fence been correctly installed and is it being properly maintained?	☐	☒	☐	
2.4	Has the plant protection zone been established at a distance of 1m from the plants as required?	☒	☐	☐	
2.5	Are all areas covered with grass and plants consistently maintained free from weeds and unwanted vegetation?	☒	☐	☐	
2.6	Are measures taken to prevent soil compaction and protect the plants?	☒	☐	☐	
2.7	Is prompt removal of litter and unwanted materials maintained in the planting area?	☐	☒	☐	
2.8	Are fixings being prevented from being driven into the plants?	☒	☐	☐	
2.9	Are the plants being intentionally avoided for the purpose of anchoring, winching, or displaying signs?	☒	☐	☐	
2.10	Are all plants consistently maintained free from pests, diseases, or fungal infections?	☒	☐	☐	
2.11	Is there sufficient space provided for the growth and development of plant roots?	☒	☐	☐	
2.12a	Is the exposure of plant roots being prevented?	☒	☐	☐	
2.12b	If not, are broken or rotting roots being avoided?	☒	☐	☐	

Advice/Observations

- 1) Please refer to the guidelines on soil improvement issued by the Greening,Landscape and Tree Management Section (GLTMS) of the development bureau (2022)to apply to monitoring and maintenance of transplanted flora species.
- 2) Daily watering frequency is needed to keep the soil moist.
- 3) Installation of a shaded net is provided below.
- 4) The wild plants that are growing in undesirable areas should be removed.
- 5) The Black Shade Net should be installed.



IEC	ETL	Contractor Representative
Name: <u>Mr. Law</u> Date: _____	<i>Lee</i> Name: <u>Mr. W.H.Lee</u> Date: <u>23-07-2024</u>	Name: <u>Marian Kong</u> Date: _____

The installation of a shaded net



Remark: Non scale & Conceptual drawing

APPENDIX I
EVENT ACTION PLANS

Appendix I:

Table I-1: Event / Action Plan for Air Quality

EVENT	ACTION			
	ET	IEC	PERMIT HOLDER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC, ER and Contractor; 3. Repeat measurement to confirm finding; and 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method.	1. Notify Contractor.	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC, ER and Contractor; 3. Advise the WKCD on the effectiveness of the proposed remedial measure; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; and	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; and 5. Monitor Implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; and 3. Ensure remedial measures properly implemented.	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; and 3. Amend proposal if appropriate.

EVENT	ACTION			
	ET	IEC	PERMIT HOLDER	CONTRACTOR
	8. If exceedance stops, cease additional monitoring.			
LIMIT LEVEL				
1.Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; and 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and the ER informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; and 5. Monitor the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; and 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; and 4. Amend proposal if appropriate.
2.Exceedance for two or more consecutive samples	1. Notify IEC, the ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss amongst ER, ET, and Contractor on the potential remedial actions;	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with IEC, agree with the Contractor on the remedial measures to be implemented;	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals;

EVENT	ACTION			
	ET	IEC	PERMIT HOLDER	CONTRACTOR
	possible mitigation to be implemented; 6. Arrange meeting with IEC, and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and 8. If exceedance stops, cease additional monitoring.	4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and 5. Monitor implementation of remedial measures.	4. Ensure remedial measures properly implemented; and 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	4. Resubmit proposals if problem still not under control; and 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Abbreviations: ET – Environmental Team, IEC – Independent Environmental Checker

Table I-2: Event / Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	PERMIT HOLDER	CONTRACTOR
Action Level	1. Notify ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the IEC and Contractor on remedial measures required; and 5. Increase monitoring frequency to check mitigation effectiveness.	1. Review the monitoring data submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise ER; and 3. Advise the ER on the effectiveness of the proposed remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measure to be implemented; and 4. Supervise the implementation of remedial measure.	1. Submit noise mitigation proposals to IEC and ER; and 2. Implement noise mitigation proposals.
Limit Level	1. Inform IEC, ER and Contractor and EPD; 2. Repeat measurements to confirm findings; 3. Increase the monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedures; 6. Discuss with the IEC, Contractor and ER on	1. Discuss amongst the ER, ET, and Contractor on the potential remedial actions; and 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;	1. Confirm receipt of notification of failure in writing; 2. Notify the Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; and 5. If exceedance continues, consider	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to the IEC and ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Submit further proposal if problem still not under control; and 5. Stop the relevant portion of works as

EVENT	ACTION			
	ET	IEC	PERMIT HOLDER	CONTRACTOR
	remedial measure required; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and 8. If exceedance stops, cease additional monitoring.		stopping the Contractor to continue working in that portion of work which causes the exceedance until the exceedance is abated.	determined by the ER until the exceedance is abated.

Abbreviations: ET – Environmental Team, IEC – Independent Environmental Checker

Table I-3: Event / Action Plan for Landscape and Visual Mitigation Measures

EVENT	ACTION			
	ET	IEC	PERMIT HOLDER	CONTRACTOR
Non-conformity on one occasion	Identify source. Inform IEC and ER. Discuss remedial actions with IEC, ER and Contractor. Monitor remedial actions until rectification has been completed.	Check report. Check Contractor's working method. Discuss with ET and Contractor on possible remedial measures. Advise ER on effectiveness of proposed remedial measures. Check implementation of remedial measures.	Notify Contractor. Ensure remedial measures are properly implemented	Amend working methods to prevent recurrence of nonconformity. Rectify damage and undertake additional action necessary.
Repeated Nonconformity	Identify source. Inform IEC and ER. Increase monitoring frequency. Discuss remedial actions with IEC, ER and Contractor. Monitor remedial actions until rectification has been completed. If non-conformity stops, cease additional monitoring.	Check monitoring report. Check Contractor's working method. Discuss with ET and Contractor on possible remedial measures. Advise ER on effectiveness of proposed remedial measures. Supervise implementation of remedial measures.	Notify Contractor. Ensure remedial measures are properly implemented.	Amend working methods to prevent recurrence of nonconformity. Rectify damage and undertake additional action necessary.

Abbreviations: ET – Environmental Team, IEC – Independent Environmental Checker

APPENDIX J
SUMMARY OF EXCEEDANCE

Appendix J: Exceedance Report

(A) Exceedance Report for Air Quality

Environmental Monitoring	Parameter	No. of non-project related Exceedance		No. of Exceedance related to the Construction Activities of this Contract		Cumulative No. of Exceedance recorded
		Action Level	Limit Level	Action Level	Limit Level	
Air Quality	1-hr TSP	0	0	0	0	0

(B) Exceedance Report for Construction Noise

Environmental Monitoring	Parameter	No. of non-project related Exceedance		No. of Exceedance related to the Construction Activities of this Contract		Cumulative No. of Exceedance recorded
		Action Level	Limit Level	Action Level	Limit Level	
Noise	Leq(30 min.) dB(A)	0	0	0	0	0

**APPENDIX K
ENVIRONMENTAL MITIGATION
IMPLEMENTATION SCHEDULE (EMIS)**

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Implementation Agent	Location / Duration of the measure	Implementation Stages ¹			Relevant Legislation & Guidelines	Implementation Status
						Des	C	O		
Air Quality Impact Construction Phase										
3.9.1	2.2	Dust Control Measures To achieve compliance with the FSP, RSP and TSP criteria during the construction phase, good practices for dust control should be implemented to reduce dust impacts. The dust control measures are detailed as follows:	Construction Dust	Contractor	Project construction site / Duration of the construction phase / Prior to commencement of operation		✓		EIA Recommendation and Air Pollution Control (Construction Dust) Regulation	
		■ Covering 80% of stockpiling area by impervious sheets and spraying all dusty material with water immediately prior to any loading transfer operations to keep the dusty materials wet during material handling at the stockpile areas								Y
		Disturbed Parts of the Roads ■ Main temporary access points should be paved with concrete, bituminous hardcore materials or metal plates and be kept clear of dusty materials; or ■ Unpaved parts of the road should be sprayed with water or a dust suppression chemical so as to keep the entire road surface wet.								Y
		Wheel washing ■ Vehicle wheel washing facilities should be provided at each construction site exit. Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels.								Y
		Use of vehicles ■ The speed of the trucks within the site should be controlled to about 10 km/hour in order to reduce adverse dust impacts and secure the safe movement around the site. ■ Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels.								Y
		Site hoarding ■ Where a site boundary adjoins a road, street, service lane or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit								Y

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Implementation Agent	Location / Duration of the measure	Implementation Stages ¹			Relevant Legislation & Guidelines	Implementation Status
						Des	C	O		
Noise Impact Construction Phase										
4.4.6	3.2	Good Site Practice Good site practice and noise management can significantly reduce the impact of construction site activities on nearby NSRs. The following package of measures should be followed during each phase of construction:	Maintain good site practice to minimise / avoid construction noise impact	Contractor	Within the Project site / During construction phase / Prior to commencement of operation.		✓		EIAO and Noise Control Ordinance	
		■ only well-maintained plant to be operated on-site and plant should be serviced regularly during the construction works;								Y
		■ material stockpiles and other structures to be effectively utilised, where practicable, to screen noise from on-site construction activities.								Y
		Adoption of QPME QPME should be adopted as far as applicable.								Y
		Use of Noise Enclosure/ Acoustic Shed Noise enclosure or acoustic shed should be used to cover stationary PME such as air compressor and generator.								Y
		Use of Noise Insulating Fabric Noise insulating fabric can also be adopted for certain PME (e.g. pilling machine etc.).								Y

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Implementation Agent	Location / Duration of the measure	Implementation Stages ¹			Relevant Legislation & Guidelines	Implementation Status
						Des	C	O		
Water Quality Impact Construction Phase										
5.6.1.1	4.2	General Construction Activities The following measures should be implemented:	Maintain good site practices to avoid pollution of water courses	Contractor	Within the Project site / During construction phase		✓		Water Pollution Control Ordinance (Cap. 358), ProPECC Note PN 1/94	
5.6.1.2	4.2	- Construction waste, debris and refuse generated on-site should be stored or contained appropriately to prevent them entering nearby watercourses or blocking stormwater drains. - Regular off-site removal of these materials should be maintained to minimise the volume of waste present on the construction site at any one time.								Y
		Construction Site Runoff The site practices outlined in ProPECC Note PN 1/94 should be followed as far as practicable in order to minimise surface runoff and the chance of erosion. The following measures are recommended: - Temporary site drainage facilities are to be designed and implemented by the Contractor prior to commencement of construction to convey surface runoff to storm drains applying adequately designed silt/ sand removal traps and sediment basins. - Runoff into the excavation areas during rainstorm events shall be minimised as far as practicable. Any wastewater pumped out of the excavation areas shall be treated to remove suspended solids prior to discharge. - Open stockpiles of material should be covered on site with waterproof layers such as tarpaulin to reduce the potential for sediment laden runoff entering the drainage system. - The wheels of all vehicles and plant should be cleaned before leaving the works areas to remove sediment, soil and debris from the tracks. The washwater should be treated to remove any suspended sediment. - Manholes (including those constructed as part of the Project) should be adequately covered and temporarily sealed at all times to prevent silt, construction materials or								Y

		debris from entering the drainage system, and to prevent storm runoff from entering foul sewers. The discharge of surface runoff into foul sewers should be prevented so as not to overload the sewerage system. Discharges should be collected by the temporary drainage system installed by the Contractor and treated on-site to remove sediment prior to discharge to the off-site drainage areas. The Contractor is required to obtain a discharge licence from EPD under the WPCO for all discharges from site with all discharges meeting the water quality requirements of the Technical Memorandum on Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters (TM-DSS)								
5.6.1.3	4.2	Accidental Spillage of Chemicals In accordance with the Waste Disposal (Chemical Waste) (General) Regulation (Cap 354C), the following measures should be implemented: - The labelling and storage of chemicals should be in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes and maintained at all times by the Contractor. - Oils and fuels should only be stored in designated areas which have appropriate pollution prevention control facilities such as oil and grease traps.	Prevent accidental discharge of chemicals into the surrounding environment	Contractor	Within the Project site / During construction phase		✓		Code of Practice on the Packaging Labelling and Storage of Chemical Wastes; Waste Disposal (Chemical Waste) (General) Regulation (Cap 354C)	Y
5.6.1.4	4.2	Sewage from Construction Workforce Portable toilets should be available throughout the construction phase and regularly maintained, collected and disposed by a licensed wastecollector to a public sewage treatment works for suitable treatment.	Prevent discharge of sewage into the surrounding environment	Contractor	Within the Project site / During construction phase		✓		Water Pollution Control Ordinance (Cap. 358), ProPECC Note PN 1/94	Y

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Implementation Agent	Location / Duration of the measure	Implementation Stages ¹			Relevant Legislation & Guidelines	Implementation Status
						Des	C	O		
Waste Management Implications Construction Phase										
7.5.1.1	6.2	Good Site Practice Recommendations for good site practices during the construction activities include:	Implement good site practices to minimise waste generation	Contractor	Project construction site / Throughout construction stage / Until completion of all construction activities		✓		Waste Disposal Ordinance (Cap 354); Waste Disposal (Chemical Wastes) (General) Regulation (Cap	Y
		■ Training of site personnel in proper waste management and chemical handling procedures ■ Provision of sufficient waste disposal points and regular collection of waste ■ Provision of wheel washing facilities before the trucks leaving the works area so as to minimise dust introduction to public roads							354C); and ETWB Technical Circular (Works) No. 19/2005 Environmental Management on Construction Site	Y
7.5.1.2	6.2	Waste Reduction Measures Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include: ■ Sort non-inert C&D materials to recover any recyclable portions ■ Segregation and storage of different types of waste in different containers or skips or stockpiles to enhance reuse or recycling of materials and their proper disposal							Waste Disposal Ordinance (Cap 354)	Y

7.5.1.3	6.2	Inert and Non-inert C&D Materials In order to minimise impacts resulting from collection and transportation of inert C&D materials for off-site disposal, the inert C&D materials should be reused on-site as fill material as far as practicable. In addition, inert C&D materials generated from excavation works could be reused as fill materials in local projects that require public fill for reclamation. The surplus inert C&D materials will be disposed of at the Government's PFRFs for beneficial use by other projects in Hong Kong. The C&D materials generated from general site clearance should be sorted on site to segregate any inert materials for reuse or disposal at PFRFs whereas the non-inert materials will be disposed of at the designated landfill site. In order to monitor the disposal of inert and non-inert C&D materials at respectively PFRFs and the designated landfill site, and to control fly-tipping, it is recommended that the Contractor should follow the DEVB Technical Circular (Works) No. 6/2010 for Trip Ticket System for Disposal of Construction & Demolition Materials issued by Development Bureau. In addition, it is also recommended that the Contractor should prepare and implement a Waste Management Plan detailing their various waste arising and waste management practices in accordance with the relevant requirements of the ETWB Technical Circular (Works) No. 19/2005 Environmental Management on Construction Site	Minimise impacts resulting from collection and transportation of inert C&D materials	Contractor	Project construction site / Throughout construction stage / Until completion of all construction activities		✓		Waste Disposal Ordinance (Cap 354); DEVB Technical Circular (Works) No.6/2010 for Trip Ticket System for Disposal of Construction & Demolition Materials; and ETWB Technical Circular (Works) No. 19/2005 Environmental Management on Construction Site	Y
7.5.1.4	6.2	Chemical Waste If chemical wastes are produced at the construction site, the Contractor will be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the "Code of Practice on the Package Labelling and Wastes" Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidising, irritant, toxic, harmful, corrosive, etc. The Contractor should use a licensed collector to transport and dispose of the chemical wastes at the approved Chemical Waste Treatment Centre or other licensed recycling facilities, in accordance with the Waste Disposal	Implement good practices to avoid chemical waste impact.	Contractor	Project construction site / Throughout construction stage / Until completion of all construction activities		✓		Code of Practice on the Packaging Labelling and Storage of Chemical Wastes; Waste Disposal (Chemical Waste) (General) Regulation (Cap 354C)	Y

		(Chemical Waste) (General) Regulation. Potential environmental impacts arising from the handling activities (including storage, collection, transportation and disposal of chemical waste) are expected to be minimal with the implementation of appropriate mitigation measures as recommended								
7.5.1.5	6.2	General Refuse General refuse should be stored in enclosed bins or compaction units separated from inert C&D materials. A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from inert C&D materials. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.	Implement good practices to avoid odour nuisance or pest/vermin problem and waste impact.	Contractor	Project construction site / Throughout construction stage / Until completion of all construction activities		✓		Waste Disposal Ordinance (Cap 354); Public Health and Municipal Services Ordinance (Cap 132) - Public Cleansing and Prevention of Nuisances	Y

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Implementation Agent	Location / Duration of the measure	Implementation Stages ¹			Relevant Legislation & Guidelines	Implementation Status
						Des	C	O		
Ecological Impact										
9.7.1	8.3	Temporary Protective Fence for Flora Species of Conservation Interest During construction phase, erection and maintenance of a temporary protective fence enclosing the flora species of conservation interest identified under the detailed vegetation survey is recommended. Monthly monitoring of any other flora species of conservation interest identified in the detailed vegetation survey should be conducted during the construction phase.	To avoid potential impact on flora species of conservation interest from construction activities such as materials storage; To make sure that the flora species of conservation interest are not affected by the construction activities of the Project	Contractor	Project construction site / Throughout construction stage / Until completion of all construction activities		✓		EIAO-TM	Y
Landscape and Visual Impacts Construction Phase										
Table 10.11	Table 9.1	CM01: Trees / woodland within the Project Site which are unaffected by the works shall be protected and preserved during the detailed design stage and construction phase. The tree preservation proposals shall be coordinated with the layout and design of the engineering and architectural works at detailed design stage for further retention of individual trees. The preservation of existing tree shall provide instant greening and screening effect for proposed works. Tree protection works will be undertaken in accordance with DEVB TC(W) 7/2015 on “Tree Preservation” and tree risk assessment in accordance with “Guidelines for Tree Risk Assessment and Management Arrangement by DEVB.	Preserve and protect existing trees	Contractor	Project area / During design stage / construction phase / Establishment Period	✓	✓		EIAO-TM; Protection of Endangered Species of Animals and Plants Ordinance (Cap 586); DEVB TC(W) No. 6/2015 Maintenance of Vegetation and Hard Landscape Features; ETWB TCW No. 29/2004 Registration of Old and Valuable Trees, and Guidelines for their Preservation; DEVB TC(W) No. 07/2015 -Tree Preservation; ETWB (2/2007) - General Guidelines on Tree Pruning; GLTMS (12/2013)	Y

									-Guidelines for Tree Risk Assessment and Management Arrangement on an Area Basis and on a Tree Basis	Y
Table 10.11	Table 9.1	CM05: Decorative screen hoarding will be erected along areas of the construction works site boundary where the works site borders publically accessible routes and/or is close to visually sensitive receivers (VSRs) to screen undesirable views of the works site. It is proposed that the screening be compatible with the surrounding environment and where possible, non-reflective, recessive colours be used	Minimise landscape and visual impacts.	Contractor	Project area – areas adjacent to sensitive receivers / During construction phase.		✓		EIAO-TM	Y

Note 1: Des = Design; C = Construction; O = Operation

APPENDIX L
WASTE GENERATION IN THE
REPORTING MONTH

Name of Department: ArchSD

Monthly Summary Waste Flow Table for 2025 (year)

Project : Design and Construction of Kong Nga Po Police Training Facilities

Contract No.: SS K509

Month	Actual Quantities of Inert C&D Materials Generated Monthly							Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Bituminous Material	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 m ³)
Cumulative in 2023	16.796	0.000	0.000	0.000	0.000	16.796	0.000	0.000	0.041	0.054	0.000	0.657
Cumulative in 2024	68.120	0.000	0.000	19.942	32.572	15.607	0.000	12.077	1.129	4.454	0.000	8.249
Jan	2.012	0.000	0.000	1.329	0.306	0.377	0.000	0.000	0.000	0.000	0.000	1.495
Feb	5.313	0.000	0.000	3.129	1.944	0.241	0.000	0.000	0.000	0.000	0.000	1.456
Mar	11.552	0.000	0.000	5.929	5.064	0.559	0.000	0.000	0.000	0.000	0.000	1.827
Apr	2.902	0.000	0.000	1.329	1.346	0.228	0.000	0.000	0.000	0.000	0.000	2.243
May	4.533	0.000	0.000	3.337	0.332	0.865	0.000	0.000	0.000	0.000	0.000	2.600
Jun	7.595	0.000	0.000	6.880	0.000	0.715	0.000	0.000	0.000	0.000	0.000	1.632
Sub-total	33.907	0.000	0.000	21.934	8.990	2.984	0.000	0.000	0.000	0.000	0.000	11.252
Jul	2.104	0.000	0.000	0.635	0.039	1.430	0.000	0.000	0.000	0.000	0.000	0.670
Aug												
Sep												
Oct												
Nov												
Dec												
Total	120.927	0.000	0.000	42.511	41.601	36.817	0.000	12.077	1.170	4.508	0.000	20.827

- Notes:
- (1) The performance targets are given in the Particular Specification on Environmental Management Plan.
 - (2) The waste flow table shall also include construction waste that are specified in the Contract to be imported for use at the site.
 - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
 - (4) Broken concrete for recycling into aggregates.
 - (5) If necessary, use the conversion factor: 1 full load of dumping truck being equivalent to 6.5 m3 by volume.

*Data of JuLY 2025 released by EPD only up to 27/7/2025 as of 4/8/2025

	Date of transaction 交易日期	Vehicle No. 車牌號 碼	Account No. 帳戶編 號	Chit No. 入帳票編 號	Time- in 進入時 間	Time- out 離開時 間	Waste depth (meter) 廢物 深度 (米)	Weight- in (tonne) 入閘重 量 (公噸)	Weight- out (tonne) 出閘重 量 (公噸)	Net weight (tonne) 淨重量 (公噸)
TM38--FB	03/07/25	UJ1*2	7046289	28871513	14:36	14:48	0	23.91	16.39	7.52
TM38--FB	03/07/25	ZJ1*47	7046289	28871383	14:39	14:53	0	37.08	17	20.08
TM38--FB	03/07/25	ZJ1*47	7046289	28871384	16:37	16:46	0	37.28	16.93	20.35
TM38--FB	04/07/25	VL8*15	7046289	28871577	09:24	09:29	0	28.28	14.02	14.26
TM38--FB	04/07/25	WA3*22	7046289	28871520	09:41	09:47	0	28.99	14	14.99
TM38--FB	04/07/25	YZ5*12	7046289	28871578	09:41	09:46	0	37.5	16.33	21.17
TM38--FB	04/07/25	DV8*4	7046289	28871580	09:51	09:56	0	28.92	14.04	14.88
TM38--FB	04/07/25	YZ2*57	7046289	28871579	09:52	09:59	0	37.21	16.27	20.94
TM38--FB	04/07/25	VL7*3	7046289	28871581	09:59	10:06	0	28.58	12.9	15.68
TM38--FB	04/07/25	DV8*4	7046289	28871582	11:39	11:47	0	29.25	13.99	15.26
TM38--FB	04/07/25	YZ5*12	7046289	28871583	11:46	11:53	0	36.61	16.3	20.31
TM38--FB	04/07/25	WA3*22	7046289	28871521	11:54	11:59	0	28.37	13.96	14.41
TM38--FB	04/07/25	YZ2*57	7046289	28871584	12:04	12:10	0	37.01	16.42	20.59
TM38--FB	04/07/25	YR3*5	7046289	28871585	12:37	12:57	0	37.08	17.28	19.8
TM38--FB	04/07/25	VL7*3	7046289	28871587	12:52	12:58	0	28.79	12.86	15.93
TM38--FB	04/07/25	VL8*15	7046289	28871586	13:03	13:07	0	28.77	13.98	14.79
TM38--FB	04/07/25	DV8*4	7046289	28871588	13:57	14:07	0	29.07	13.98	15.09
TM38--FB	04/07/25	YZ2*57	7046289	28871589	14:13	14:21	0	37.01	16.4	20.61
TM38--FB	04/07/25	YZ5*12	7046289	28871590	14:19	14:27	0	36.34	16.29	20.05
TM38--FB	04/07/25	YR3*5	7046289	28871591	14:32	14:38	0	37.03	17.26	19.77
TM38--FB	04/07/25	VL8*15	7046289	28871592	14:35	14:40	0	28.55	13.94	14.61
TM38--FB	04/07/25	XZ1*19	7046289	28871593	15:01	15:10	0	36.84	16.11	20.73
TM38--FB	04/07/25	YG6*3	7046289	28871594	15:36	15:45	0	36.25	16.06	20.19
TM38--FB	04/07/25	DV8*4	7046289	28871595	15:48	16:01	0	29.07	13.93	15.14
TM38--FB	04/07/25	YZ2*57	7046289	28871559	16:17	16:28	0	36.59	16.37	20.22
TM38--FB	04/07/25	VL8*15	7046289	28871557	16:32	16:38	0	28.23	13.91	14.32
TM38--FB	04/07/25	YZ5*12	7046289	28871560	16:35	16:42	0	36.6	16.24	20.36
TM38--FB	04/07/25	XZ1*19	7046289	28871562	16:49	16:54	0	37.27	16.08	21.19
TM38--FB	04/07/25	UJ1*2	7046289	28871561	17:07	17:14	0	23.21	16.26	6.95
TM38--FB	04/07/25	YG6*3	7046289	28871563	17:29	17:37	0	36.81	16.03	20.78
TM38--FB	04/07/25	YR3*5	7046289	28871558	17:34	17:40	0	36.65	17.18	19.47
TM38--FB	04/07/25	ZJ4*30	7046289	28871565	17:42	18:01	0	36.68	16.51	20.17
TM38--FB	04/07/25	VY5*12	7046289	28871564	17:44	17:56	0	36.71	16.33	20.38
TM38--FB	05/07/25	VY5*12	7046289	28871566	09:06	09:15	0	36.76	16.29	20.47
TM38--FB	05/07/25	YZ5*12	7046289	28871568	09:17	09:24	0	36.47	16.18	20.29
TM38--FB	05/07/25	YZ2*57	7046289	28871567	09:19	09:33	0	36.85	16.31	20.54
TM38--FB	05/07/25	DG6*05	7046289	28871569	09:22	09:28	0	29.52	14.1	15.42
TM38--FB	05/07/25	RD1*3	7046289	28871525	09:47	09:53	0	36.74	16.54	20.2
TM38--FB	05/07/25	DG6*05	7046289	28871573	11:14	11:21	0	29.01	14.1	14.91
TM38--FB	05/07/25	YZ5*12	7046289	28871572	11:29	11:38	0	36.84	16.38	20.46
TM38--FB	05/07/25	YZ2*57	7046289	28871656	11:36	11:45	0	37.02	16.43	20.59
TM38--FB	05/07/25	VY5*12	7046289	28871571	11:37	11:46	0	36.69	16.29	20.4
TM38--FB	05/07/25	WA3*22	7046289	28871526	11:46	11:51	0	28.11	13.87	14.24
TM38--FB	05/07/25	RD1*3	7046289	28871527	11:55	12:03	0	37.06	16.49	20.57
TM38--FB	05/07/25	UJ1*2	7046289	28871574	12:10	12:20	0	23.4	16.43	6.97
TM38--FB	05/07/25	DG6*05	7046289	28871657	13:50	13:57	0	28.5	14.08	14.42
TM38--FB	05/07/25	YZ5*12	7046289	28871658	14:09	14:17	0	37.26	16.5	20.76
TM38--FB	05/07/25	VY5*12	7046289	28871659	14:13	14:22	0	36.45	16.29	20.16
TM38--FB	05/07/25	RD1*3	7046289	28871529	14:33	14:40	0	37.63	16.48	21.15
TM38--FB	05/07/25	ZJ1*47	7046289	28871385	14:48	14:56	0	36.72	16.86	19.86
TM38--FB	05/07/25	YZ2*57	7046289	28871660	14:54	15:01	0	36.45	16.43	20.02

TM38--FB	05/07/25	DG6*05	7046289	28871661	15:44	15:51	0	29.42	14.06	15.36
TM38--FB	05/07/25	RP3*13	7046289	28871386	15:49	16:01	0	29.24	14.73	14.51
TM38--FB	05/07/25	YZ5*12	7046289	28871662	16:08	16:15	0	37.01	16.21	20.8
TM38--FB	05/07/25	UJ1*2	7046289	28871575	16:18	16:29	0	23.2	16.41	6.79
TM38--FB	05/07/25	VY5*12	7046289	28871663	16:24	16:30	0	36.46	16.23	20.23
TM38--FB	05/07/25	ZJ1*47	7046289	28871387	16:32	16:39	0	36.04	16.84	19.2
TM38--FB	05/07/25	RD1*3	7046289	28871530	16:41	16:48	0	36.31	16.45	19.86
TM38--FB	05/07/25	YZ2*57	7046289	28871664	16:47	16:54	0	36.85	16.38	20.47
TM38--FB	05/07/25	WA3*22	7046289	28871531	17:29	17:36	0	28.89	14.04	14.85
TM38--FB	07/07/25	YG6*3	7046289	28871668	09:11	09:19	0	36.73	16.12	20.61
TM38--FB	07/07/25	WA3*22	7046289	28871388	09:29	09:35	0	28.83	13.98	14.85
TM38--FB	07/07/25	XL5*42	7046289	28871669	09:30	09:38	0	36.89	16.12	20.77
TM38--FB	07/07/25	XZ1*19	7046289	28871667	09:38	09:45	0	36.73	16.14	20.59
TM38--FB	07/07/25	ZJ1*47	7046289	28871389	09:55	10:02	0	36.6	16.74	19.86
TM38--FB	07/07/25	DF6*31	7046289	28871670	10:17	10:23	0	36.18	16.21	19.97
TM38--FB	07/07/25	XL5*42	7046289	28871671	11:20	11:28	0	37.27	16.1	21.17
TM38--FB	07/07/25	ZJ1*47	7046289	28871532	11:46	11:52	0	36.77	16.72	20.05
TM38--FB	07/07/25	WA3*22	7046289	28871390	11:54	12:01	0	27.8	13.95	13.85
TM38--FB	07/07/25	DF6*31	7046289	28871672	12:12	12:30	0	36.03	16.19	19.84
TM38--FB	07/07/25	XL5*42	7046289	28871673	14:18	14:26	0	36.89	16.2	20.69
TM38--FB	07/07/25	DF6*31	7046289	28871675	14:31	14:38	0	36.17	16.17	20
TM38--FB	07/07/25	ZJ1*47	7046289	28871391	14:41	14:46	0	36.61	16.91	19.7
TM38--FB	07/07/25	YZ5*12	7046289	28871637	16:09	16:15	0	36.84	16.19	20.65
TM38--FB	07/07/25	YG6*3	7046289	28871639	17:32	17:44	0	36.99	16.08	20.91
TM38--FB	07/07/25	DF6*31	7046289	28871638	17:56	18:04	0	36.21	16.15	20.06
TM38--FB	08/07/25	WA3*22	7046289	28871392	09:33	09:40	0	29.63	14.01	15.62
TM38--FB	08/07/25	RD1*3	7046289	28871393	09:38	09:48	0	37.6	16.55	21.05
TM38--FB	08/07/25	YN1*02	7046289	28871395	12:06	12:16	0	28	20.27	7.73
TM38--FB	08/07/25	WA3*22	7046289	28871394	12:16	12:30	0	28.7	13.95	14.75
TM38--FB	08/07/25	RD1*3	7046289	28871676	14:12	14:24	0	36.42	16.51	19.91
TM38--FB	09/07/25	RD1*3	7046289	28871678	10:11	10:17	0	37.1	16.43	20.67
TM38--FB	11/07/25	UJ1*2	7046289	28871596	16:16	16:24	0	23.58	16.39	7.19
TM38--FB	15/07/25	ZJ4*30	7046289	28871679	14:57	15:07	0	36.19	16.38	19.81
TM38--FB	15/07/25	ZJ4*30	7046289	28871680	17:01	17:08	0	35.37	16.36	19.01
TM38--FB	16/07/25	RN8*15	7046289	28871681	10:28	10:33	0	29.71	14.29	15.42
TM38--FB	16/07/25	ZJ4*30	7046289	28871682	14:15	14:23	0	36.59	16.28	20.31
TM38--FB	16/07/25	RN8*15	7046289	28871683	14:27	14:44	0	28.59	14.25	14.34
TM38--FB	16/07/25	ZJ4*30	7046289	28871684	16:36	16:43	0	36.51	16.25	20.26
TM38--FB	17/07/25	RN8*15	7046289	28871685	15:45	15:50	0	28.58	14.15	14.43
TM38--FB	18/07/25	TU1*89	7046289	28871687	12:43	12:49	0	28.75	13.92	14.83
TM38--FB	18/07/25	RN8*15	7046289	28871686	12:44	12:51	0	28.91	14.34	14.57
TM38--FB	18/07/25	RN8*15	7046289	28871688	15:10	15:16	0	28.63	14.3	14.33
TM38--FB	19/07/25	ZJ4*30	7046289	28871689	12:13	12:18	0	36.55	16.68	19.87
TM38--FB	19/07/25	ZJ1*47	7046289	28871690	12:45	12:51	0	36.12	16.63	19.49
TM38--FB	19/07/25	ZJ4*30	7046289	28871691	14:28	14:33	0	36.39	16.65	19.74
TM38--FB	19/07/25	ZJ1*47	7046289	28871692	14:34	14:41	0	36.09	16.58	19.51
TM38--FB	19/07/25	ZJ4*30	7046289	28871693	16:41	16:47	0	36.98	16.59	20.39
TM38--FB	19/07/25	ZJ1*47	7046289	28871694	16:46	16:52	0	36.76	16.54	20.22
TM38--FB	21/07/25	RP3*13	7046289	28871607	11:05	11:11	0	28.41	14.58	13.83
TM38--FB	21/07/25	RP3*13	7046289	28871608	14:03	14:11	0	28.93	14.52	14.41
TM38--FB	21/07/25	RP3*13	7046289	28871609	15:52	15:59	0	28.47	14.5	13.97
TM38--FB	21/07/25	RP3*13	7046289	28871610	17:58	18:04	0	28.76	14.52	14.24
TM38--FB	22/07/25	ZJ1*47	7046289	28871545	12:23	12:30	0	36.67	16.54	20.13
TM38--FB	22/07/25	RN8*15	7046289	28871695	14:46	14:52	0	29.23	14.24	14.99
TM38--FB	22/07/25	ZJ1*47	7046289	28871696	14:49	14:55	0	35.88	16.46	19.42
TM38--FB	22/07/25	RN8*15	7046289	28871697	16:45	16:51	0	28.63	14.21	14.42
TM38--FB	22/07/25	ZJ1*47	7046289	28871698	16:59	17:05	0	36.04	16.45	19.59
TM38--FB	23/07/25	RP3*13	7046289	28871615	09:07	09:18	0	30.07	14.57	15.5

TM38--FB	23/07/25	SB5*50	7046289	28871699	09:17	09:24	0	28.76	13.83	14.93
TM38--FB	23/07/25	ZJ1*47	7046289	28871700	09:17	09:25	0	36.18	16.43	19.75
TM38--FB	23/07/25	RN8*15	7046289	28871701	10:36	10:44	0	29.21	14.33	14.88
TM38--FB	23/07/25	ZJ1*47	7046289	28871703	11:08	11:18	0	36.31	16.39	19.92
TM38--FB	23/07/25	RP3*13	7046289	28871702	11:10	11:20	0	28.5	14.55	13.95
TM38--FB	23/07/25	TP9*82	7046289	28871705	11:27	11:37	0	27.98	14.36	13.62
TM38--FB	23/07/25	SB5*50	7046289	28871704	11:29	11:37	0	28.54	13.8	14.74
TM38--FB	23/07/25	RN8*15	7046289	28871706	13:51	14:04	0	29.83	14.28	15.55
TM38--FB	23/07/25	ZJ4*30	7046289	28871708	14:08	14:20	0	36.11	16.56	19.55
TM38--FB	23/07/25	SB5*50	7046289	28871707	14:09	14:23	0	28.54	13.77	14.77
TM38--FB	23/07/25	ZJ1*47	7046289	28871709	14:15	14:26	0	36.84	16.55	20.29
TM38--FB	23/07/25	RN8*15	7046289	28871710	16:05	16:18	0	29.61	14.25	15.36
TM38--FB	23/07/25	SB5*50	7046289	28871712	16:21	16:44	0	28.61	13.73	14.88
TM38--FB	23/07/25	ZJ1*47	7046289	28871713	16:27	16:39	0	36.21	16.52	19.69
TM38--FB	23/07/25	ZJ4*30	7046289	28871711	16:30	16:55	0	37.03	16.73	20.3
TM38--FB	24/07/25	ZJ1*47	7046289	28871714	09:23	09:31	0	36.99	16.48	20.51
TM38--FB	24/07/25	KZ9*1	7046289	28871715	09:25	09:33	0	36.02	16.73	19.29
TM38--FB	24/07/25	DV8*4	7046289	28871718	09:26	09:33	0	29.03	14.07	14.96
TM38--FB	24/07/25	WA3*22	7046289	28871716	09:27	09:34	0	28.63	14.03	14.6
TM38--FB	24/07/25	RT6*9	7046289	28871719	09:29	09:36	0	29.01	14	15.01
TM38--FB	24/07/25	VL7*3	7046289	28871717	09:32	09:39	0	28.02	12.8	15.22
TM38--FB	24/07/25	ZJ4*30	7046289	28871721	09:36	09:42	0	37.1	16.7	20.4
TM38--FB	24/07/25	RS7*56	7046289	28871720	09:38	09:46	0	28.3	14.12	14.18
TM38--FB	24/07/25	TU1*89	7046289	28871722	09:43	09:51	0	27.93	13.91	14.02
TM38--FB	24/07/25	ZJ1*47	7046289	28871723	12:00	12:06	0	36.18	16.44	19.74
TM38--FB	24/07/25	KZ9*1	7046289	28871724	12:07	12:15	0	36.38	16.7	19.68
TM38--FB	24/07/25	DV8*4	7046289	28871725	12:12	12:17	0	28.87	14.03	14.84
TM38--FB	24/07/25	RS7*56	7046289	28871728	12:19	12:29	0	28.42	14.3	14.12
TM38--FB	24/07/25	RT6*9	7046289	28871726	12:23	12:30	0	28.52	13.98	14.54
TM38--FB	24/07/25	TU1*89	7046289	28871729	12:24	12:33	0	28.22	13.91	14.31
TM38--FB	24/07/25	WA3*22	7046289	28871727	12:40	12:48	0	28.53	14	14.53
TM38--FB	24/07/25	ZJ1*47	7046289	28871730	13:47	13:56	0	35.9	16.42	19.48
TM38--FB	24/07/25	SB5*50	7046289	28871731	13:54	14:05	0	28.43	13.83	14.6
TM38--FB	24/07/25	DV8*4	7046289	28871732	13:57	14:09	0	29.35	14	15.35
TM38--FB	24/07/25	RT6*9	7046289	28871733	14:04	14:14	0	28.41	13.95	14.46
TM38--FB	24/07/25	TU1*89	7046289	28871734	14:16	14:24	0	28.43	13.95	14.48
TM38--FB	24/07/25	WA3*22	7046289	28871735	14:28	14:40	0	28.55	13.96	14.59
TM38--FB	24/07/25	RS7*56	7046289	28871736	14:30	14:39	0	28.78	14.26	14.52
TM38--FB	24/07/25	ZJ1*47	7046289	28871737	15:32	15:40	0	36	16.38	19.62
TM38--FB	24/07/25	SB5*50	7046289	28871738	15:45	15:53	0	28.83	13.79	15.04
TM38--FB	24/07/25	DV8*4	7046289	28871739	15:48	15:58	0	28.74	13.98	14.76
TM38--FB	24/07/25	RT6*9	7046289	28871740	15:51	15:57	0	28.18	13.91	14.27
TM38--FB	24/07/25	WA3*22	7046289	28871741	16:09	16:18	0	29.34	13.92	15.42
TM38--FB	24/07/25	RS7*56	7046289	28871742	16:31	16:45	0	28.03	14.24	13.79
TM38--FB	24/07/25	ZJ1*47	7046289	28871743	17:28	17:40	0	36.14	16.35	19.79
TM38--FB	25/07/25	YP7*8	7046289	28871744	09:29	09:36	0	35.95	16.61	19.34
TM38--FB	25/07/25	WA3*22	7046289	28871745	09:40	09:47	0	28.9	14.02	14.88
TM38--FB	25/07/25	DV8*4	7046289	28871746	09:47	09:55	0	29.13	14.12	15.01
TM38--FB	25/07/25	UM6*39	7046289	28871748	10:00	10:07	0	28.52	14.42	14.1
TM38--FB	25/07/25	TU1*89	7046289	28871749	10:04	10:10	0	28.26	13.86	14.4
TM38--FB	25/07/25	RL7*88	7046289	28871750	10:14	10:22	0	28.24	14.46	13.78
TM38--FB	25/07/25	XL5*42	7046289	28871747	10:22	10:28	0	37.18	16.21	20.97
TM38--FB	25/07/25	YP7*8	7046289	28871751	11:19	11:27	0	36.24	16.47	19.77
TM38--FB	25/07/25	DV8*4	7046289	28871752	11:39	11:50	0	28.82	14.09	14.73
TM38--FB	25/07/25	UM6*39	7046289	28871753	11:46	11:52	0	28.26	14.39	13.87
TM38--FB	25/07/25	TU1*89	7046289	28871754	12:00	12:08	0	28.4	13.86	14.54
TM38--FB	25/07/25	XL5*42	7046289	29029212	12:25	12:34	0	36.56	16.2	20.36
TM38--FB	25/07/25	RL7*88	7046289	28871755	12:40	12:48	0	28.6	14.44	14.16

TM38--FB	25/07/25	WA3*22	7046289	29029213	13:15	13:31	0	29.56	13.98	15.58
TM38--FB	25/07/25	UM6*39	7046289	29029214	13:28	13:37	0	28.76	14.36	14.4
TM38--FB	25/07/25	DV8*4	7046289	29029215	14:17	14:27	0	29.23	14.11	15.12
TM38--FB	25/07/25	TU1*89	7046289	29029216	14:22	14:27	0	28.28	13.81	14.47
TM38--FB	25/07/25	XL5*42	7046289	29029217	14:27	14:36	0	37.38	16.12	21.26
TM38--FB	25/07/25	RL7*88	7046289	29029218	15:01	15:07	0	28	14.42	13.58
TM38--FB	25/07/25	UM6*39	7046289	29029219	15:17	15:29	0	28.4	14.33	14.07
TM38--FB	25/07/25	WA3*22	7046289	29029220	16:08	16:15	0	28.77	14.03	14.74
TM38--FB	25/07/25	TU1*89	7046289	29029221	16:12	16:22	0	28.67	13.83	14.84
TM38--FB	25/07/25	DV8*4	7046289	29029222	16:16	16:25	0	28.83	14.07	14.76
TM38--FB	25/07/25	XL5*42	7046289	29029223	16:30	16:40	0	36.87	16.24	20.63
TM38--FB	25/07/25	RL7*88	7046289	29029224	17:13	17:23	0	28.41	14.39	14.02
TM38--FB	25/07/25	UM6*39	7046289	29029225	17:23	17:28	0	28.99	14.53	14.46
TM38--FB	25/07/25	ZJ4*30	7046289	29029226	17:41	17:48	0	36.37	16.36	20.01
TM38--FB	26/07/25	WA3*22	7046289	29029228	09:05	09:14	0	28.83	14.18	14.65
TM38--FB	26/07/25	XL5*42	7046289	29029227	09:07	09:17	0	36.86	16.19	20.67
TM38--FB	26/07/25	WT9*68	7046289	29029229	09:14	09:31	0	36.19	15.73	20.46
TM38--FB	26/07/25	UM6*39	7046289	29029230	09:16	09:30	0	28.62	14.48	14.14
TM38--FB	26/07/25	YZ5*12	7046289	29029231	09:32	09:46	0	37.13	16.28	20.85
TM38--FB	26/07/25	ZJ1*47	7046289	29029232	09:36	09:51	0	36.9	16.52	20.38
TM38--FB	26/07/25	DF6*31	7046289	29029233	09:41	09:50	0	36.2	16.25	19.95
TM38--FB	26/07/25	RL7*88	7046289	29029234	09:51	09:59	0	28.3	14.62	13.68
TM38--FB	26/07/25	RG9*4	7046289	29029235	09:52	10:05	0	29.1	14.81	14.29
TM38--FB	26/07/25	XL5*42	7046289	28871764	11:25	11:35	0	36.78	16.13	20.65
TM38--FB	26/07/25	UM6*39	7046289	29029236	11:29	11:34	0	28.71	14.45	14.26
TM38--FB	26/07/25	YZ5*12	7046289	29029237	11:48	12:00	0	36.41	16.25	20.16
TM38--FB	26/07/25	WT9*68	7046289	29029238	11:50	11:56	0	36.35	15.71	20.64
TM38--FB	26/07/25	ZJ1*47	7046289	29029239	11:57	12:02	0	36.16	16.48	19.68
TM38--FB	26/07/25	RG9*4	7046289	28871765	12:05	12:10	0	28.39	14.76	13.63
TM38--FB	26/07/25	DF6*31	7046289	29029240	12:23	12:30	0	36	16.22	19.78
TM38--FB	26/07/25	YZ2*57	7046289	29029241	12:34	12:44	0	36.43	16.29	20.14
TM38--FB	26/07/25	ZX3*35	7046289	29029244	13:05	13:23	0	36.57	15.87	20.7
TM38--FB	26/07/25	WA3*22	7046289	29029243	13:06	13:14	0	27.56	14.08	13.48
TM38--FB	26/07/25	RL7*88	7046289	29029242	13:09	13:25	0	28.28	14.58	13.7
TM38--FB	26/07/25	UM6*39	7046289	29029245	13:10	13:15	0	28.83	14.42	14.41
TM38--FB	26/07/25	XL5*42	7046289	29029246	13:27	13:33	0	36.65	16.12	20.53
TM38--FB	26/07/25	ZJ1*47	7046289	29029247	13:33	13:38	0	35.98	16.44	19.54
TM38--FB	26/07/25	RG9*4	7046289	29029248	14:02	14:19	0	28.61	14.79	13.82
TM38--FB	26/07/25	ZJ4*30	7046289	28871766	14:15	14:20	0	36.11	16.47	19.64
TM38--FB	26/07/25	YZ5*12	7046289	29029250	14:57	15:17	0	36.68	16.2	20.48
TM38--FB	26/07/25	WT9*68	7046289	29029249	15:02	15:19	0	36.27	15.68	20.59
TM38--FB	26/07/25	ZJ1*47	7046289	29029252	15:21	15:34	0	37.67	16.43	21.24
TM38--FB	26/07/25	YZ2*57	7046289	29029253	15:26	16:12	0	37.33	16.26	21.07
TM38--FB	26/07/25	UM6*39	7046289	29029254	15:27	16:08	0	28.7	14.39	14.31
TM38--FB	26/07/25	XL5*42	7046289	29029251	15:28	16:07	0	36.84	16.23	20.61
TM38--FB	26/07/25	DF6*31	7046289	29029255	15:41	15:57	0	36.34	16.19	20.15
TM38--FB	26/07/25	WA3*22	7046289	29029257	15:58	16:18	0	27.25	13.93	13.32

TM38--FB	26/07/25	ZJ4*30	7046289	28871767	16:00	16:10	0	35.88	16.42	19.46
TM38--FB	26/07/25	RG9*4	7046289	29029256	16:03	16:22	0	29.27	14.75	14.52
TM38--FB	26/07/25	ZX3*35	7046289	29029258	16:18	16:38	0	36.49	15.82	20.67
TM38--FB	26/07/25	ZJ1*47	7046289	29029259	17:06	17:13	0	36.43	16.4	20.03
TM38--FB	26/07/25	YZ5*12	7046289	29029260	17:41	17:53	0	35.97	16.18	19.79
TM38--FB	26/07/25	ZJ4*30	7046289	28871768	17:53	18:03	0	36.91	16.42	20.49

REMARKS

堆填區 Landfill	NENT	新界東北堆填區 North East New Territories Landfill
公眾填料接收設施 Public fill reception facilities	TM38--FB	屯門第38區填料庫 Fill Bank at Tuen Mun Area 38

APPENDIX M
COMPLAINT LOG

Appendix M - Complaint Log

Reporting month: July 2025

Complaint Log Ref.	EPD Log Ref.	Location	Received Date	Details of Complaint	Investigation/ Mitigation Action Status	Status
C001	N07/RN/00020836-23	Kong Nga Po Road (Lamp post GD0470)	29-Aug-23	The complainant alleged that the general construction noise except renovation (within Restricted Hours) from at Kong Nga Po Road (Lamp post GD0470), and commented that "晚上八九點地盤有噪音有人工作". The work sites under complaint are adjacent to the captioned Designated Project area.	Record of Site Investigation Refer to the public complaint which was no mention the certain time, based on daily record provided, CSJV was confirmed that the working period on 26, 27 & 28 Aug 2023 and the working hours were within the approved restricted hour. The equipment applied on the mentioned periods were listed in the Group D of the CNP No. GW-RN0882-23 (Effective date from 24/08/2023 to 23/11/2023) According to the written reply, the Contractor has implemented both the notification of the neighborhood on the schedule of night works and erect noise barriers to screen noisy works for neighborhood. Please be advised that the Contractor is strictly adhering to the conditions of the construction noise permit.	Closed
C002	N07/RN/00029993-23	The river(s) near the San Uk Ling Holding Centre	14-Dec-23	The complainant alleged that the river(s) near the San Uk Ling Holding Centre has recently had a large amount of soil/muddy water. (新屋嶺扣留中心附近的河流，近日有大量黃泥水)	Record of Site Investigation In reference to the public complaint, it has been noted that the complainant did not provide a precise description of the river(s) location adjacent to the San Uk Ling Holding Centre, where there has been a recent influx of soil-laden water. EPD officers carried out site inspection on 15/12/2023 at 11:20 –12:00. EPD officers checked the U-channels, catchpits and wastewater treatment facility at WTF. No water including muddy water was discharged from Construction sites to the drainage. The Contractor has checked the drainage and wastewater treatment facilities at WTF and SOTF, which is near the complaint area. No water was discharged from the above locations. Advice: For the Contractor: 1)The Contractor strictly complies with the	Closed

					requirements of relevant environmental ordinances and EM&A Manual. 2)The promotional flyer contains a Community Liaison Hotline: 9790 2879 that can be placed in residents' mailboxes, so they can directly contact you to resolve environmental issues. For EPD officer: 1)Please consider that the Community Liaison Hotline: 9790 2879 will be provided for the complainant to directly contact the Contractor to resolve environmental issues. 2) Please consider encouraging the complainant to provide more accurate and detailed information to facilitate our follow-up efforts.	
C003		Soil/muddy water from San Uk Leng at Man Kam To Road near Designated Project of the Police Facilities in Kong Nga Po, near San Uk Leng at Man Kam To Road	7-Apr.-2024	The complainant alleged in Chinese, as shown below: 1)4月6日下午約一點下了一場雨，但到7號已過一天，河水還是泥黃色 2)投訴人表示為上水新屋嶺附近居民，在新屋嶺練靶場附近有一政府地盤，由中國建築進行有關政府機動步隊的工程。投訴人表示建築公司沒有一個妥善的排污系統，把地盤所產生的黃泥水直接排在新屋嶺或經新屋嶺排走，導致黃泥水經引水道流入新屋嶺及新屋嶺漁塘，嚴重影響附近居民，現要求有關部門盡快跟進及處理。	Record of Site Investigation Based on a complaint investigation conducted by the Contractor, no muddy water was found discharged from the site. Mitigation measures have been strengthened by plugging off the last manholes of the site. According to the document provided, the improvement measures implemented by the Contractor include the following: 1) Manhole SMH-0503 was plugged off, 2) Water pump was placed in the manhole to pump wastewater, if any, to the wastewater treatment facilities, 3) Manhole SMH-1305 was plugged off, and 4) Water pump was placed in the manhole to pump wastewater, if any, to the wastewater treatment facilities.	Closed

Cumulative Complaint Log

Complaint Log Reporting Period	Total no. of Complaint Received
This reporting month	0
From 1st April 2023 to end of the reporting month	3

APPENDIX N
SUMMARY OF SUCCESSFUL
PROSECUTION

Appendix N - Summary of Successful Prosecution

Date of Successful Prosecution	Details of the Successful Prosecution	Status	Follow Up	Total no. Received in this Reporting Month	Total no. Received since Project Commencement
--	--	--	--	--	--

APPENDIX O

**The potential seriousness of the forthcoming
environmental impacts and the use of
machineries**

A list of potential environmental impacts	The advice includes, but is not limited to, the following	Consideration of possible alternative methods
Visual Impact: The presence of machinery, equipment, and temporary structures associated with ground investigation and plate load testing may have visual impacts on the surrounding landscape, altering the aesthetic qualities of the area.	Screening and Camouflage: Use screening techniques, such as temporary fencing, barriers, or landscaping, to visually conceal the machinery, equipment, and temporary structures from view. This can help minimize the visual impact on the surrounding landscape.	N.A.
Noise and Vibration: The operation of heavy machinery can contribute to noise and vibration pollution, which can disturb local wildlife or sensitive wildlife habitats.	Use of Low Noise and Vibration Equipment: Whenever possible, equipment produces lower levels of noise and vibration should be used. The use of noise barriers around the site can also help to mitigate the impact on local communities and wildlife.	Use of Electric-Powered Equipment: Electric- powered equipment is generally quieter than diesel powered equipment to help reduce noise pollution.
Disturbance of Local Ecosystems: The drilling operations, particularly those involving excavation, can potentially disturb the local ecosystems and impacting biodiversity.	Training and Awareness: trainings are provided for site personal about the importance of minimizing disturbance to local ecosystems, such as minimized noise and light pollution, how to handle waste properly, and what to do if they encounter local wildlife.	Employing construction methods of a low-impact nature, such as the utilization of machinery that is lightweight and drilling techniques which are minimally invasive
Air Pollution: Machinery used in construction sites can emit pollutants into the air. These pollutants may include Particulate Matter (PM), Nitrogen Oxides (NOx), Sulfur Oxides (SOx), and Volatile Organic Compounds (VOCs), contributing to air pollution and potentially impacting air quality in the surrounding area.	Dust Control Measures: Implement dust control measures such as water sprays, dust screens, or using dust suppression chemicals to reduce particulate matter emissions, and training for all staff on the importance of air quality and measures to reduce air pollution.	1. Improved Fuel Efficiency and Maintenance: Promoting fuel-efficient practices and regular maintenance of machinery can help reduce emissions. 2. Properly maintained equipment operates more efficiently, resulting in lower fuel consumption and reduced emissions. Implementing fuel-saving measures, such as reducing idling time and optimizing equipment usage, can further minimize air pollution during construction.
Water Pollution: Drilling operations have the	Proper containment and lining of mud pools is crucial to	1. Horizontal Directional Drilling (HDD): HDD is a

potential to contaminate local water sources, particularly if improper waste management practices are used.	prevent contamination. Mud pools should have an impermeable liner, such as HDPE or bentonite clay, to prevent seepage into the ground. Berms can be constructed around the perimeter to contain any overflow. Regular inspection and maintenance of the liner integrity is important.	trenchless method that causes less disturbance to the surrounding environment and mitigates the risk of water contamination. It could be a viable alternative depending on the geology of the site and the purpose of the drilling operation. 2. Dry Drilling Techniques: Depending on the geology of the site, dry drilling techniques could be considered. These methods do not use drilling fluids and therefore reduce the risk of water contamination from these sources.
Soil Disturbance: The use of heavy machinery can cause soil compaction and disturbance, particularly during drilling operations or movement of equipment. This soil disturbance can disrupt the natural structure and composition of the soil, affecting its ability to support vegetation growth and nutrient cycling.	1. Proper Planning and Design: Incorporate soil protection measures into the initial planning and design phase of construction projects. This includes identifying sensitive areas and implementing appropriate construction techniques to minimize soil disturbance. 2. Ground Improvement Techniques: Techniques like soil stabilization, grouting, and compaction can help improve the soil's strength and stability, reducing the likelihood of soil disturbance during construction.	A helical pile is a type of deep foundation system used in construction. It consists of a steel shaft with helical plates or blades that are twisted into the ground to provide support for structures. Helical piles are commonly used in situations where traditional foundation methods are impractical or costly, such as in areas with poor soil conditions or limited access for heavy machinery.
Energy Consumption: The operation of machinery requires energy, typically derived from fossil fuels. The extraction, processing, and combustion of these fuels contribute to greenhouse gas emissions and contribute to climate change.	1. Training: workers are trained in the importance of energy conservation and efficiency. This could involve instruction on when to turn off equipment, how to use machinery efficiently, and the benefits of energy conservation. 2. Efficient Equipment and Machinery: Use energy-efficient machinery and equipment that consume less energy during operation. Regular maintenance and proper calibration of machinery can also improve energy efficiency and reduce energy waste.	1. Prefabrication and Modular Construction: Prefabrication and modular construction methods involve manufacturing building components off-site and assembling them on-site. This approach reduces energy consumption by streamlining the construction process, minimizing material waste, and optimizing energy usage during manufacturing. 2. Lean Construction: This methodology helps energy optimization in construction processes.

Waste Generation: Ground investigation and plate load testing may generate various types of waste, including drilling cuttings, excess soil, and construction debris. Improper disposal or management of these wastes can result in soil and water contamination or contribute to landfill usage.	Education and Training: education and training are provided to construction workers and staff on proper waste management practices. Raise awareness about the importance of waste reduction, recycling, and responsible disposal methods. Encourage worker participation and engagement in waste management initiatives.	Cone Penetration Testing (CPT): CPT is a method of ground investigation that produces minimal waste compared to traditional drilling methods. It involves pushing a cone-shaped probe into the ground and measuring the resistance, which can provide valuable information about the soil conditions with less soil disturbance.
---	--	--

APPENDIX P
A LIST OF MACHINERIES USED IN
CONSTRUCTIN SITE

SSK509 Design and Construction of Kong Nga Po Police Training Facilities
NRMM & QPME List

	Type	Brand	Model	S/N No.	Engine Make	Engine Model	NRMM No.	Approval, Exemption or Modification	QPME no.	QPME Expiry Date	Sound Power Level
1	Generator	Airman	SDG1005-3B1	1533B10240	ISUZU	BI-4HK1XYGD-02	EPD-A-003542-2017	Approval	EPD-06206R	十二月-29	92
2	Forklift	Mitsubishi	fd25nt	CF18C-81179	Mitsubishi	S4S	EPD-A-007117-2016	Approval			
3	Generator	Airman	SDG605-3B1	14A3B10240	ISUZU	BJ-4J1XYGD-04	EPD-A-003657-2017	Approval	EPD-06274R	十二月-29	90
4	Generator	Denyo	DCA-220E5EI	3936288	ISUZU	6U2I	EPD-A-001848-2019	Approval	EPD-08614	八月-25	96
5	Forklift	Doosan	D30NXP	FDA41-1670-02844	YANMAR	4TNE98-BQDF1CC	EPD-A-000153-2023	Approval			
6	Generator	Nippon Sharyo	NES150TI	DG041900	ISUZU	BH-6HK1X	EPD-A-001707-2018	Approval	EPD-07118R	七月-30	92
7	Forklift	Mitsubishi	FD30NT	CF14E-16891	Mitsubishi	S4S	EPD-A-000779-2017	Approval			
8	Generator	Nippon Sharyo	NES220EM	FJ083800	Guangxi Yuchai	YC6A275-D30	EPD-M-002058-2020	Approval	EPD-01840R	十月-25	95
9	Excavator	Komatsu	PC138US-8NM	29202	KOMATSU	SAA4D95LE-5	EPD-A-000710-2021	Approval			
10	Excavator	Hitachi	ZX75US-3	HCM1P300A00062042	ISUZU	AU-4LE2X	EPD-A-003158-2019	Approval			
11	Generator	Nissha	NES150TI	DG028600	Isuzu	BH-6HK1X	EPD-A-004698-2016	Approval	EPD-03628R	四月-28	92
12	Generator	Airman	SDG455-3B1	1333B10475	Kubota	V3800-T	EPD-A-000053-2018	Approval	EPD-06536R	二月-30	87
13	Excavator	Yanmar	VIO70-3A	35012B	YANMAR	4TNV98-ZWBV	EPD-A-000188-2020	Approval			
14	Generator	Nippon Sharyo	NES150TI	DG042300	ISUZU	BH-6HK1X	EPD-A-002077-2018	Approval	EPD-07262	八月-30	92
15	Excavator	Yanmar	VIO40-5	51036B	Yanmar	4TNV88-PBV	EPD-A-000128-2019	Approval			
16	Excavator	Hitachi	ZX350K-3	HCM1V900T00056936	ISUZU	6HK1-XDHAA-01-C2	EPD-A-000772-2020	Approval			
17	Excavator	Liugong	CLG922E	CLG922EZHPE718565	Cummins	Q5B7	EPD-A-003163-2023	Approval			
18	Road works machine	BITELLI	DTV325	000816	HATZ	2M41	EPD-EE-018554-2015	Exemption			
19	Loader	Bobcat	S450	B1ED11528	Kubota Corporation	V2403-M-DI-EU32	EPD-A-005651-2016	Approval			
20	Excavator	Kobelco	SK225SR	YB05-03058	Hino	AA-J05E-TA	EPD-A-001400-2022	Approval			
21	Excavator	Kato	HD820V	KWJ01E01PC0006237	Mitsubishi	4M50-TLE3A	EPD-A-003461-2021	Approval			
22	Excavator	Kobelco	SK135SR-2	YY06-22265	Mitsubishi	D04FR	EPD-A-005755-2016	Approval			
23	Generator	Nippon Sharyo	NES60TK2	KS013000	Kubota	V3800-DI-TI-K3A	EPD-A007294-2016	Approval	EPD-04519R	十二月-28	90
24	Road works machine	Dynapac	CC1300	10000334E0A010764	Kubota	V22030	EPD-EE-019550-2015	Exemption			
25	Road works machine	BOMAG	BW131AD-2	751750101550	KUBOTA	V1505	EPD-A-001349-2022	Approval			
26	Loader	Liugong	CLG365B	LGC365BZCPC503358	Perkins	404D-22	EPD-A-000432-2024	Approval			
27	Generator	Airman	SDG605-3B1	14A3B10618	ISUZU	BJ-4J1XYGD-04	EPD-A-002916-2022	Approval	EPD-12884	十二月-28	90
28	Generator	Airman	SDG125S-3B1	1263B10611	ISUZU	BI-4HK1XYGD-02	EPD-A-000878-2024	Approval	EPD-14678	四月-30	92
29	Generator	Airman	SDG150S-3B1	1723B10569	ISUZU	BH-6HK1XYGD-11	EPD-A-002208-2023	Approval	EPD-13957	九月-29	95
30	Generator	Nippon Sharyo	NES220EM	FJ091800	Guangxi Yuchai	YC6A275-D30	EPD-M-003034-2023	Approval	EPD-02303R	六月-26	95
31	Excavator	Kobelco	SK135SR-2	YY06-18660	Mitsubishi	D04FR	EPD-A-003077-2019	Approval			
32	Generator	Airman	SDG220L-5B1	P88B1-0529	ISUZU	BH-6U21XYGD-04	EPD-A-001084-2024	Approval	EPD-14827	五月-30	94
33	Excavator	Kobelco	SK210D	YN11-50763	Hino	AA-J05E-TA	EPD-A-002407-2019	Approval			
34	Loader	BOBCAT	S450	B5NB11534	KUBOTA	V2403	EPD-A-001492-2024	Approval			
35	special purpose vehicle	BOBCAT	D30NXP	FDA41-4920-03786	Yanmar	4TNE98	EPD-A-001869-2024	Approval			
36	Mobile Crane	SANY	STB650T5-8	TE0065CE0130	WEICHAI	WP7G300E473	EPD-A-001095-2024	Approval	EPD-14911	六月-30	104
37	Mobile Crane	XCMG	XCT90	LXGCPA488KA013688	Sinotruk	MC11.40-50	EPD-A-001854-2019	Approval			
38	Mobile Crane	XCMG	XCT60L6	LXGCPA468MA016172	Sinotruk	MC11.36-50	EPD-A-002675-2021	Approval			
39	Generator	Airman	SDG605-3B1	14A3B10251	ISUZU	BJ-4J1XYGF-04	EPD-A-000731-2018	Approval	EPD-06744R	四月-30	90
40	Generator	Nippon Sharyo	NES60TK2	KS016800	Kubota	V3800-T	EPD-A-001681-2017	Approval	EPD-05465R	六月-29	90
41	special purpose vehicle	Toyota	82-8FD25	808FD25-60042	Toyota	3Z	EPD-A-006031-2016	Approval			
42	special purpose vehicle	Mitsubishi	FD25NT	CF18C-81122	Mitsubishi	S4S	EPD-A-006795-2016	Approval			
43	Excavator	YANMAR	VIO40-5B	53530B	Yanmar	4TNV88-BXBV	EPD-A-000971-2023	Approval			
44	special purpose vehicle	HANGCHA	CPCD30	15BD03754	ZHEJIANG XINCHAI	3E22YG51	EPD-A-002453-2024	Approval			
45	Generator	Nippon Sharyo	NES220TI	FM029600	ISUZU	BH-6U21X	EPD-A-001692-2017	Approval	EPD-05457R	六月-29	94
46	Generator	Nippon Sharyo	NES125TI2	CJ010600	ISUZU	BI-4HK1X	EPD-A-007295-2016	Approval	EPD-04530R	十二月-28	93
47	special purpose vehicle	Doosan	D30NXP	FDA41-1670-03634	Yanmar	4TNE98	EPD-A-001105-2024	Approval			
48	Excavator	KATO	HD308USV	KWJ08E01KE0006092	ISUZU	4LE2	EPD-A-002162-2024	Approval			
49	special purpose vehicle	Toyota	82-8FD25	808FD25-80056	Toyota	3Z	EPD-A-000403-2021	Approval			
50	Road works machine	Dynapac	CC142	10000309LOA005769	DEUTZ	D2011L03I	EPD-EE-011031-2015	Exemption			
51	Generator	Denyo	DCA-400E5EI	3925008	ISUZU	6WG1	EPD-A-001956-2018	Approval	EPD-07182R	七月-30	97
52	Generator	Nippon Sharyo	NES60TK2	KS023500	Kubota	V3800-T	EPD-A-001633-2018	Approval	EPD-07064R	六月-30	90
53	Generator	Airman	SDG455-3B1	13A3B10347	Kubota	V3800-T	EPD-A-003470-2017	Approval	EPD-06202R	十二月-29	87
54	Excavator	KATO	HD513MRV	KWJ03E01PD0005309	Isuzu	4JX1DJJA	EPD-A-001157-2021	Approval			
55	special purpose vehicle	XCMG	XCT95L7	LXGDP48XNA002670	Sinotruk	MC11.44-50	EPD-A-000121-2022	Approval			
56	Excavator	Yanmar	VIO30-6B	BG768	YANMAR	3TNV88	EPD-A-001698-2023	Approval			
57	Excavator	Komatsu	PC138US-8	31146	KOMATSU	SAA4D95LE-5	EPD-A-000904-2023	Approval			
58	Generator	BAIFA	ST-G400	2410207	BAUDOUIN	6M21G2D3/5	EPD-A-000095-2025	Approval			
59	Excavator	Komatsu	PC138US-8	31146	KOMATSU	SAA4D95LE-5	EPD-A-000904-2023	Approval			
60	Generator	BAIFA	ST-G400	2410207	BAUDOUIN	6M21G2D3/5	EPD-A-000095-2025	Approval			

APPENDIX Q
Wastewater Discharge Layout Plan

臨時排水系統



- 隔沙缸
- 環保缸
- 排水點
- Sump pit

Temporary kerbs are erected to avoid overflow of water out of site

kerb

kerb

kerb

